



Republic of the Philippines
PROVINCIAL GOVERNOR'S OFFICE
Communication & Information Services Office
Pagadian City, Zamboanga del Sur
-oOo-



PROJECT PROFILE

of

Victory FREE WiFi

**Internet sa Barangay Project
Phase II - Public School WiFi**

Implemented by:

**PROVINCIAL GOVERNMENT
OF ZAMBOANGA DEL SUR**

Submitted by:

JUSTIN AHMED PAOLO C. HERRERA
Project Manager
VFW-CISO



Table of Contents

Table of Contents	1
Executive Summary	2
I. Project Description	4
II. Project Workplan	5
III. Human Resources	5
IV. Organizational Structure	6
V. Project Sites	7
VI. Project Monitoring	8
VII. Source of Fund	9
Attachment 1 – Pagadian City Sites	15
Attachment 2 – Labangan Sites	16
Attachment 3 – Tukuran Sites	17
Attachment 4 – Aurora Sites	18
Attachment 5 – R. Magsaysay Sites	19
Attachment 6 – Tambulig Sites	20
Attachment 7 – Molave Sites	21
Attachment 8 – Mahayag Sites	22
Attachment 9 – Josefina Sites	23
Attachment 10 – Dumingag Sites	24
Attachment 11 – Sominot Sites	25
Attachment 12 – Midsalip Sites	26
Attachment 13 – Dumalinao Sites	27
Attachment 14 – Guipos Sites	28
Attachment 15 – San Pablo Sites	29
Attachment 16 – Dinas Sites	30
Attachment 17 – Dimataling Sites	31
Attachment 18 – Tabina Sites	32
Attachment 19 – Pitogo Sites	33
Attachment 20 – V. Sagun Sites	34
Attachment 21 – Margosatubig Sites	35
Attachment 22 – Lapuyan Sites	36
Attachment 23 – San Miguel Sites	37
Attachment 24 – Kumalarang Sites	38
Attachment 25 – Bayog Sites	39
Attachment 26 – Lakewood Sites	40
Attachment 27 – Tigbao Sites	41
Attachment 28 – Backbone Link	42
Attachment 29 – Sample Captive Portal	43
Attachment 29 – Sample Installation Certificate	44

Executive Summary

In conjunction with the COVID-19 pandemic, internet access is a basic need nowadays to support government programs, especially in the education sector. The DepEd was implemented distance learning and online modules to encourage social distancing.

Part of the essential services is internet access. But it seems, most of the remote communities are lacking in it.

The national government, through DICT, however, has ongoing Public WiFi Projects, but only 102 sites were initiated out of 681 barangays for the entire province.

Because of this, the Provincial Governor made an initiative to break these barriers by implementing a Province-Wide Internet Project that can be available for every barangays.

ORGANIZATION

This project was organized mainly for public welfare, through the effort of the energetic leadership of the Honorable Victor J. Yu, the provincial governor of Zamboanga del Sur with his spirited behalf, Divina Grace C. Yu, Congresswoman of 1st District and the technical team of the Communication and Information Services Office, and with the technical support from the Department of Information and Communication Technology (DICT) made this happen in reality.

PROJECT DESCRIPTION

This project was called Victory FREE WiFi. The scope of this project is province-wide and shall cater to 600+ barangays and or about 100,000 users more or less. The general public (users) has access, and through it can connect to other networks or the Internet.

The network data center, management, and control are at the provincial capitol building. (*Network Topologies as described in the attachments*).

The infrastructure uses mostly wireless technology utilizing the 2.4Ghz and 5Ghz bands from the bridge, base stations, and access points.

PROJECT WORKPLAN

Implementation activities are the following:

- Procuring Materials and Equipment.
- Training / Workshop on Network Installation.
- Configuration - Equipment IP Pairing and Testing.
- Onsite Installation - Router Bridges, Base Stations, CPEs, Access Points, and Relays.
- Dry Run - Network Management, Testing, and Fine Tuning.

HUMAN RESOURCES

1. Technical Working Group

- 1 Project Manager - Provides Logistics Support and Over-All project coordinator.
- 1 Programmer for Network Management – Monitors, Manage Network Links and Status.
- 1 Project Monitoring Statistics and Analysis

2. Technicians / Installers

- 6 Team Leaders for Net Plans & Deployment - Conduct Site Surveys and Supervise Installations.
- 24 IT / Electrician / Rigger - Assist the Team Leader for Installation.
- 6 Dispatch Drivers - Equipment and Personnel Transporter

3. Project Monitoring

- Project Maintenance Team (Team Backbone)
- Clustered Barangay Facilitator (CBF) serves as an integral part of a project maintenance team.

PROJECT SITES

Sites include the Data Center located at the Provincial Capitol Building, then Central Base Station at Mt. Palpalan, then municipalities with two (2) or more Base Stations and 600 more or less Barangay Access Points and Extenders. *(Please refer to the attached Project Sites for Geolocation).*

PROJECT MONITORING

Network Infrastructure was monitored remotely through the Ubiquiti Network Management System (UNMS) and UniFi Controller by any or an authorized member of the Project Maintenance Team with CBF functioning as an onsite correspondent for efficient system repair and maintenance.

BUDGETARY REQUIREMENTS

The budgetary requirement of the project was from PGO Annual Budget CY 2022 – MOOE and PGO Supplemental Budget No. 1 CY 2022 – Capital Outlay as breakdown below:

• Communication Networks (Capital Outlay)	-	Php 65,442,464.88
• IT Equipment (Capital Outlay)	-	Php 915,031.00
• Other Machinery and Equipment (Capital Outlay)	-	Php 17,516,899.40
• Other Supplies – Tools (MOOE)	-	Php 363,481.30

TOTAL	-	Php 84,237,876.18
--------------	---	--------------------------

I. PROJECT DESCRIPTION

A. Background

Amidst the COVID-19 pandemic, the provincial government of Zamboanga del has never been hampered by its commitment to deliver essential services to its constituents.

Part of the essential services is internet access. But it seems, most of the remote communities are lacking about in

The national government, through DICT, however, has Public WiFi Projects, but only 100+ sites were initiated out of 600+ barangays for the entire province.

In this regard, the provincial government of Zamboanga del Sur took a collaborative effort with the concerned technical agency and other resources to break these barriers.

This project was dubbed “Province-wide Internet” that can be available for every barangays. In relation to the Republic Act 10929, otherwise known as the “Free Internet Access in Public Places Act” signed by President Rodrigo Roa Duterte.

B. Purpose and Scope

In conjunction with the COVID-19 pandemic, internet access is a basic need nowadays to support government programs, especially in the education sector. The DepEd was implementing distance learning or online modules to encourage social distancing.

This Victory FREE WiFi will be the solution to the nowadays problem. The scope of this project is province-wide and shall cater to 600+ barangays of 27 municipalities or about 100,000 users more or less. The general public (users) has access, and through it can connect to other networks or the Internet.

C. Technical

The network infrastructure uses mostly wireless technology utilizing the 2.4Ghz and 5Ghz bands from the bridge, base stations, and to access point and extenders.

The network Data Center Control are at the provincial capitol building. Network Topologies were described in the attachments.

The public (Users) with a captive portal (authentication) can access the WiFi Hotspot access points wirelessly within a range of 500 meters radius with the managed speed of upto 2mbps approximately and can browse essential web content. Clean browsing or content filtering shall be imposed to avoid exploitation of the network bandwidth.

Cache Server, Bandwidth Management, User Management, and other network solutions shall be utilized to maximize system performance.

II. PROJECT WORKPLAN

- A. Site Surveys
- B. Procuring Materials and Equipment.
- C. Training / Workshop on Network Installation.
- D. Configuration – Equipment IP Pairing and Testing.
- E. Onsite Installation – Router Bridges, Base Stations, CPEs, Access Points, and Extenders.
- F. Dry Run – Network Management, Testing, and Fine Tuning.

PROJECT ACTIVITY MATRIX

ID	Activity	Specific Task	Responsible	Days
A	Site Survey	Site Survey and Inventory of Existing Towers	VWF Team	-
B	Procurement	Procurement of Equipment, Materials, and Tools	PGO-CISO	-
C	Training/Workshop	Network Installation Training of Human Resources	PGO-CISO-TWG	-
D	Configuration	Equipment Configuration and Testing (IP Pairing)	PGO-CISO-TWG	-
E	Installation	Servers, Switch, Routers, AP, Antenna Installations	VWF Team	-
F	Dry Run	Network Management, Testing & Configurations	PGO-CISO-TWG	-

PROJECT TIME FRAME

ID	Activity/Task	Start	Finish	%
A	Site Survey	-	-	-
B	Procurement – Procurement of Equipment, Materials, and Tools	-	-	-
C	Training/Workshop – Network Installation Training of Human Resources	-	-	-
D	Configuration – Equipment Configuration and Testing (IP Pairing)	-	-	-
E	Installation – Servers, Switches, Routers, AP, Antenna Installations	-	-	-
F	Dry Run – Network Management, Testing & Configurations	-	-	-

III. HUMAN RESOURCES

1. Technical Working Group

- 1 Project Manager - Provides Logistics Support and Over-All project coordinator.
- 1 Programmer for Network Management - Monitors, Manage Network Links and Status.
- 1 Project Monitoring - Statistics and Analysis

2. Technicians and Installers


- 6 Team Leaders for Net Plans & Deployment - Conduct Site Surveys and Supervise Installations.
- 24 IT / Electrician / Rigger - Assist the Team Leader for the Installation.
- 6 Dispatch Drivers - Equipment and Personnel Transporter

3. Project Monitoring

- Project Maintenance Team (Team Backbone)
- Clustered Barangay Facilitator (CBF) serves as an integral part of a project maintenance team.

IV. ORGANIZATIONAL STRUCTURE

This project was organized mainly for public welfare, through the effort of the energetic leadership of Engr. Victor J. Yu, the provincial governor of Zamboanga del Sur with his strong-willed behalf Divina Grace Yu, Congresswoman of 1st District and the technical team of the Communication and Information Services Office, and with the technical support from the Department of Information and Communication Technology (DICT) made this happen in reality.

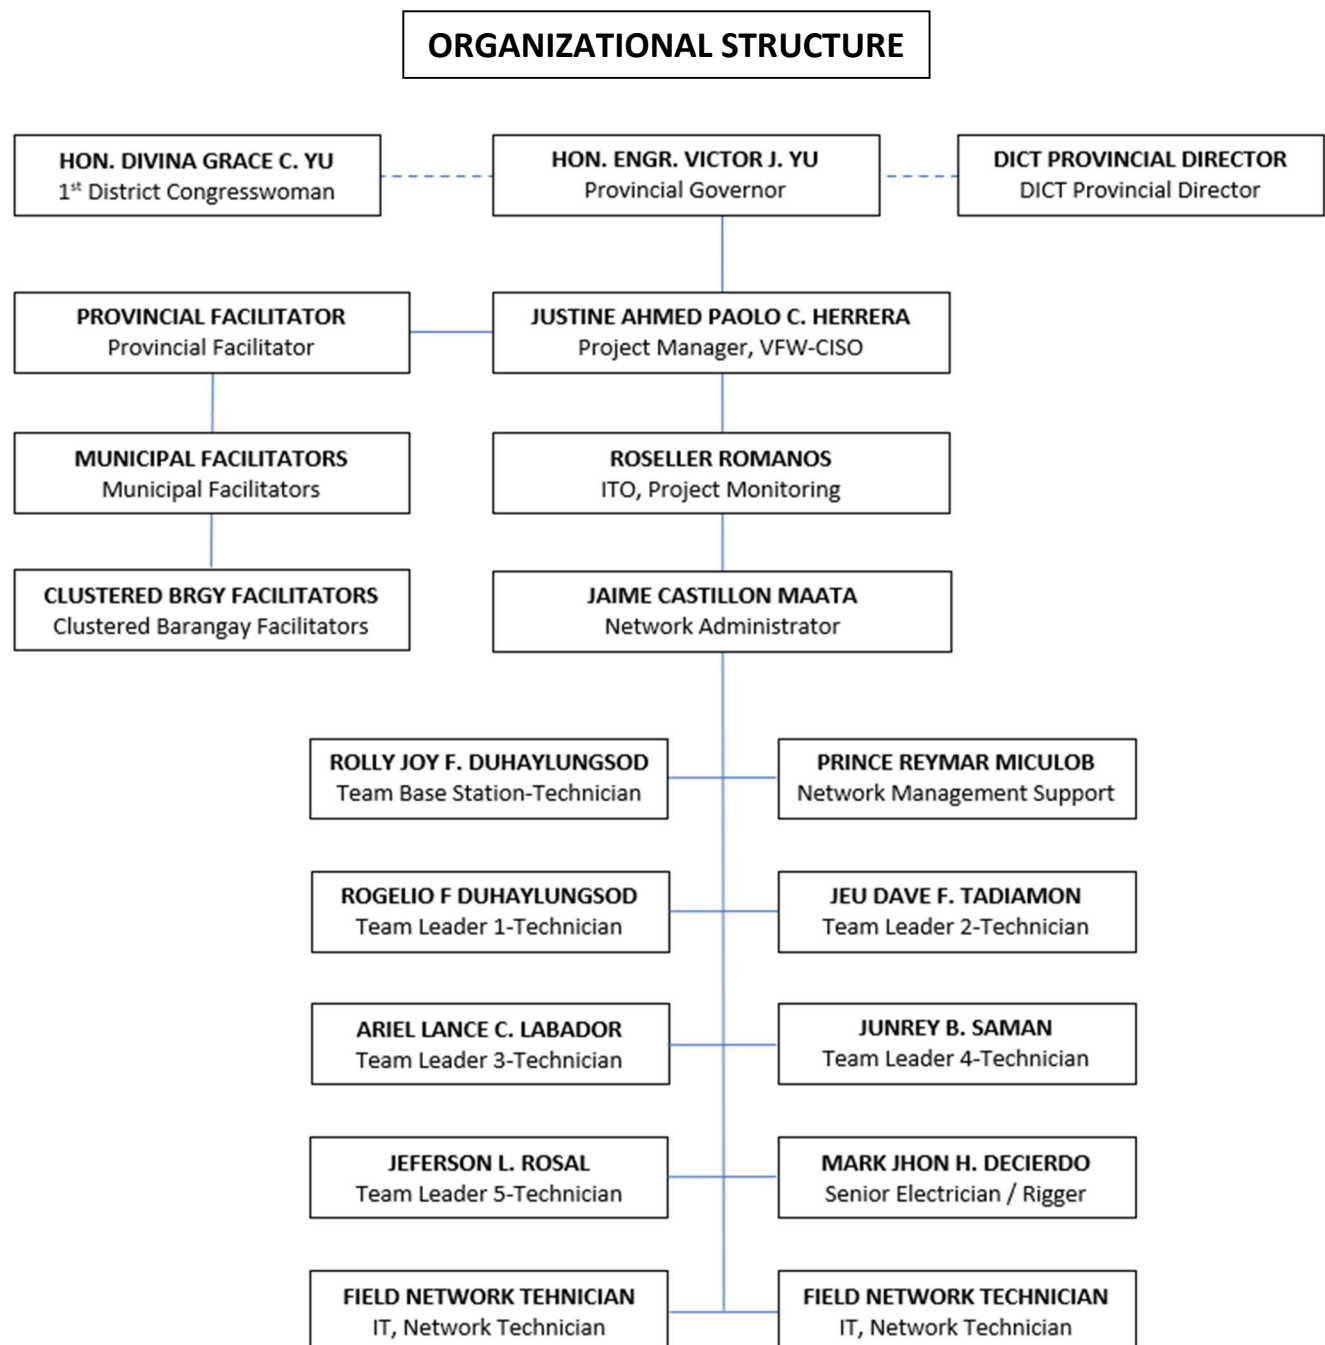


V. PROJECT SITES

Project Sites are located mostly in the province of Zamboanga del Sur. The initial implementation of the project (Phase I) are Barangay Halls, but in Phase II (current), Public Schools were set to be a priority.

Sites include the Data Center located at the Provincial Capitol Building, then to Central Base Station at Palpalan, Kapamanok, and Dipalutao, then to municipalities with two (2) or more Base Stations and to 600 more or less Barangay Access Points and Extenders. *(Please refer to the attached Project Sites).*

Network Backbone Topology

The illustration shows the Network Backbone Topology, how every municipality is connected to the network, and its geographical locations. *(Barangay Access Points are drawn in separate sheets).*

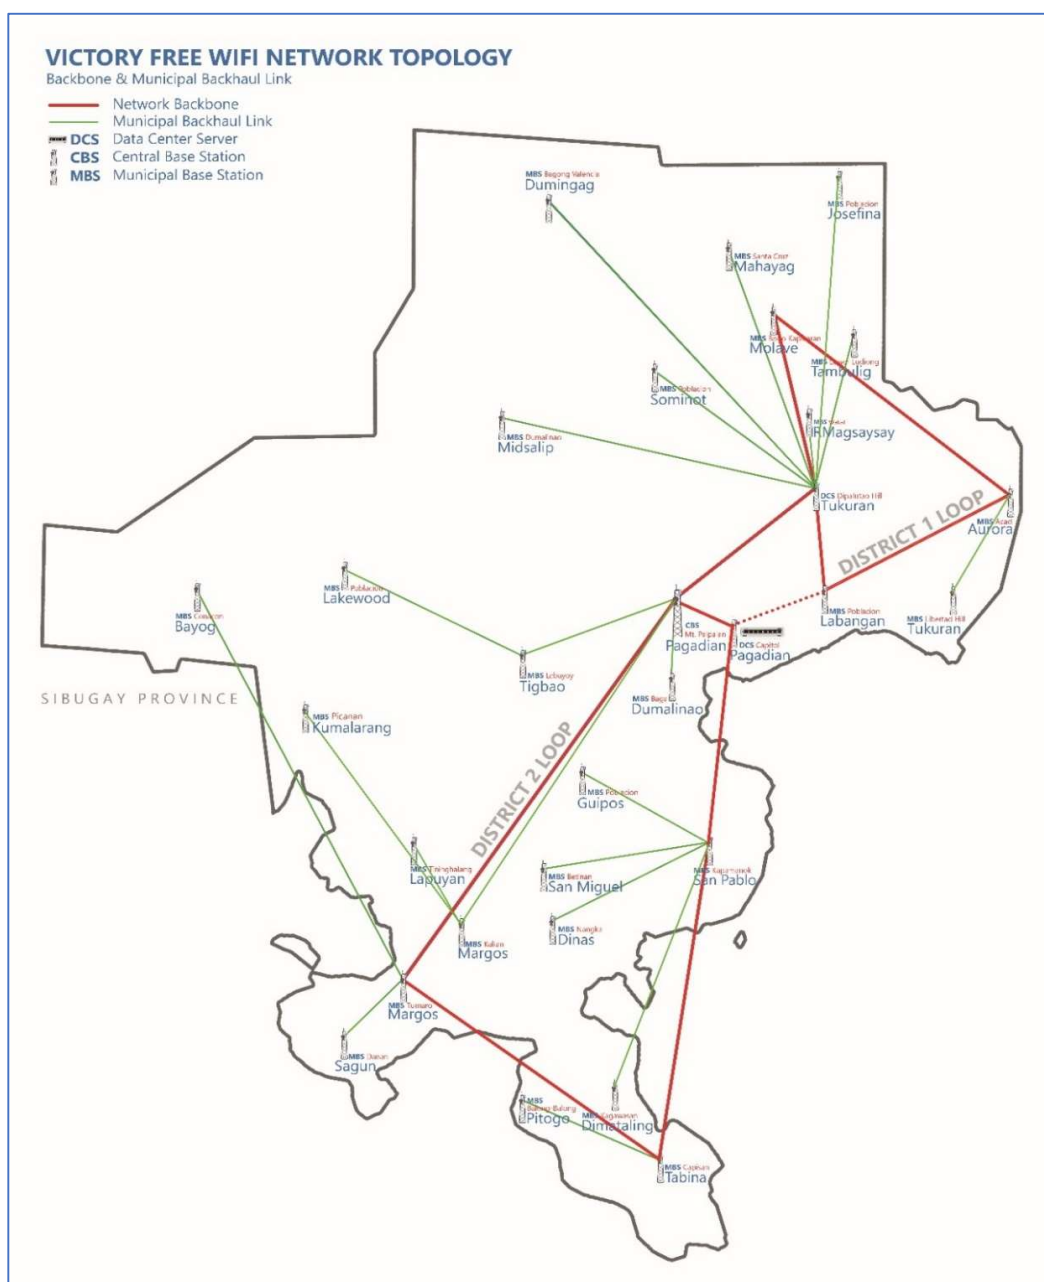

VI. PROJECT MONITORING

Network Infrastructure shall be monitored remotely through the Ubiquiti Network Management System (UNMS) by any or an authorized member of the Project Maintenance Team with MFs and CBFs functioning as an onsite correspondent.

Fig. 3. UNMS Interface



Using UNMS, a network administrator at a single location can manage groups of Ubiquiti devices: monitor the network, track usage, and make changes to more than one device at a time. UNMS offers these features:

- airOS® Device Monitoring and Management
- Mass Configuration for airOS 5 and airOS 6
- Mass Firmware Upgrade
- Network Topology Visualization
- Setup of Alerts and Notifications
- Smart Grouping and Filtering of Devices (using Device Groups)
- Device Discovery and Automatic Network Topology Resolution
- Configurable Charts
- Tasks and Task Scheduling
- Configurable Device List (Control View)
- Map Support
- Ping, Speed Test
- Malware Cleanup Utility

UNMS supports almost all devices used by the project like the Ubiquiti® airMAX® M series, airMAX AC series, and airFiber® series products of which the Victory FREE WiFi project uses most of these products.

VII. BUDGETARY REQUIREMENTS

The budgetary requirement of the project was from PGO Annual Budget CY 2022-MOOE Other Supplies Tools. The largest amount of the allocation was from PGO Supplemental Budget No. 1 CY 2022-Capital Outlay:

A. Communication Networks (Capital Outlay)	-	Php 65,442,464.88
B. IT Equipment (Capital Outlay)	-	Php 915,031.00
C. Other Machinery and Equipment (Capital Outlay)	-	Php 17,516,899.40
D. Other Supplies – Tools (MOOE)	-	Php 363,481.30
TOTAL	-	Php 84,237,876.18

A. COMMUNICATION NETWORKS

#	Description	Model	Image	Qty	Unit	Unit Price	Total
1	MikroTik Basebox 2 (RB912UAG-2HPnD-OUT)	RB912UAG-2HPnD-OUT		300	20pcs/box	\$150.00	\$45,000.00
2	UNIFI AC MESH Access Point	UAP-AC-M-US		600	10pcs/box	\$99.00	\$59,400.00
3	Access Point Mesh Dual-Brand Antenna(UMA-D)	UMA-D		100	20pcs/box	\$99.00	\$9,900.00
4	AirMax LiteBeam AC 5 GHz Bridge Gen2(LBE-5AC-US)	LBE-5AC-GEN2		200	8pcs/box	\$65.00	\$13,000.00
5	AirMax PowerBeam AC 5 GHz,620 Bridge Gen 2(PBE- 5AC-620-US)	PBE-5AC-620-US		600	1pc/box	\$219.00	\$131,400.00
6	AirMax Rocket Prism AC 5 GHz, Gen 2 Radio (RP-5AC US)	RP-5AC-GEN2		250	10pcs/box	\$249.00	\$62,250.00
7	AirMax Sector 5 GHz, 90°,20dBi Antenna(AM5G20-90)	AM-5G20-90		20	4pcs/box	\$139.00	\$2,780.00
8	airMax RocketDish, 5 GHz, 30 dBi LW Antenna	RD-5G30-LW		40	2pcs/box	\$109.00	\$4,360.00
9	Ethernet Surge Protector(ETH-SP-G2)	ETH-SP-G2		50	50pcs/box	\$15.30	\$765.00
10	Switch Flex Mini(USW-Flex- Mini)	USW-Flex-Mini		900	30pcs/box	\$37.00	\$33,300.00
11	Switch Flex Mini(USW-Flex- Utility)	USW-Flex-Utility		900	5pcs/box	\$54.00	\$48,600.00


B. IT EQUIPMENT

#	Description	Model	Image	QTY	Unit	Unit Price	Total
12	Server Computer, R740 4210R*2/64G/3.84TSS D*4/H 330/1100W	R740-Server		1	Unit	\$7,610.00	\$7,610.00
13	15.6' Laptop Computer for i7- 1195G7, 15.6 inch FHD IPS, 8G + 512GB SSD, 1M Camera	I7-1065G7		6	Unit	\$720.00	\$4,320.00
14	2U Micro ATX Rackmount Case	2U-ATX-CASE		2	Unit	\$72.00	\$144.00
15	27' LED Display Monitor	VM-27HV		2	Unit	\$170.00	\$340.00
16	Wireless Keyboard and Mouse	RF7302TZ		2	Set	\$23.00	\$46.00
17	2TB Solid State Drive(SSD) For Proxy/ Cache Server	EVO-870		4	Pcs	\$402.00	\$1,608.00
18	Dream Machine Pro(UDM- Pro)	UDM-PRO		1	Unit	\$475.00	\$475.00
19	MikroTik RB1100AHx4 Dude Edition Router	RB1100AHx4		6	Unit	\$495.00	\$2,970.00
20	1 Meter R45 Cat6 Patch Cord	RJ45-CAT6-1M		100	Pcs	\$2.50	\$250.00
21	RJ45 PVC Boots For Cat5,Cat5e,and Cat6(100pcs)	RJ45-BOOT-CAT6		2	Bag	\$2.20	\$4.40
22	Pack AMP CAT6 IO JACK Keystone or Modular Jack	NT-K008U6		100	Pcs	\$3.00	\$300.00
23	Ubiquiti 1Gb RJ45 SFP Module(UF-MM-1G-20)	UF-MM-1G		120	30pcs /box	\$35.00	\$4,200.00
24	AirFiber PoE Injector,50V/60W (POE-50- 60W)	POE-50V-60W		50	50pcs /box	\$21.00	\$1,050.00
25	1 Core 3 Steel Wire Outdoor G657a FTTH Drop Cable	GJYXCH-1B6		60	Roll	\$46.80	\$2,808.00

26	1 Pair(2pcs) 1000Mbps A/B Gigabit Fiber Optical Media Converter	WOR- 910PSS20- LC		120	Pair	\$47.00	\$5,640.00
27	LC Fiber Quick Connector	LC-UPC		60	Pcs	\$2.25	\$135.00
28	FTTH Fiber Optic Welding Splicing Machine(Optical Fiber Fusion Splicer 100- 240V)	AI-9		1	Pcs	\$982.00	\$982.00
29	Rocketdish PoE Injector,24V DC,30W(POE-24V- 30W)	POE-24V- 30W		150	Pcs	\$20.00	\$3,000.00
30	RJ45 Network Toughcable connectors Passthrough (small box)	TC-CON-100		200	100 pcs/ Box	\$70.00	\$14,000.00
31	Comlink UTP Cable Cat6 Outdoor 305m/Roll	UTP-CAT6- 23AWG		300	Roll	\$98.50	\$29,550.00
32	10GB PCI-E NIC Network Card, Dual Copper RJ45 Port, With Intel X540-BT2 Controller, PCI Express Ethernet LAN Adapter	F1002T-V1.6		5	Unit	\$380.00	\$1,900.00

C. OTHER MACHINERY AND EQUIPMENT

#	Description	Model	Image	Qty	Unit	Unit Price	Total
33	SPF 2000TL HVM-24 (2KVA/2KW; VDC 24V/220V;MPPT 50A; AC Charge 30A) Brand: Growatt	SPF-2000TL- HVM-24		300	Unit	\$454.00	\$136,200.00
34	270W Mono Crystalline Panel with 30V/8.3AMP	Mono-270W- 30V8.3A		300	Pcs	\$167.00	\$50,100.00
35	200AH Rechargeable Li- ion Battery 12.8Volts 483*170*241mm	R- LFP12.8V200 Ah		300	Pcs	\$758.00	\$227,400.00
36	CIRCUIT BREAKER DIN RAIL TYPE, AC 10A	SCB8-63-2P		500	Pcs	\$8.00	\$4,000.00
37	Mechanical Timer	TB388		20	Pcs	\$16.80	\$336.00
38	Circuit Breaker 25AMP DIN Rail Type	AC2P-25A-400V		500	Pcs	\$9.00	\$4,500.00

39	Magnetic Contactor (3P,50 amp)	AC-3P-50A		20	Pcs	\$36.00	\$720.00
40	Circuit Breaker 2P,32amp,400V (AC)	AC2P-32A-400V		60	Pcs	\$10.00	\$600.00
41	Metal Rack(1.5H) Outer: 600*1500*600mm with base, inner size:480*1100*510mm	HW-U1500-00		60	Unit	\$556.00	\$33,360.00
42	Metal Enclosure Box(40x60x25cm)	VM-40X60X25		250	Unit	\$82.00	\$20,500.00
43	G.I PIPE SCHEDULE 40, 2INCHES DIAMETER (6 meters) Q235 Diameter 4.8cm , 3mm thickness, 6 meter	G.I.-D4.8-3MM		1500	Pcs	\$26.50	\$39,750.00
44	Galvanized CABLE-TIE WIRE #10 (35KG, 550meter/Roll)	Galvanized Wire 10#		300	Roll	\$55.00	\$16,500.00
45	Scaffolding Swivel Clamp for 2 inches Pipe	BS1139 Clamp		1500	Pair	\$4.80	\$7,200.00
46	Nylon Cable Tie, 16 inches	GB5-400-4.8		700	Bag	\$5.20	\$3,640.00
47	Turn Buckle, 16 inches	DIN1480-16		900	Pcs	\$6.95	\$6,255.00
48	Porcelain Stay Insulator (Small)	Pin Type 54-4		900	Pcs	\$3.90	\$3,510.00
49	Cutting Disc (4 inches)	107D-1.2TH		1000	Pcs	\$0.58	\$580.00
50	Threaded Rod (12mm diameter)	TR-D12MM-3M		300	Pcs	\$5.80	\$1,740.00
51	Welding Rod, AWS E6013 / J421, 20KG/BOX	AWS E6013		10	Box	\$40.00	\$400.00
52	THW 12AWG (standard Wire) 600V UL83, copper wire	12AWG-THW		150	Roll	\$58.00	\$8,700.00

53	THW 10AWG (standard Wire) 600V UL83, copper wire	10AWG- THW		80	Roll	\$86.00	\$6,880.00
54	Service Drop Wire 6AWG, Voluta 2x6AWG+1xAWG AAC/XLPE+ACSR 600V	SDW-2x6AWG/ 1xAWG		4000	M	\$1.68	\$6,720.00
55	Angle Bar (1 1/2x3/16) Width:38mm,Height:38m m* thickness:4.78mm , Length:6m	A36-38-4.8MM		400	Pcs	\$28.00	\$11,200.00
56	Electronic Tape (3M Brand) Length:10yards/roll, PVC material, <600V Tolarence	XH003884422		1000	Roll	\$0.80	\$800.00
57	Flat Cord #14 (2x14AWG 300V) , 100% copper wire	FT-14#		70	Roll	\$98.00	\$6,860.00
58	12V Fan 90X90X25	9025FAN- 12V		300	Pcs	\$8.50	\$2,550.00

D. OTHER SUPPLIES – TOOLS

#	Description	Model	Image	Qty	Unit	Unit Price	Total
59	Safety Harness, Material Polyester, double 1.8 and hooks Standard: GB24543- 2009	SH-PD1.8		40	Set	\$24.00	\$960.00
60	32 Feet Extension Ladder	EX-LA-10M		5	Set	\$199.00	\$995.00
61	Military Grade Binoculars	YJM62- 8X30E		10	Set	\$178.00	\$1,780.00
62	Drill Bit Masonry(1/8) Diameter 3.17mm	DB-MS1/8		500	Pcs	\$0.35	\$175.00
63	Drill Bit Metal(1/8) Diameter 3.17mm	DB-ML1/8		500	Pcs	\$0.55	\$275.00
64	Cordless Impact Drill 18V/2.0 with Extra Battery , two batteries, Brand: BOSCH	GSR18V-50		4	Unit	\$251.00	\$1,004.00

Prepared by:

JUSTIN AHMED PAOLO C. HERRERA

Head, VFW-CISO Logistics

VFW Project Manager

Reviewed by:

Recommending Approval


APPROVED BY:

HON. VICTOR J. YU


Provincial Governor

Zamboanga del Sur


Attachment 1 - Site Link Plan - Pagadian City

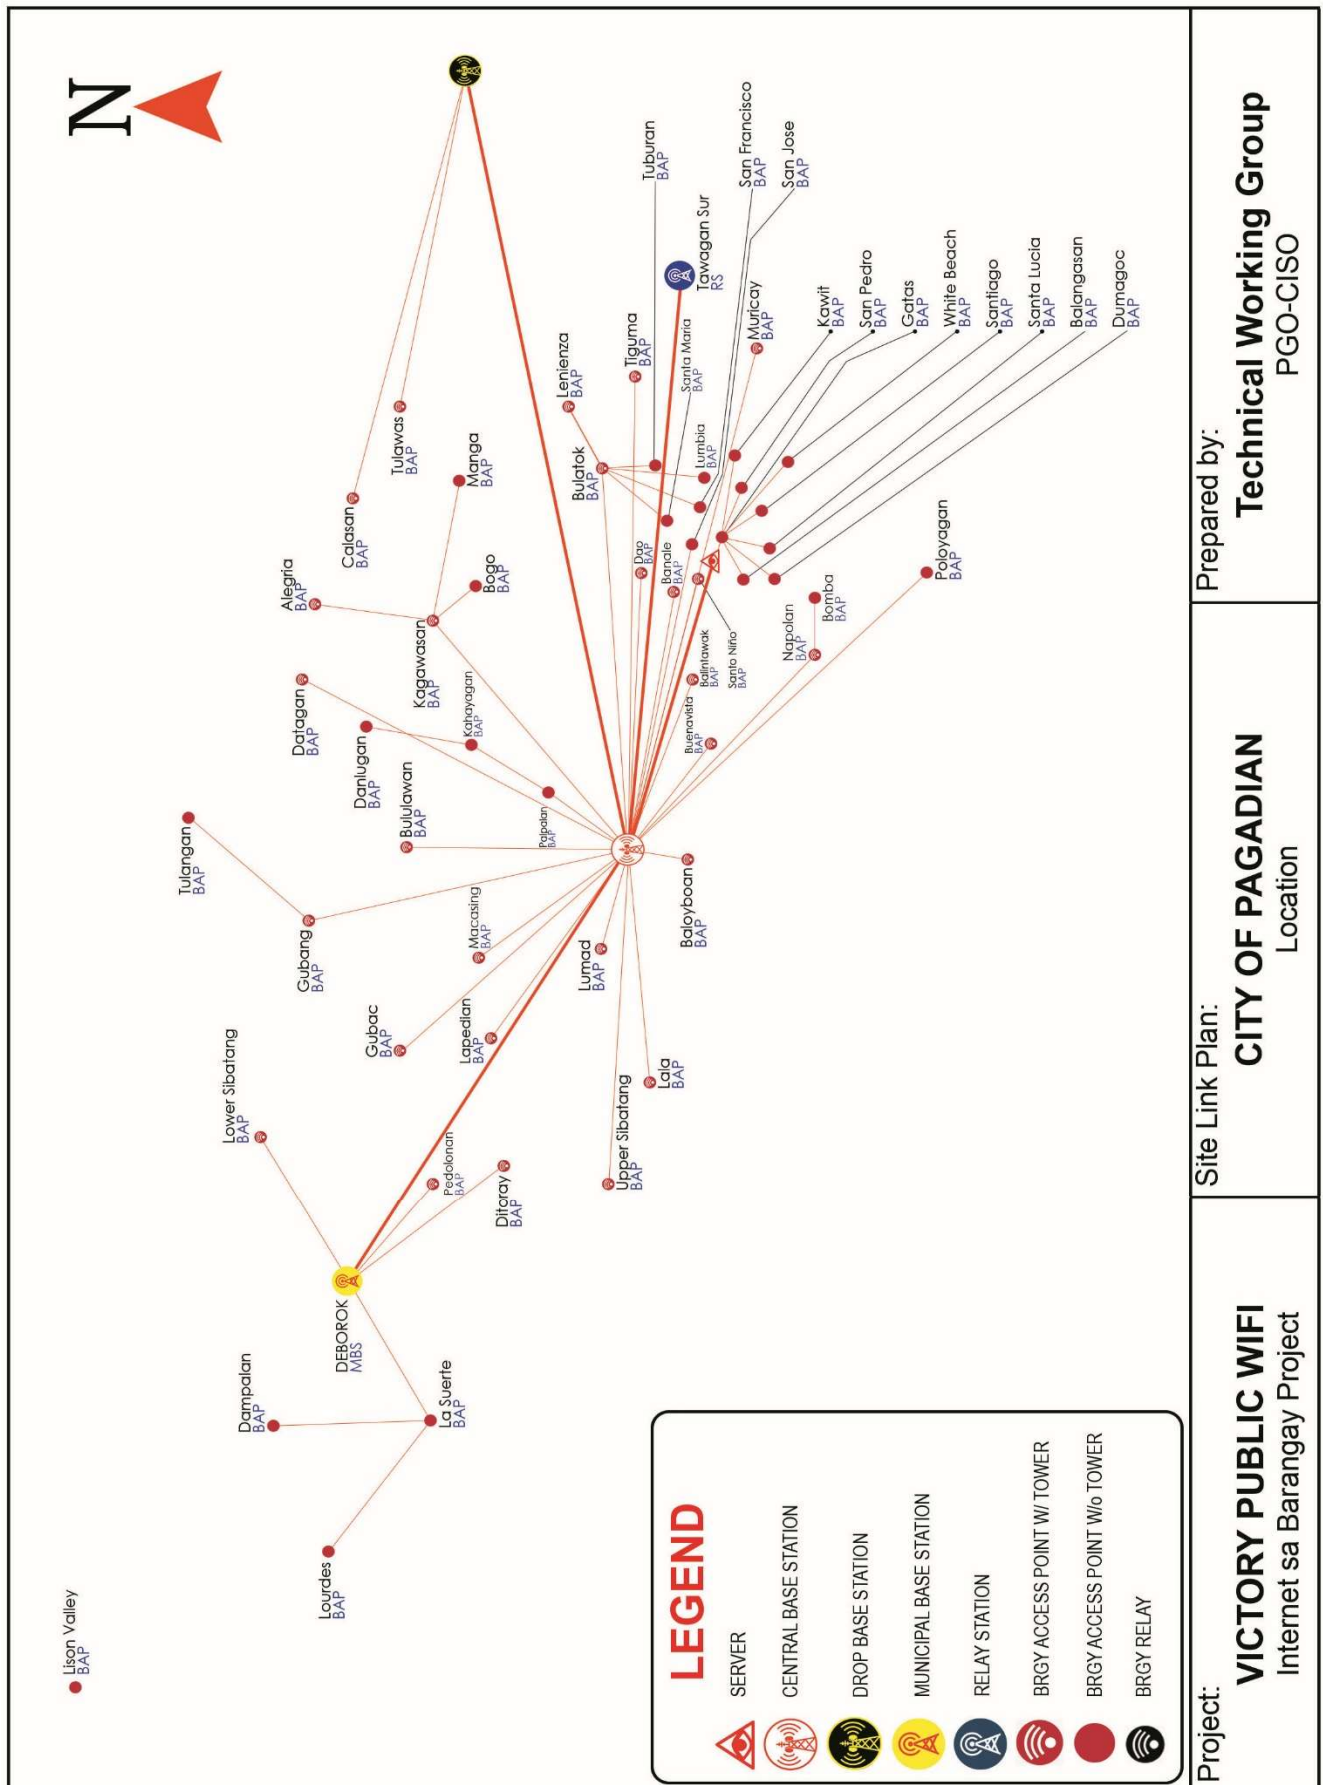

Attachment 2 - Site Link Plan - Labangan

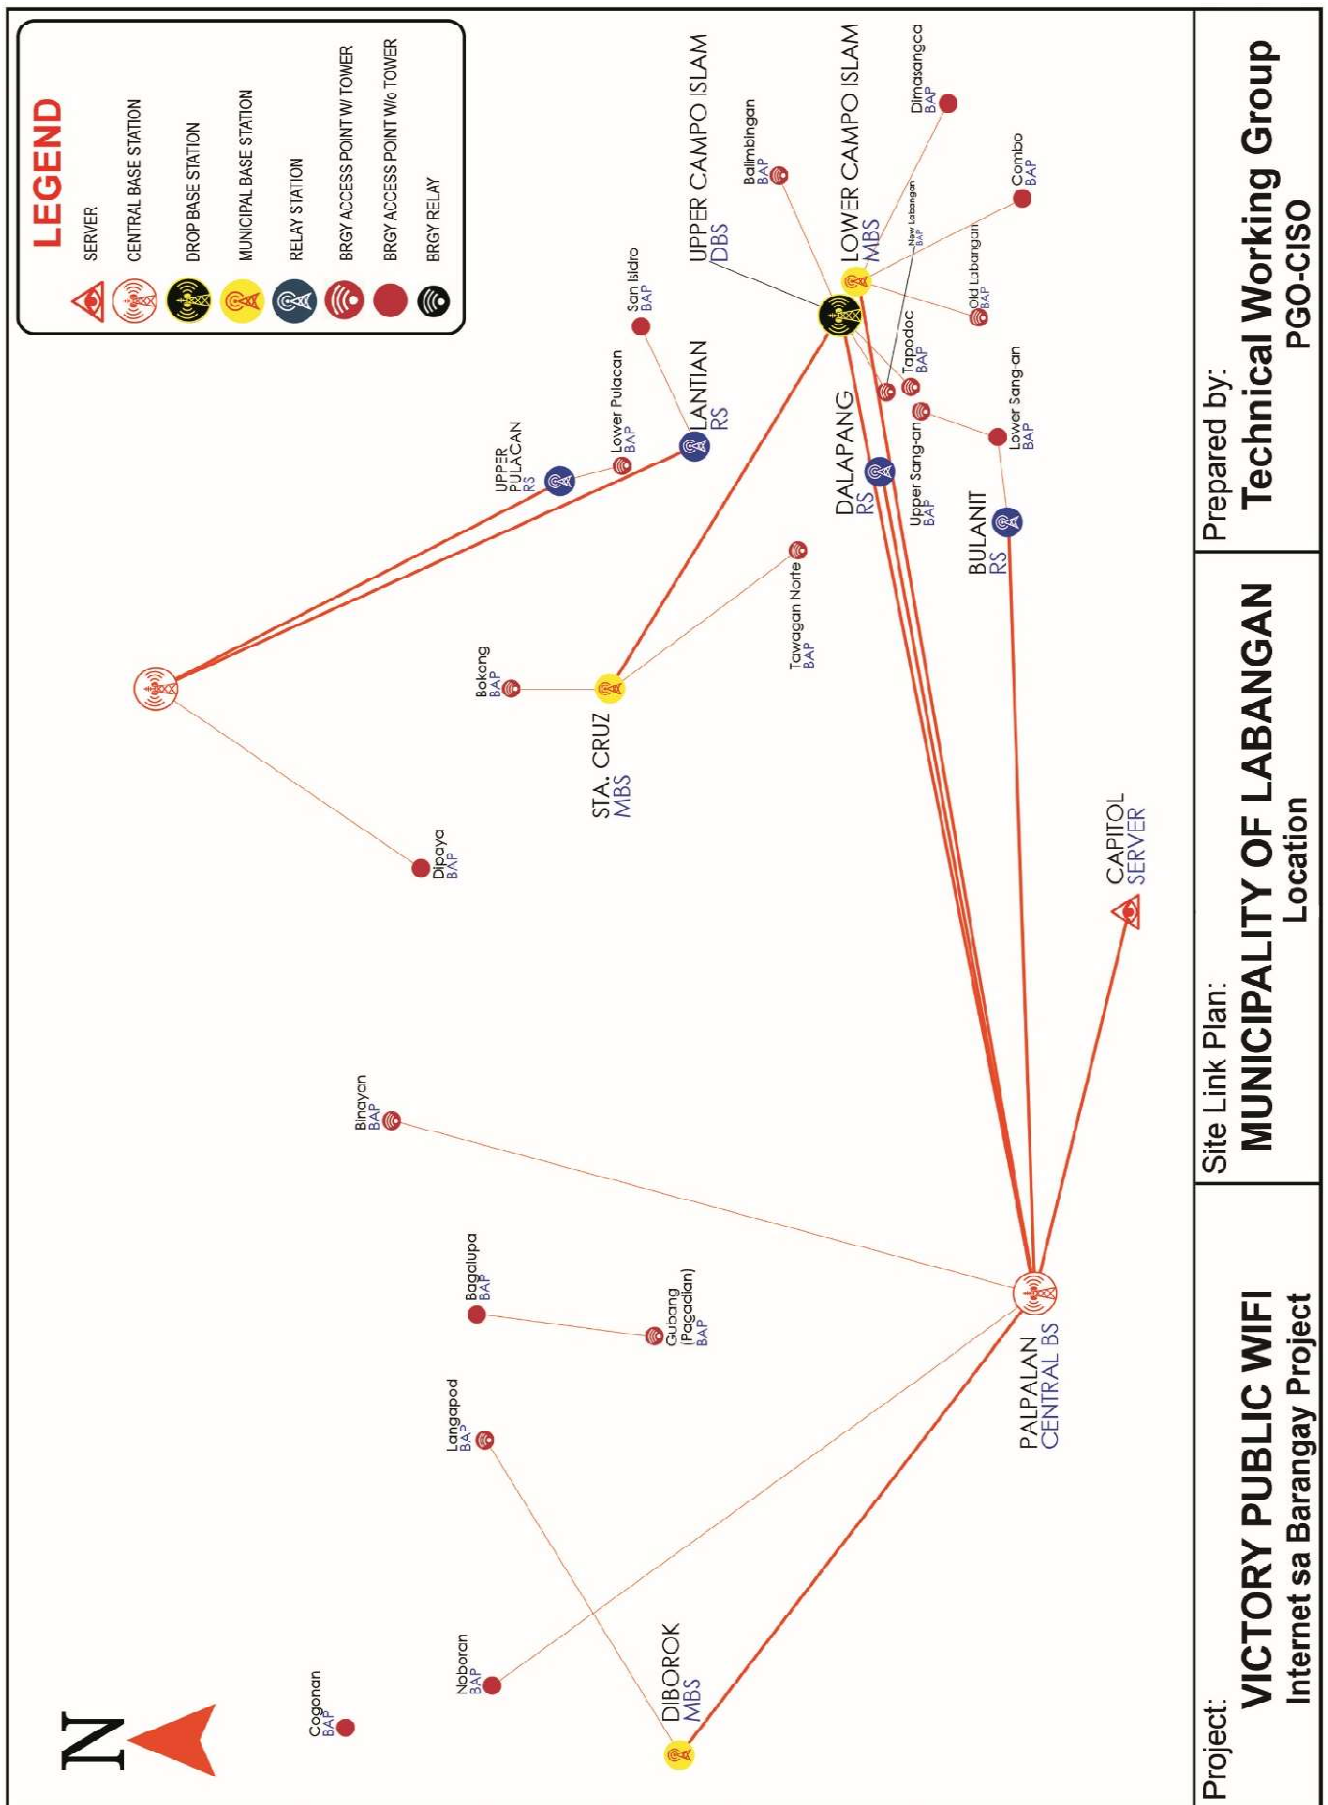

Attachment 3 - Site Link Plan - Tukuran

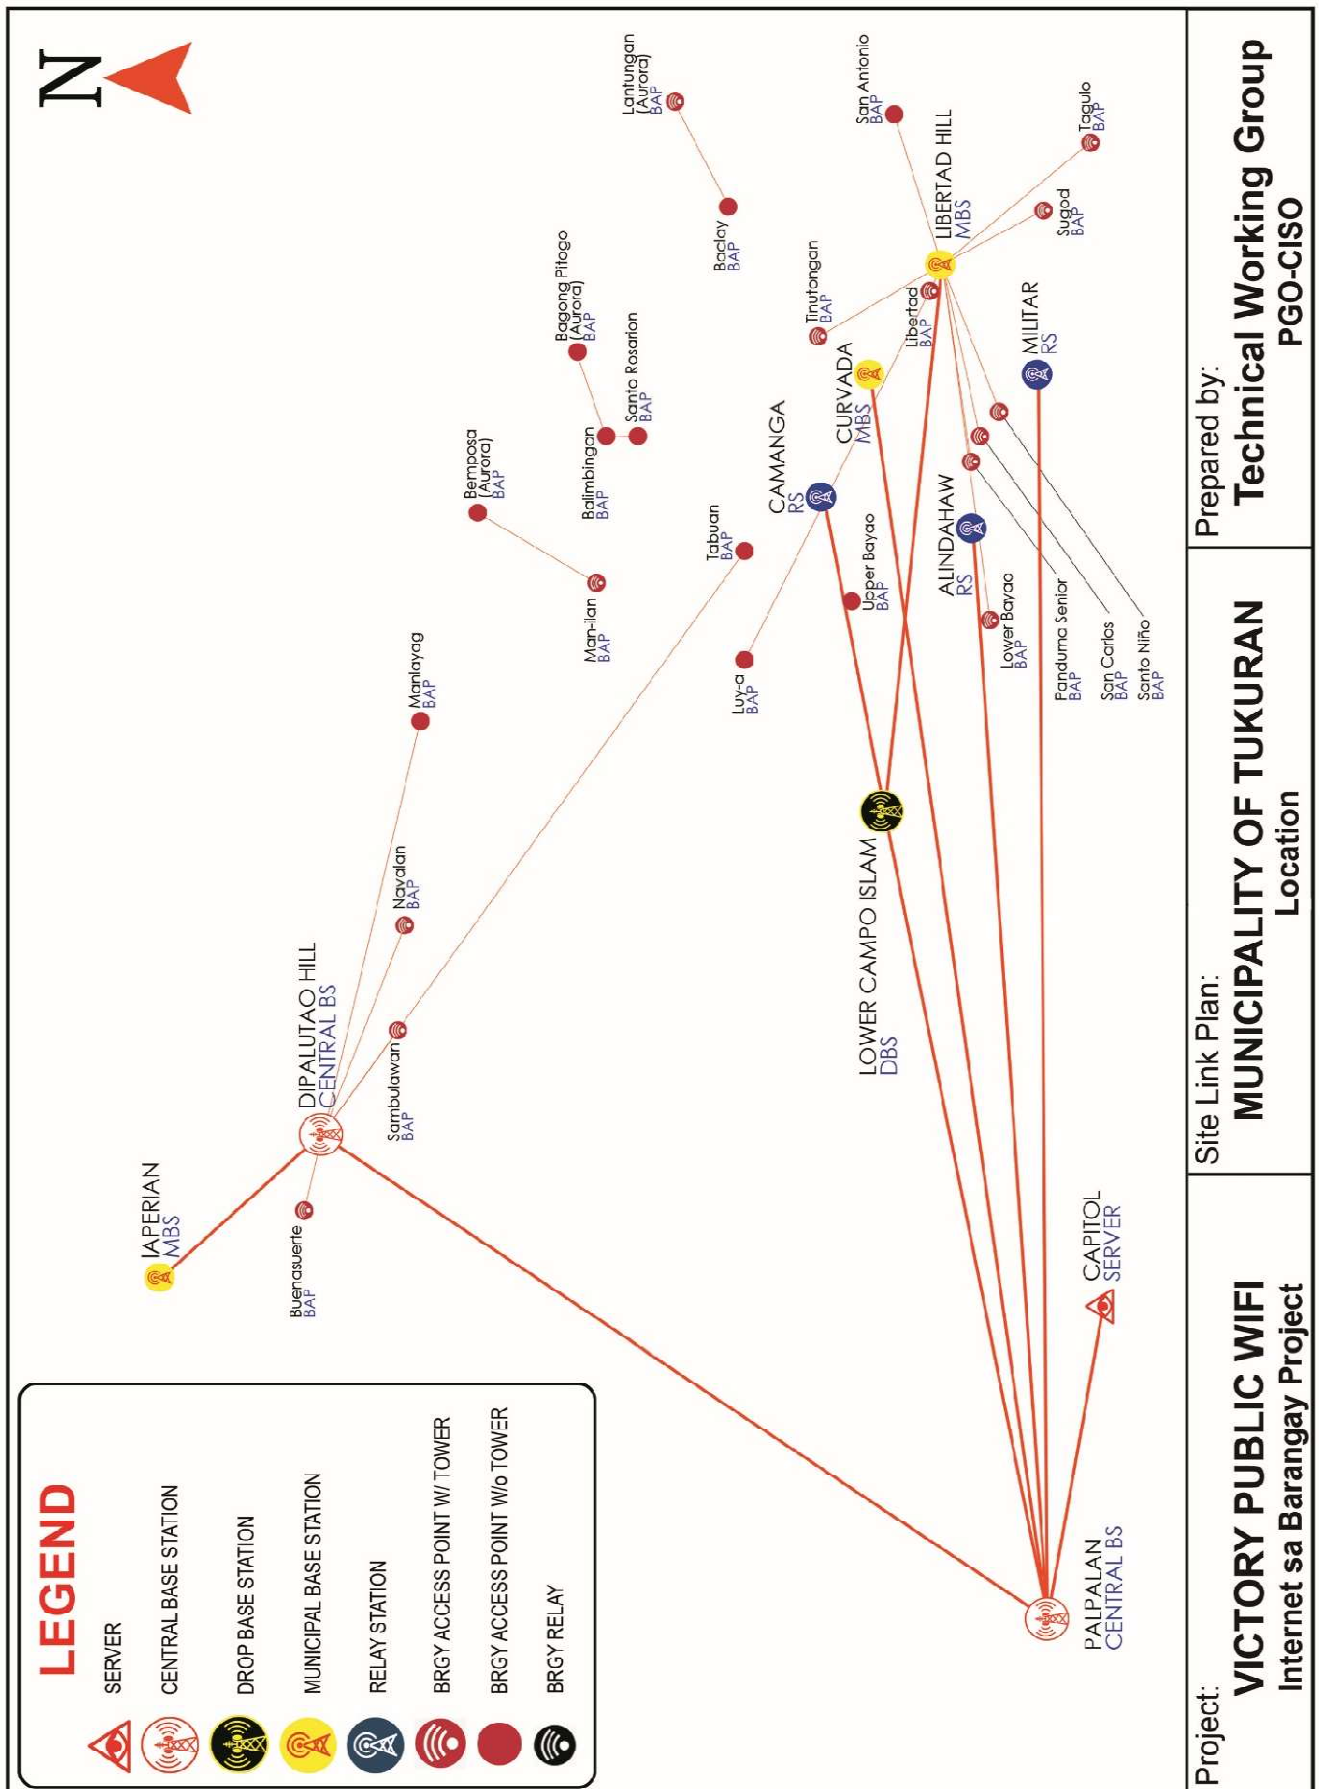

LEGEND

- SERVER
- CENTRAL BASE STATION
- DROP BASE STATION
- MUNICIPAL BASE STATION
- RELAY STATION
- BRGY ACCESS POINT W/ TOWER
- BRGY ACCESS POINT W/o TOWER
- BRGY RELAY

Site Link Plan:


MUNICIPALITY OF AURORA
Location

Project:
VICTORY PUBLIC WIFI
Internet sa Barangay Project

Prepared by:
Technical Working Group
PGO-CISO


The diagram illustrates the network topology for the Victory Public WiFi project in the Municipality of Aurora. It shows the central server, the central base station, and the various base stations and access points connected to the network. The network is organized into several clusters, including the Palpalan CBS, the Dipalutao CBS, and the various Brgy Access Points. The map also shows the location of the Capitol Server and the various Brgy Access Points. The network is designed to provide internet access to the entire municipality, with a focus on the barangays. The diagram is a detailed site link plan, showing the physical connections between the various components of the network. It includes a legend, a north arrow, and a detailed map of the municipality. The map shows the various base stations and access points, and the connections between them. The network is designed to be a robust and reliable system, capable of providing internet access to all the residents of the municipality. The diagram is a technical drawing, and it is intended for use by the technical working group and the PGO-CISO. It is a detailed and comprehensive plan, and it is a key component of the project. The diagram is a site link plan, and it is a technical drawing. It is a detailed and comprehensive plan, and it is a key component of the project. The diagram is a site link plan, and it is a technical drawing. It is a detailed and comprehensive plan, and it is a key component of the project.

Attachment 5 - Site Link Plan - Ramon Magsaysay

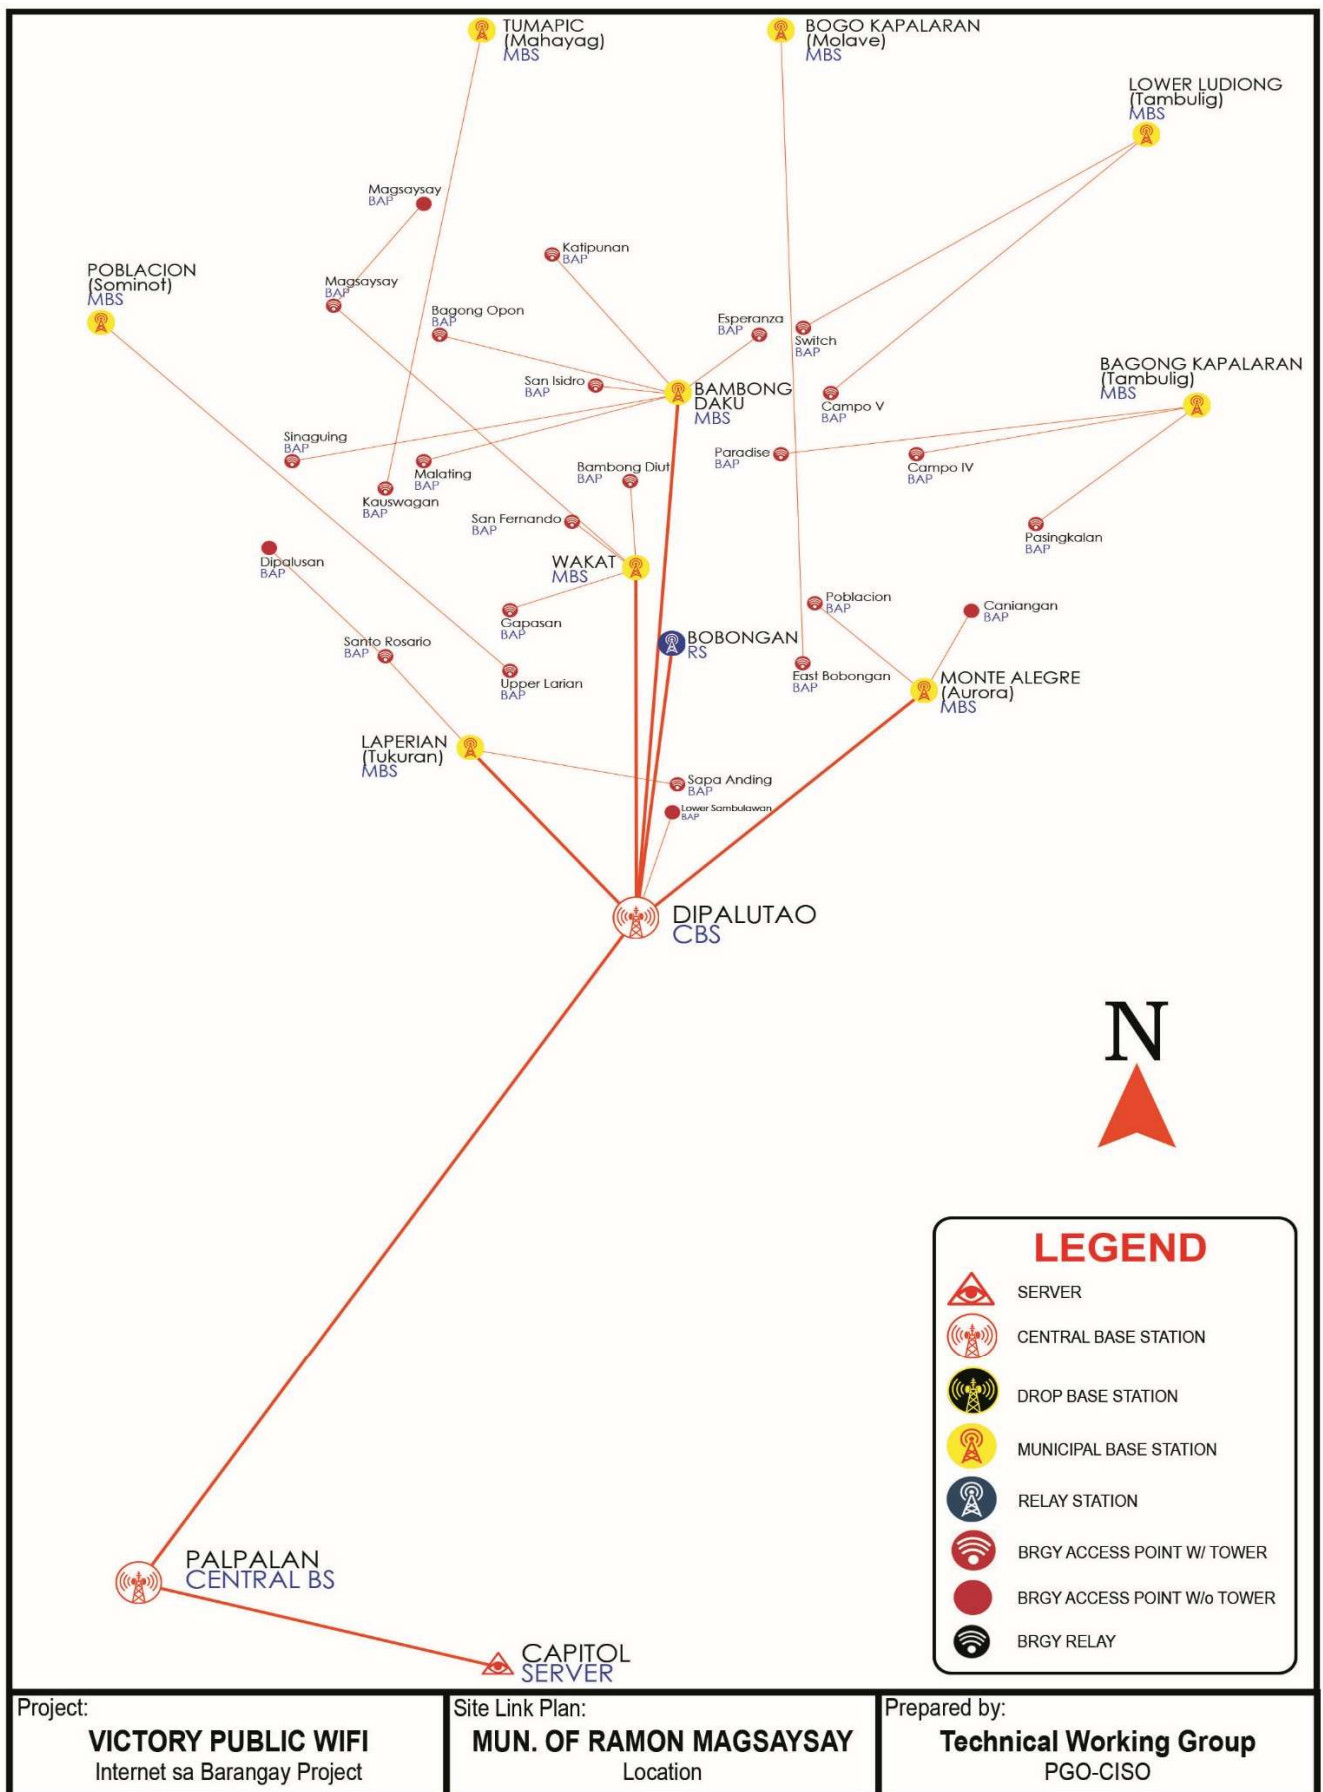


[illegible]


Attachment 7 - Site Link Plan - Molave

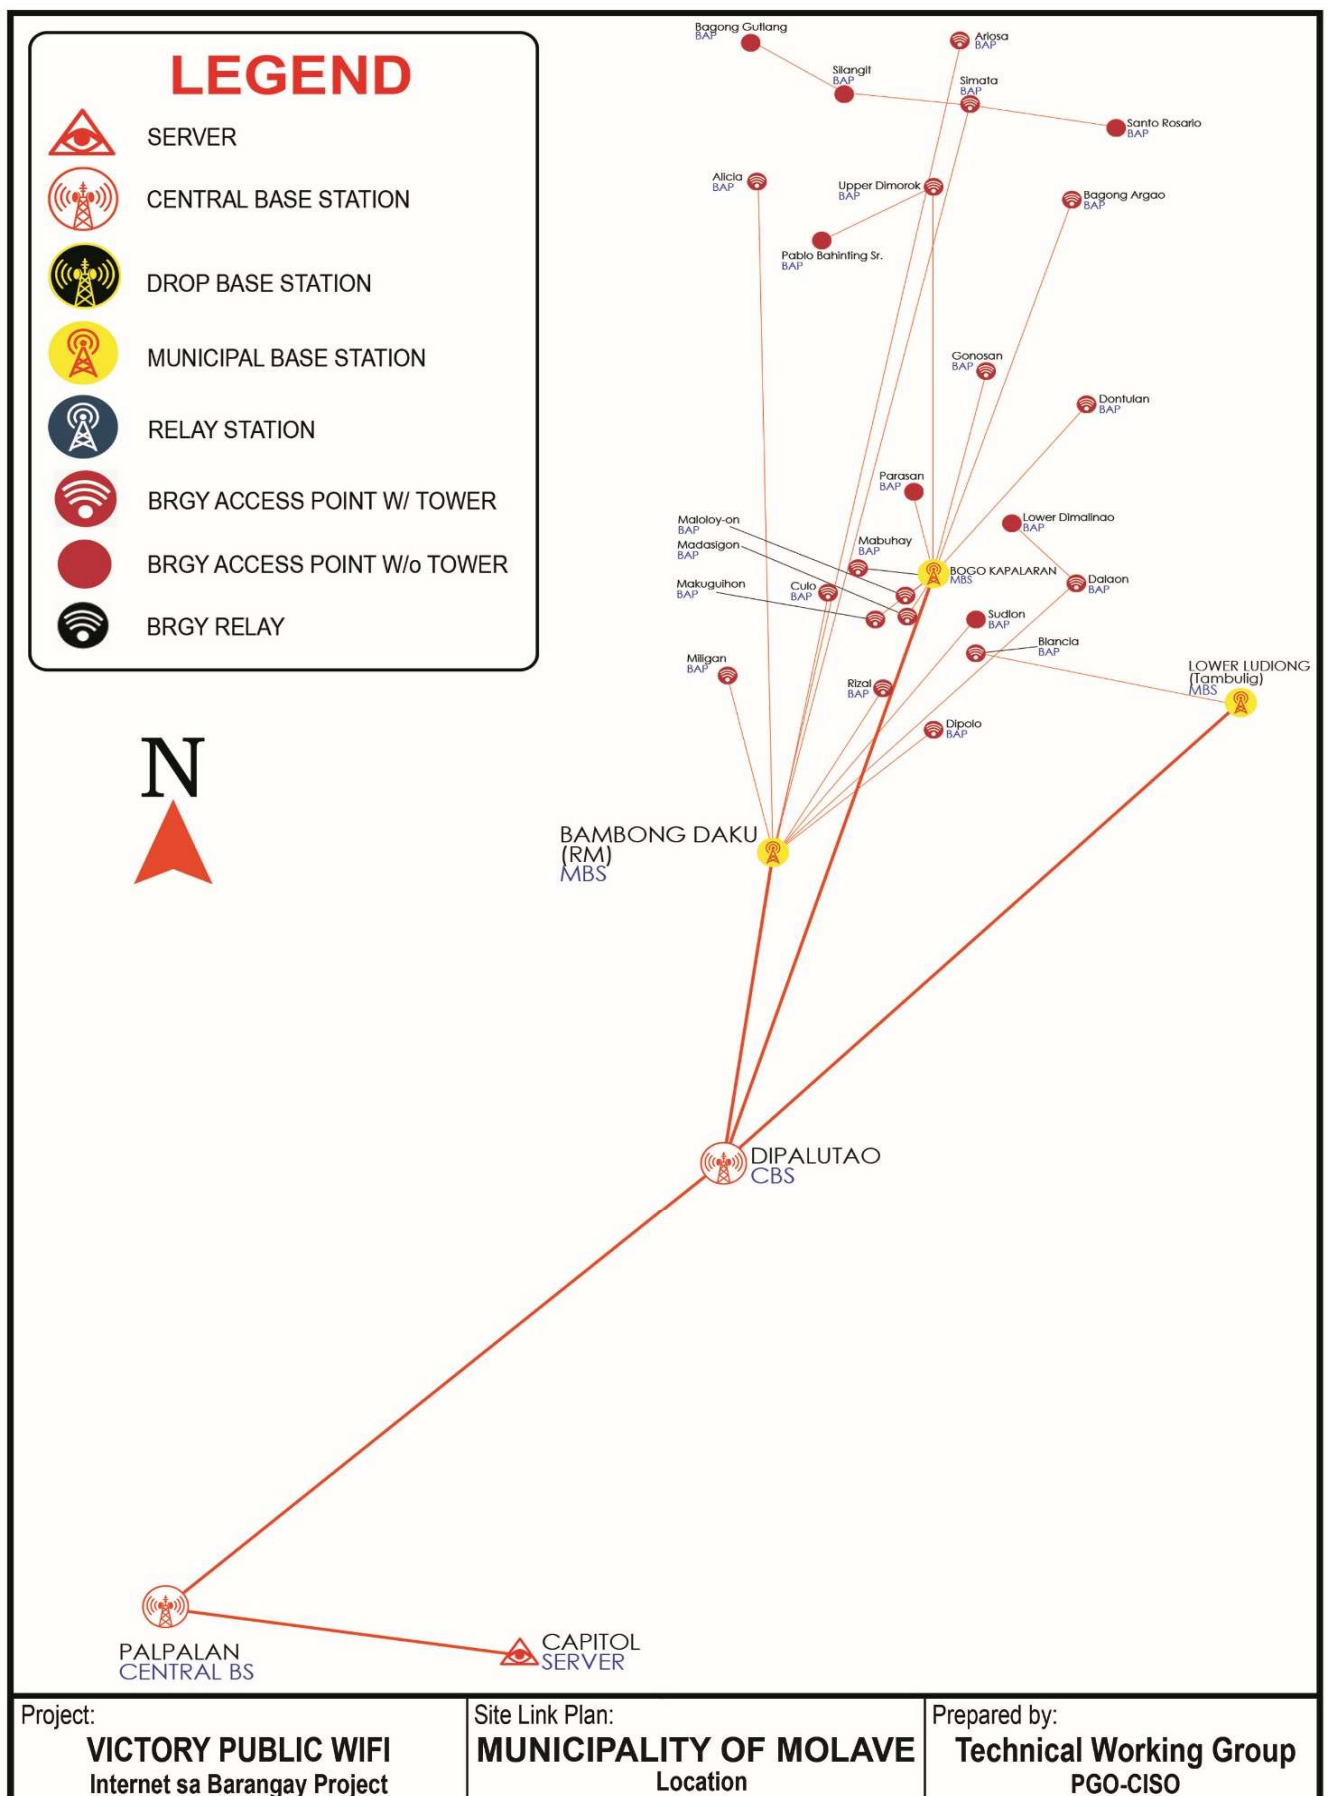


Attachment 8 - Site Link Plan - Mahayag

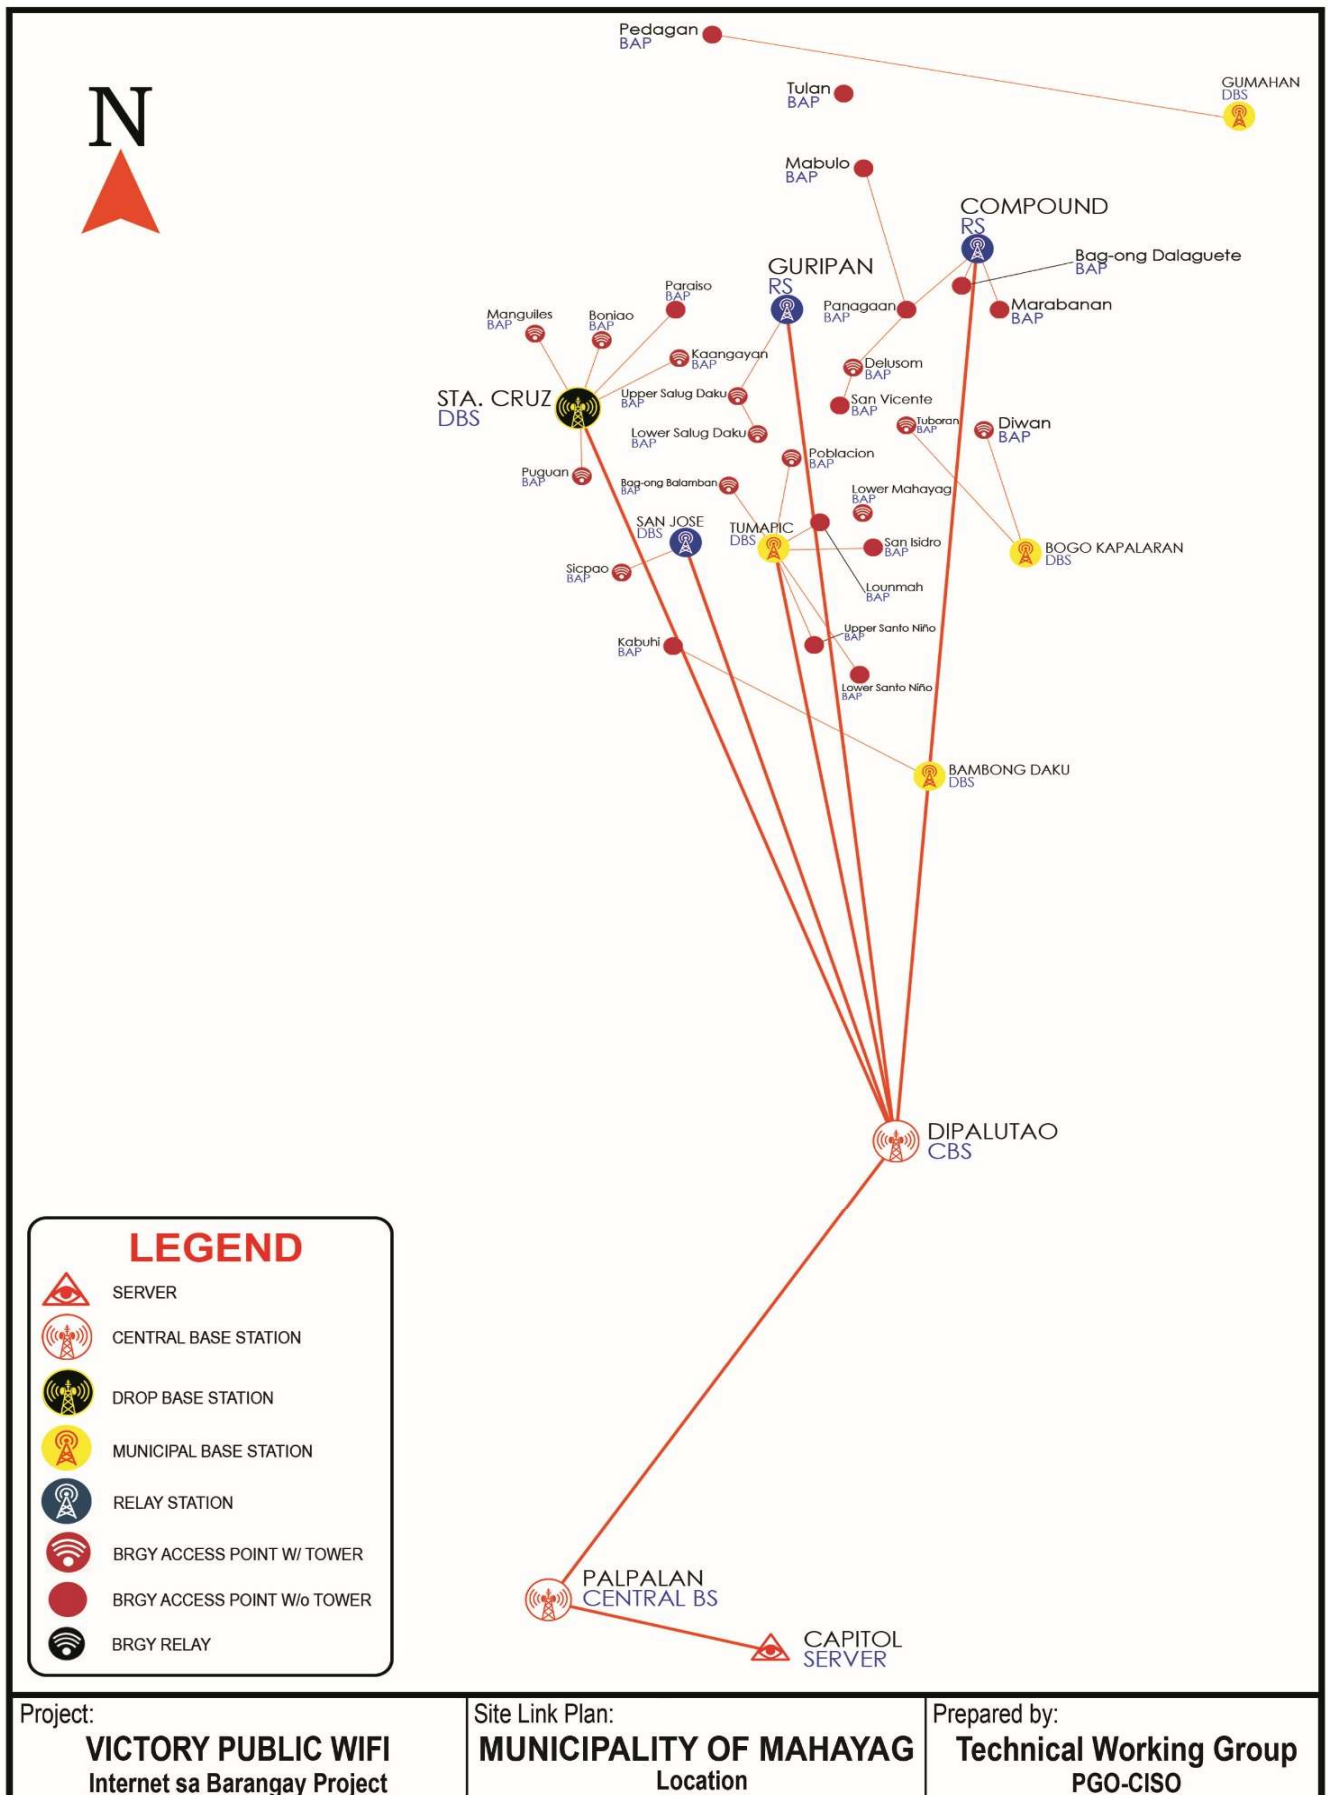


Attachment 9 - Site Link Plan - Josefina

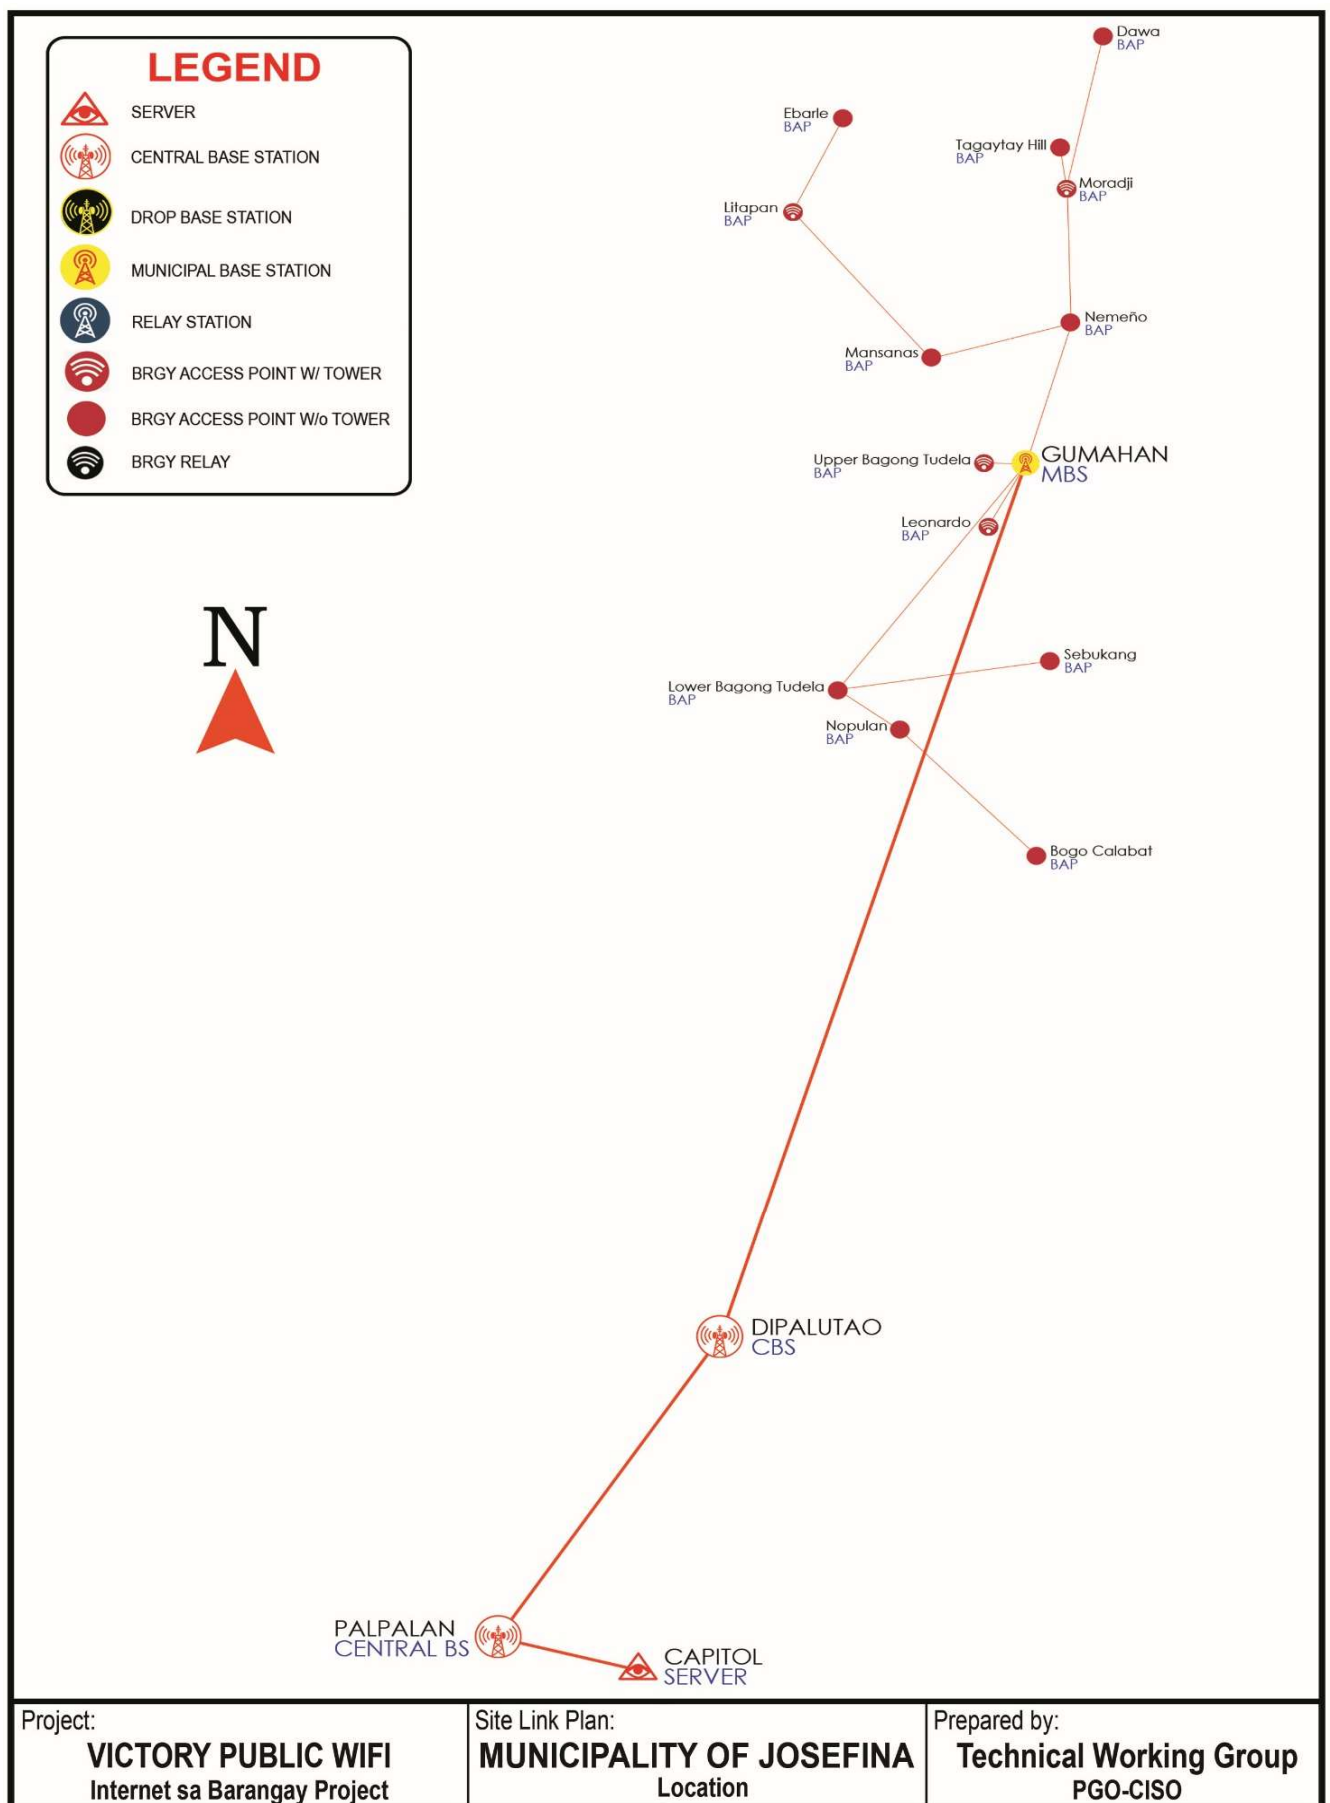


Attachment 10 - Site Link Plan - Dumingag

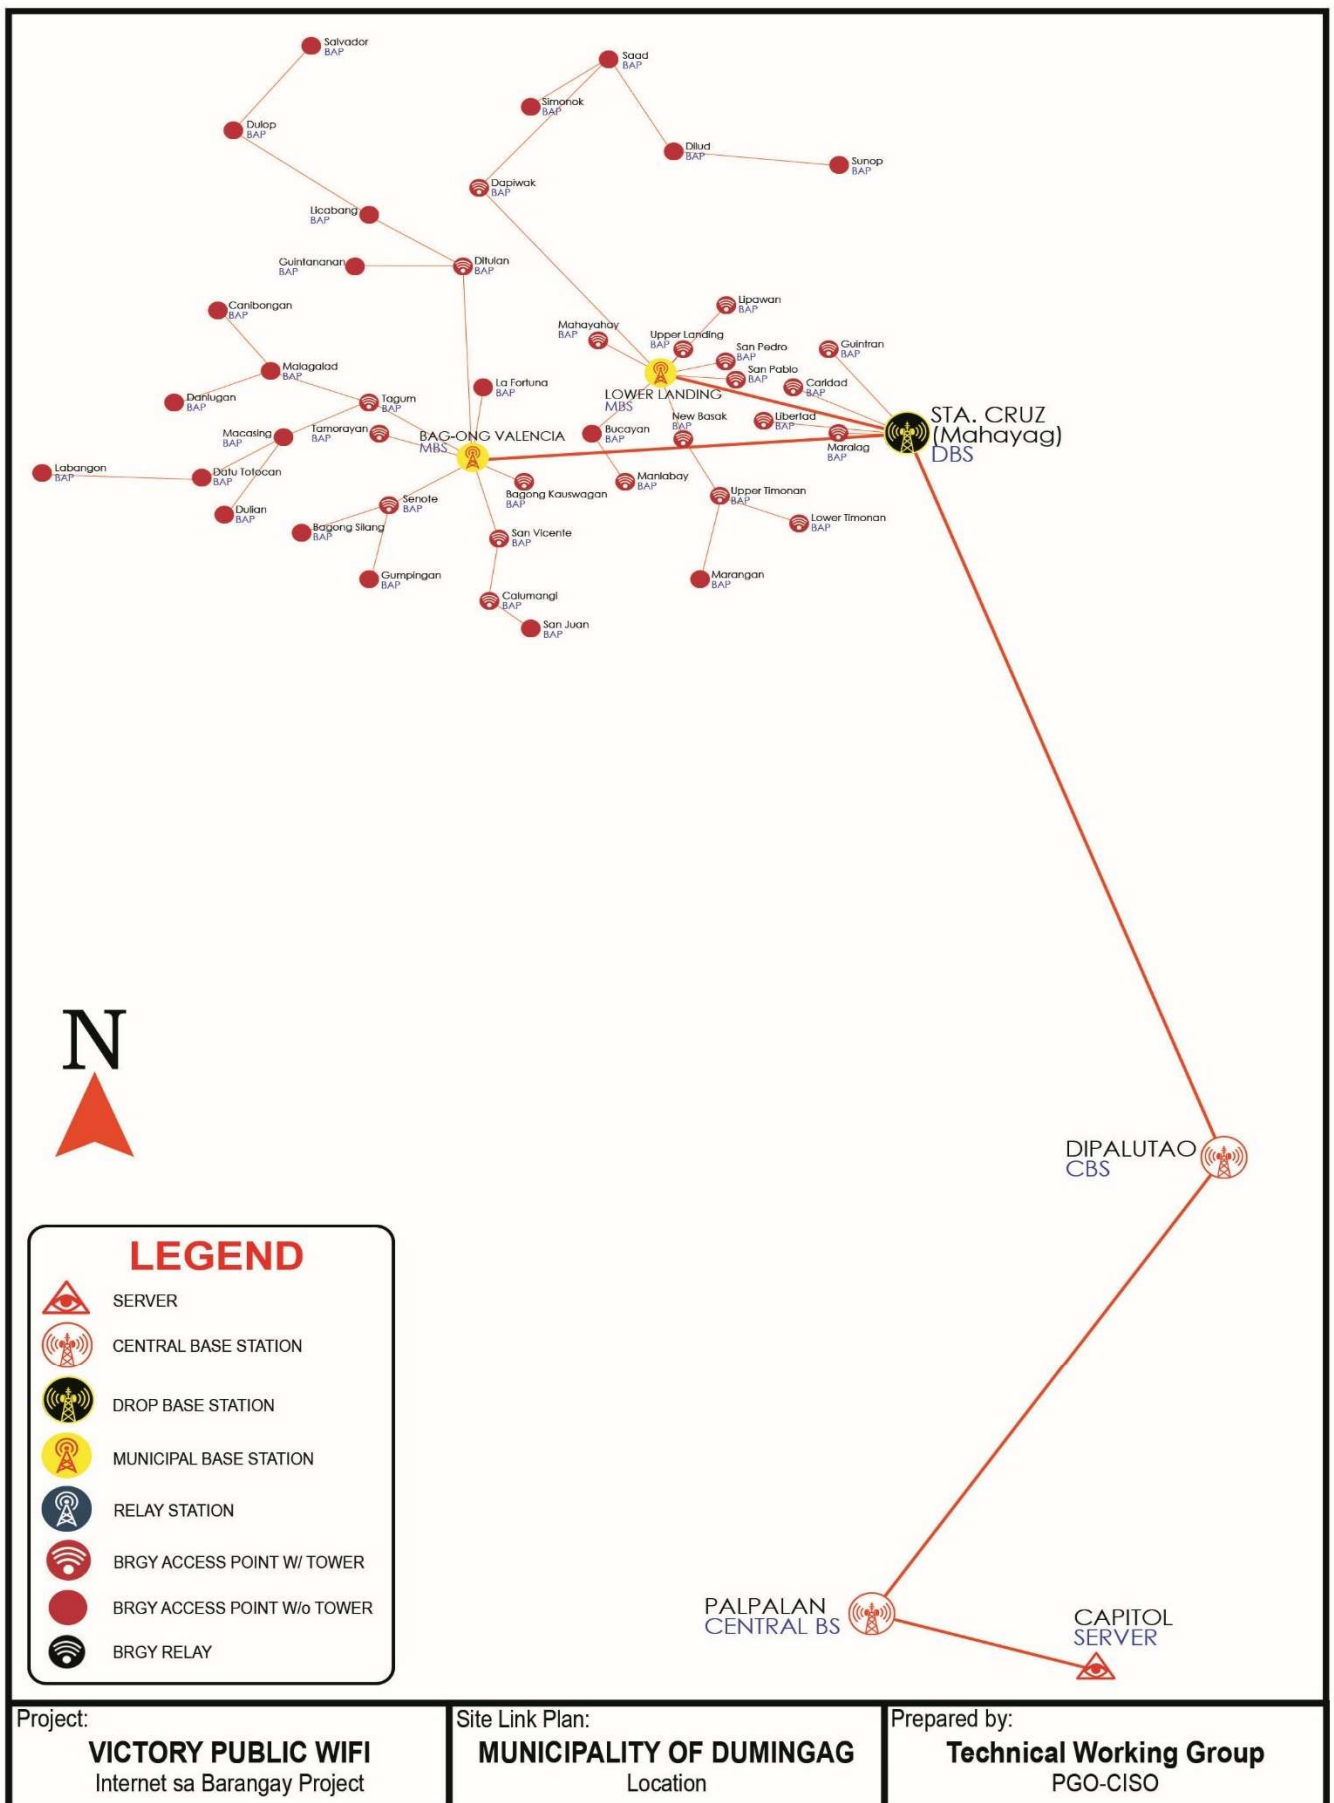


Attachment 11 - Site Link Plan - Sominot

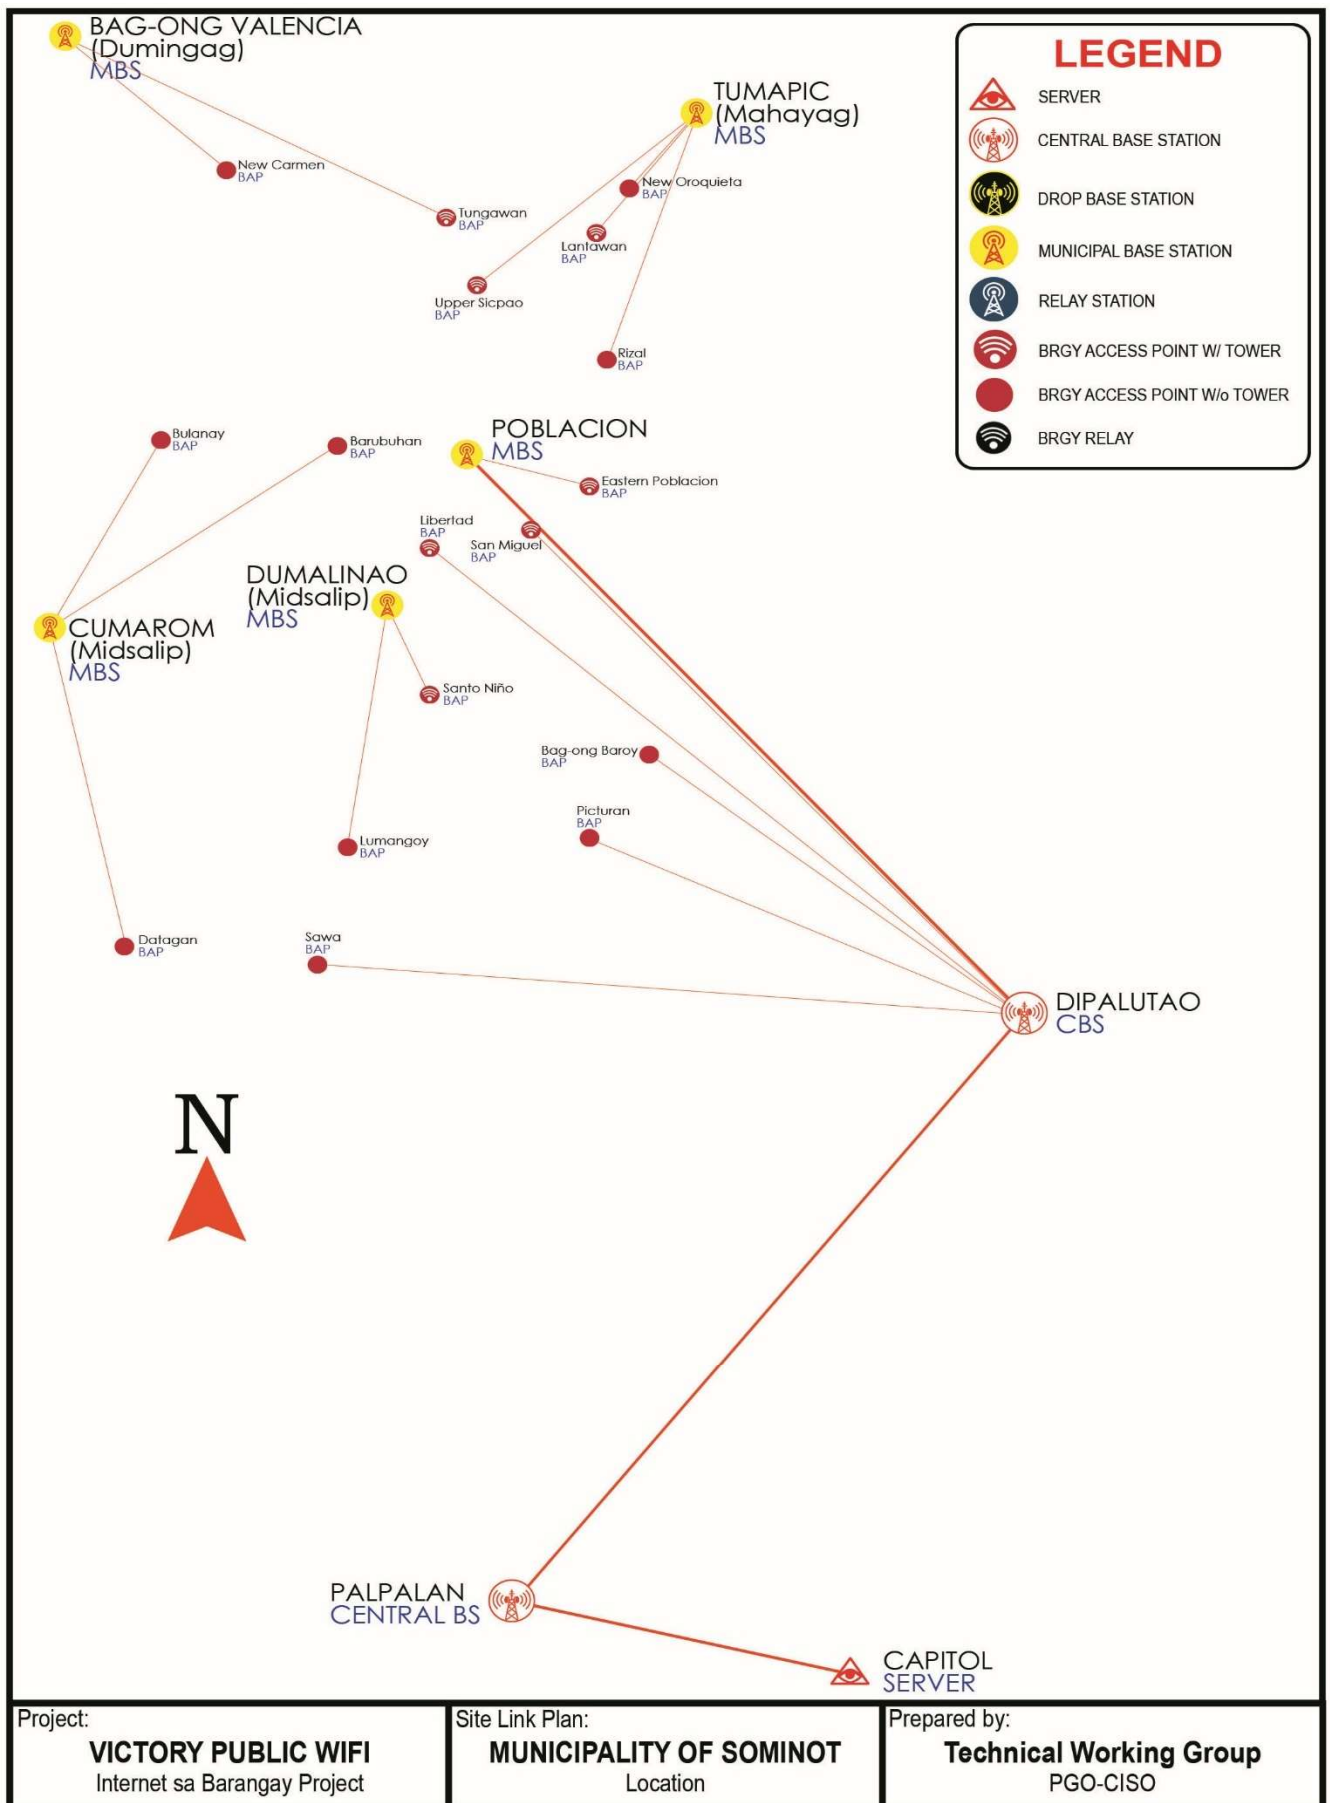


Attachment 12 - Site Link Plan - Midsalip

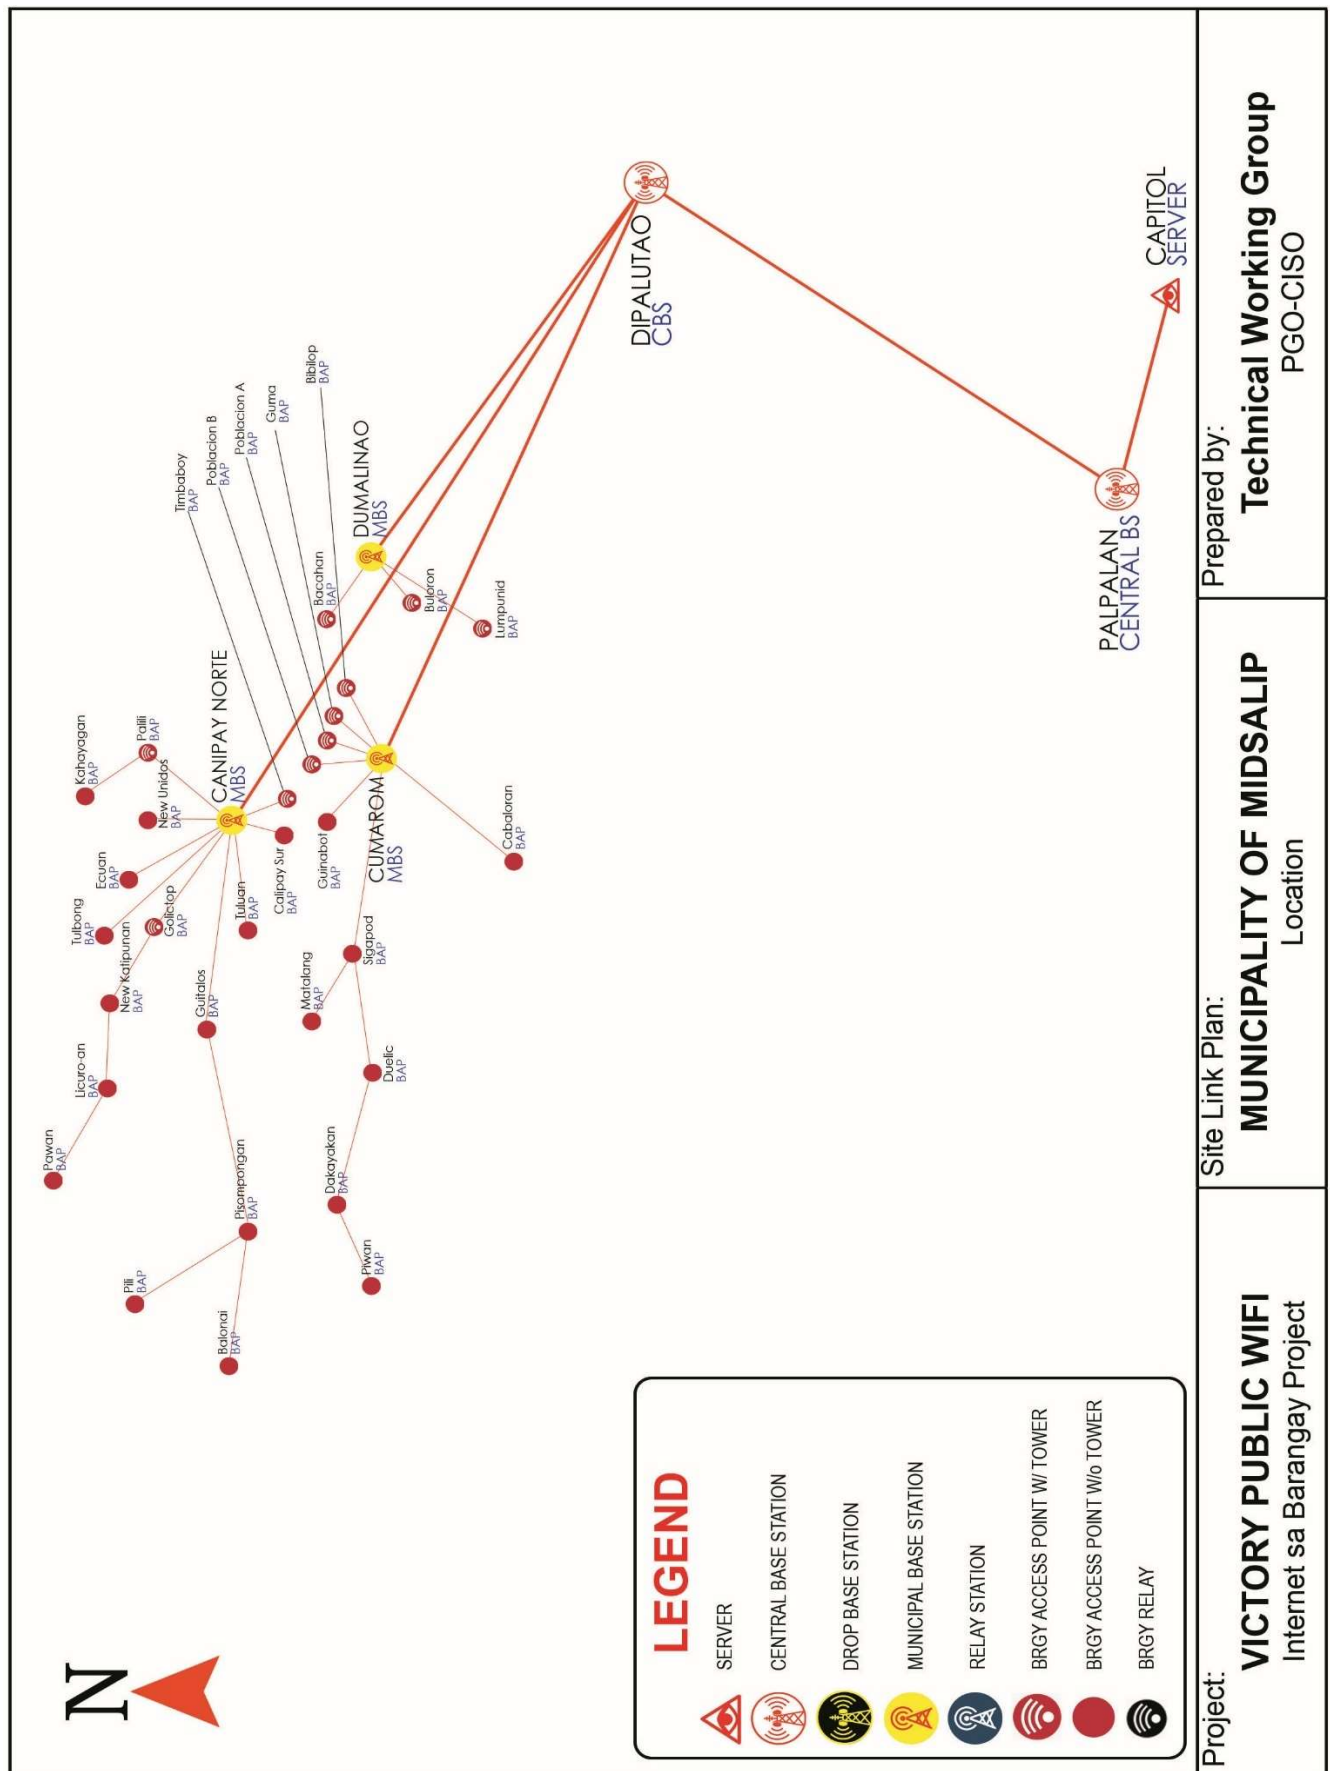


Attachment 13 - Site Link Plan - Dumalinao

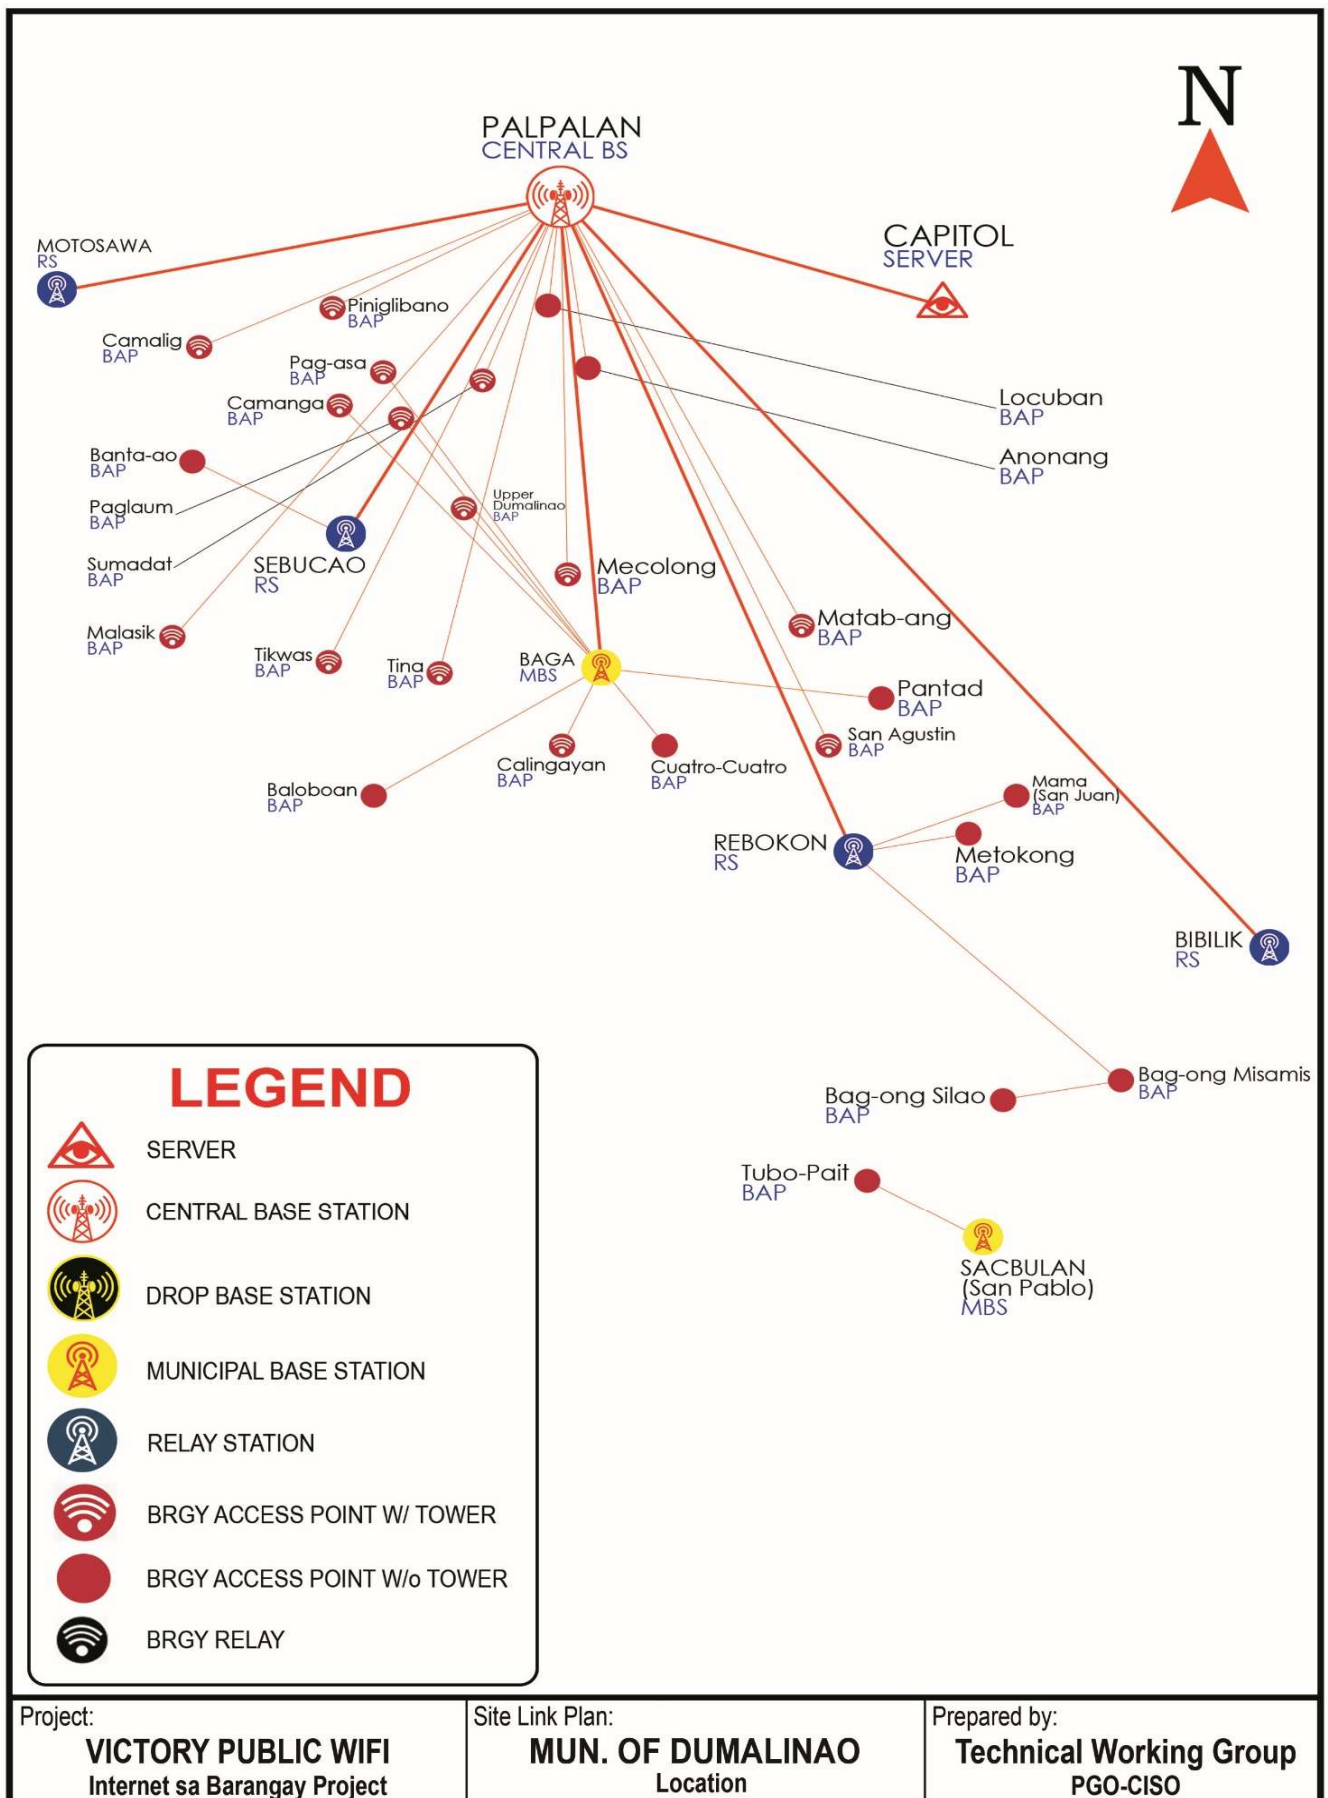


Attachment 14 - Site Link Plan - Guipos

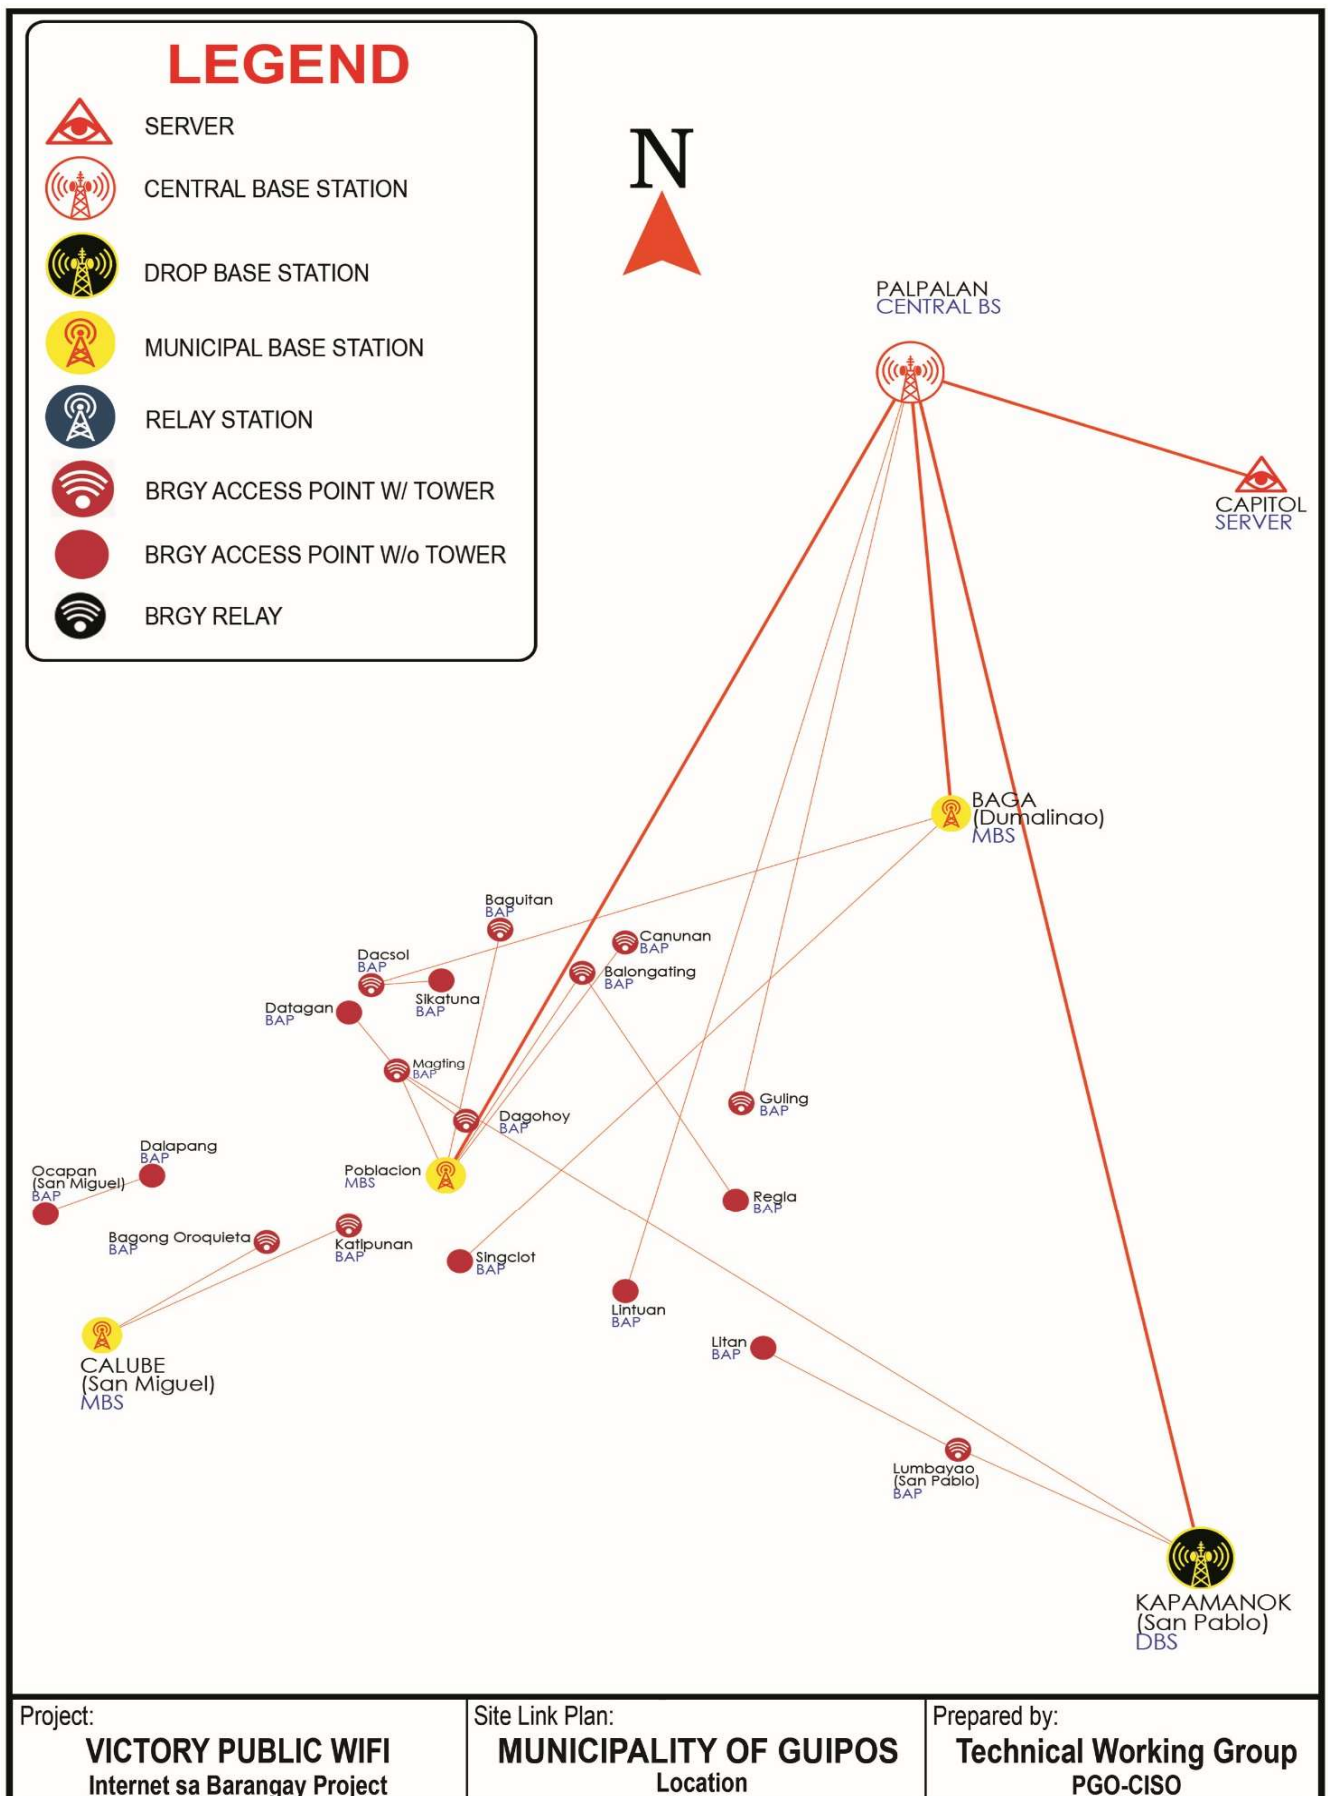


Attachment 15 - Site Link Plan - San Pablo

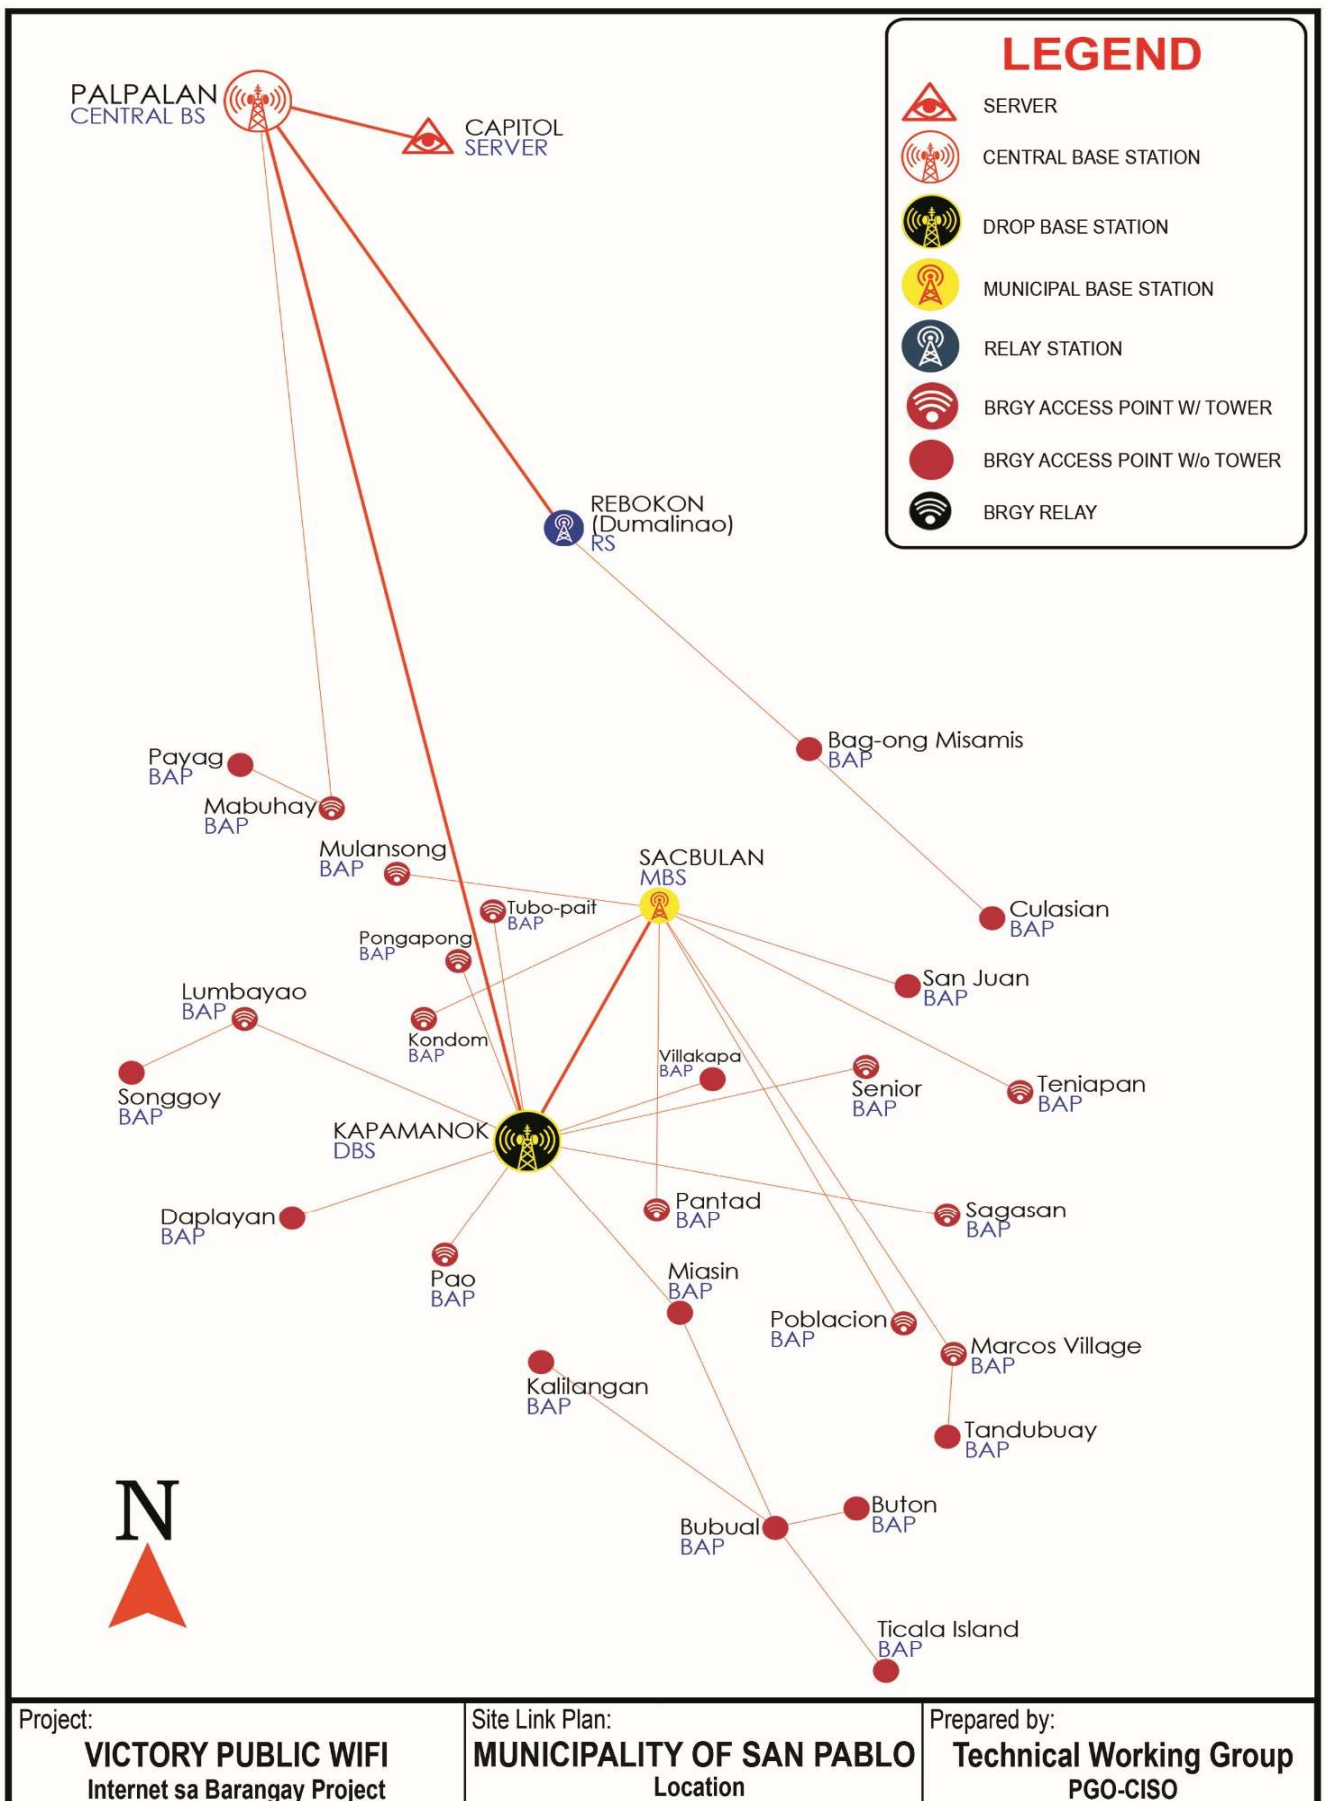


Attachment 16 - Site Link Plan - Dinas

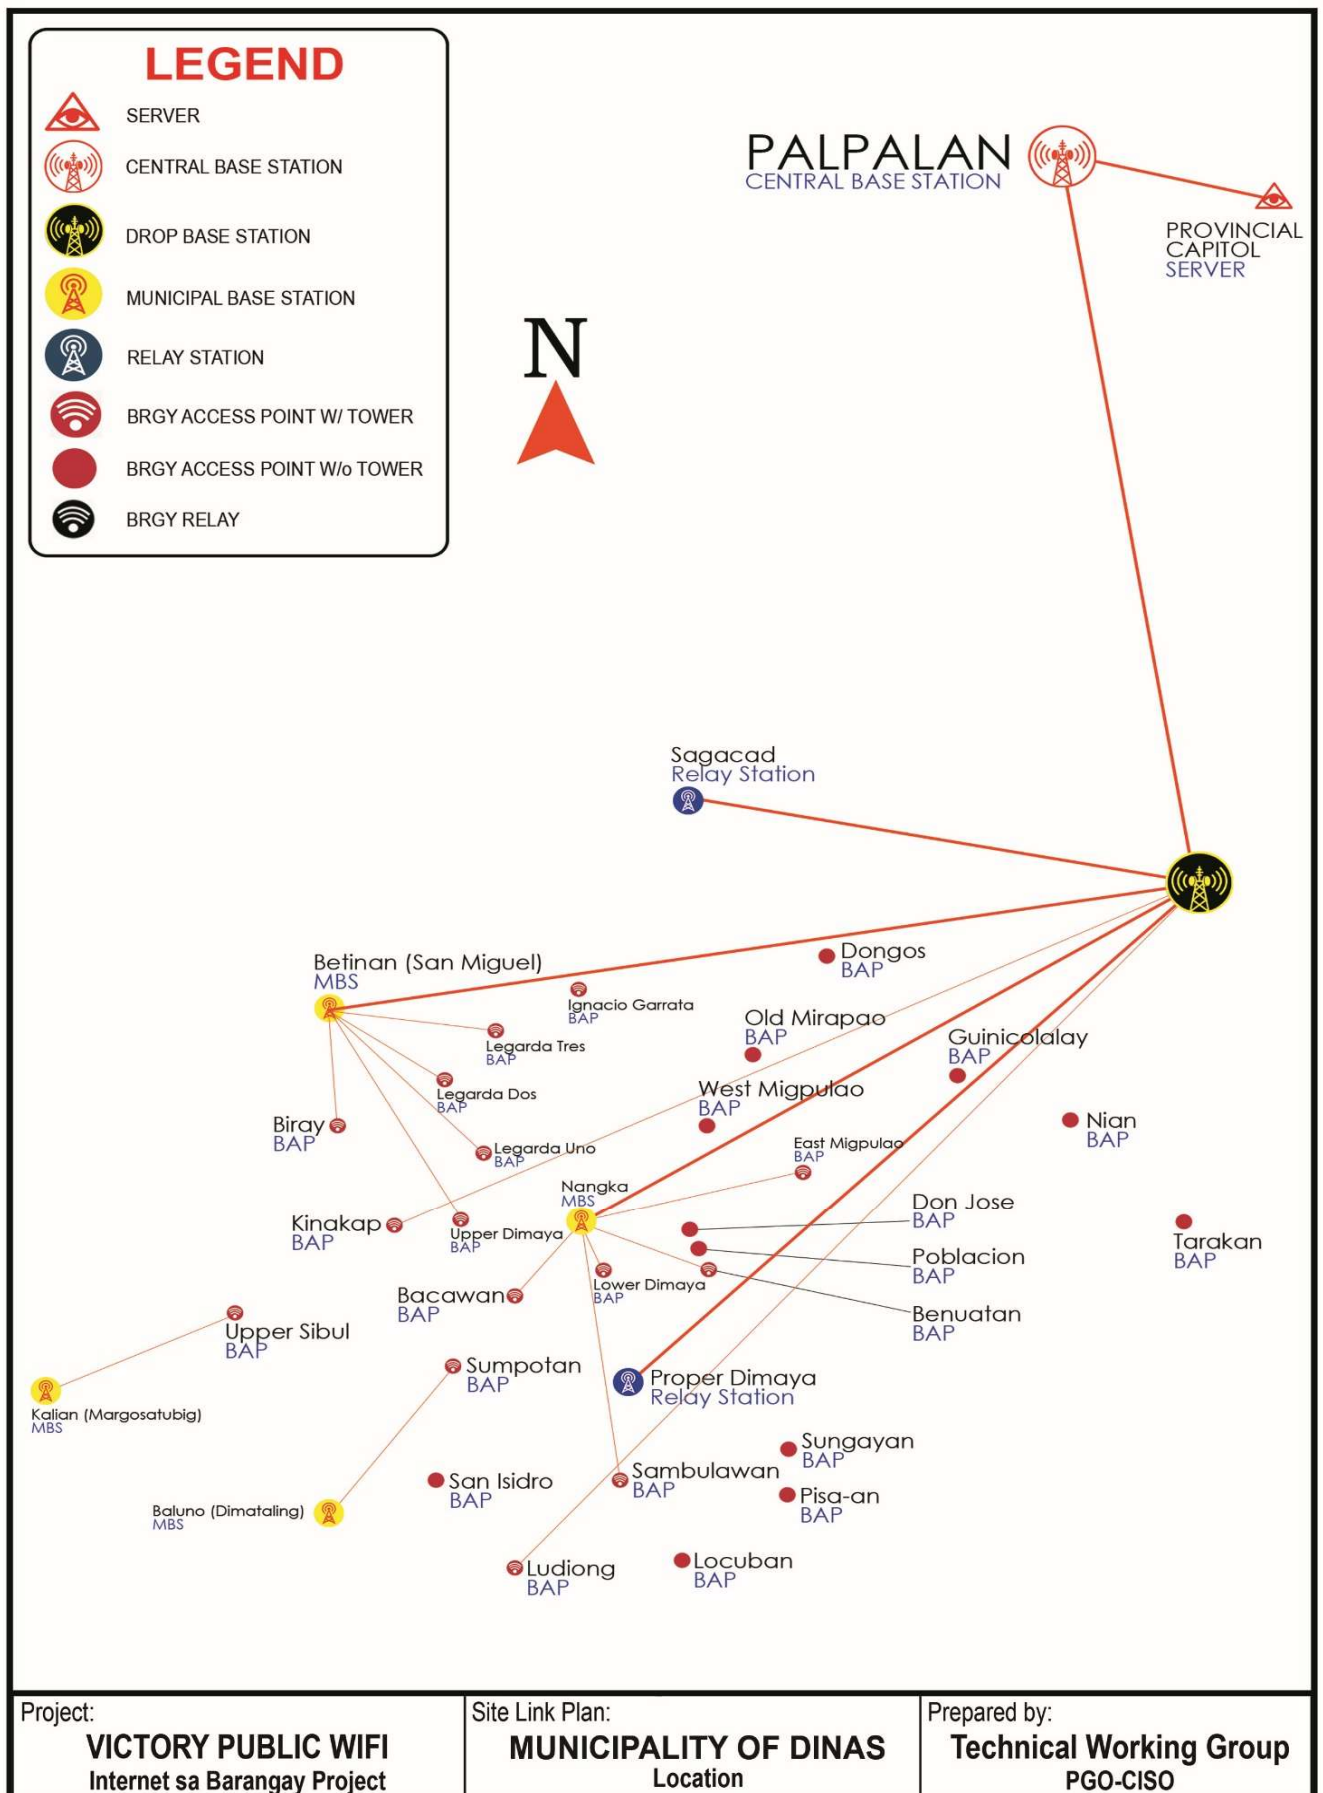


Attachment 17 - Site Link Plan - Dimataling

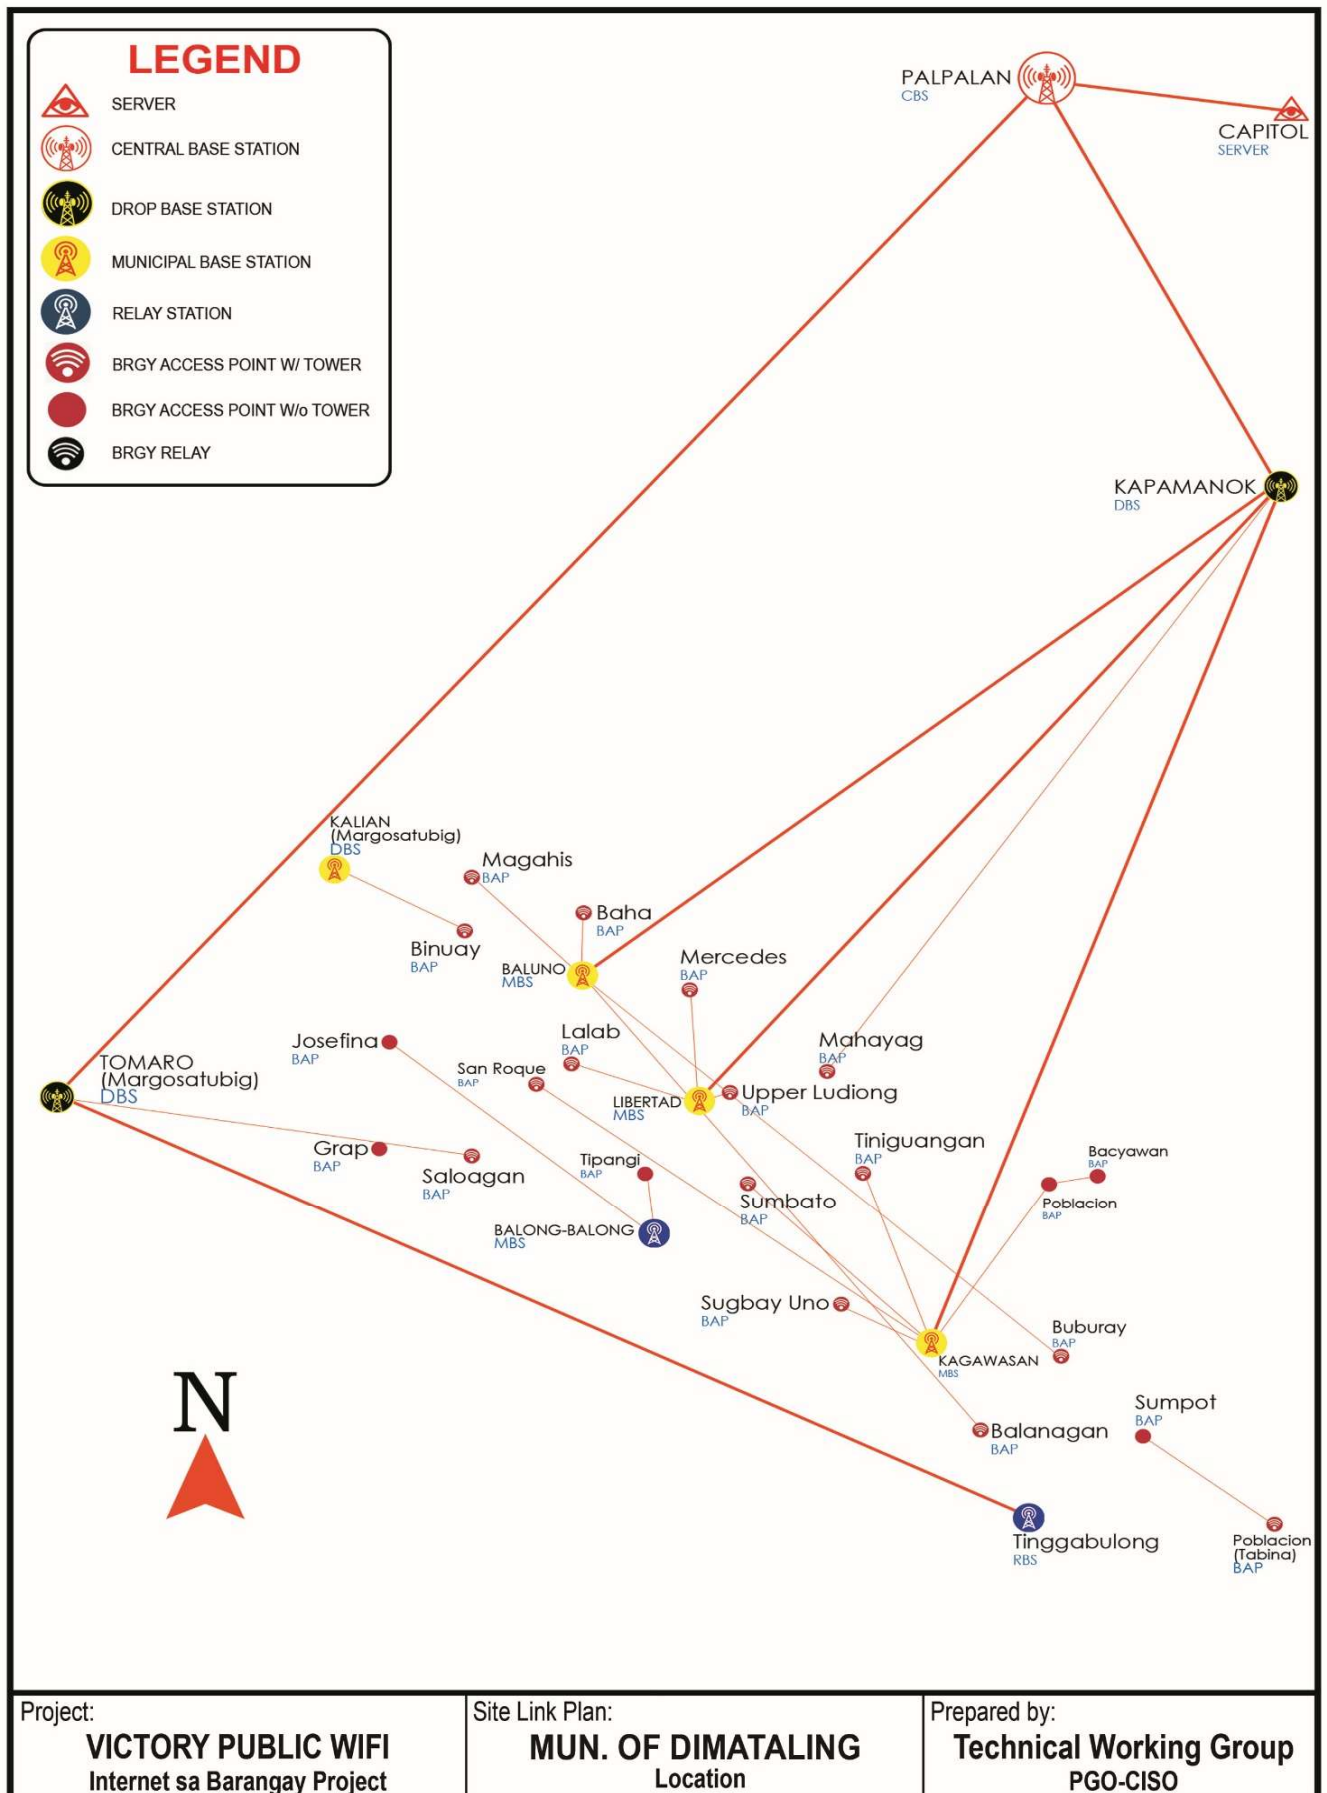


Attachment 18 - Site Link Plan - Tabina

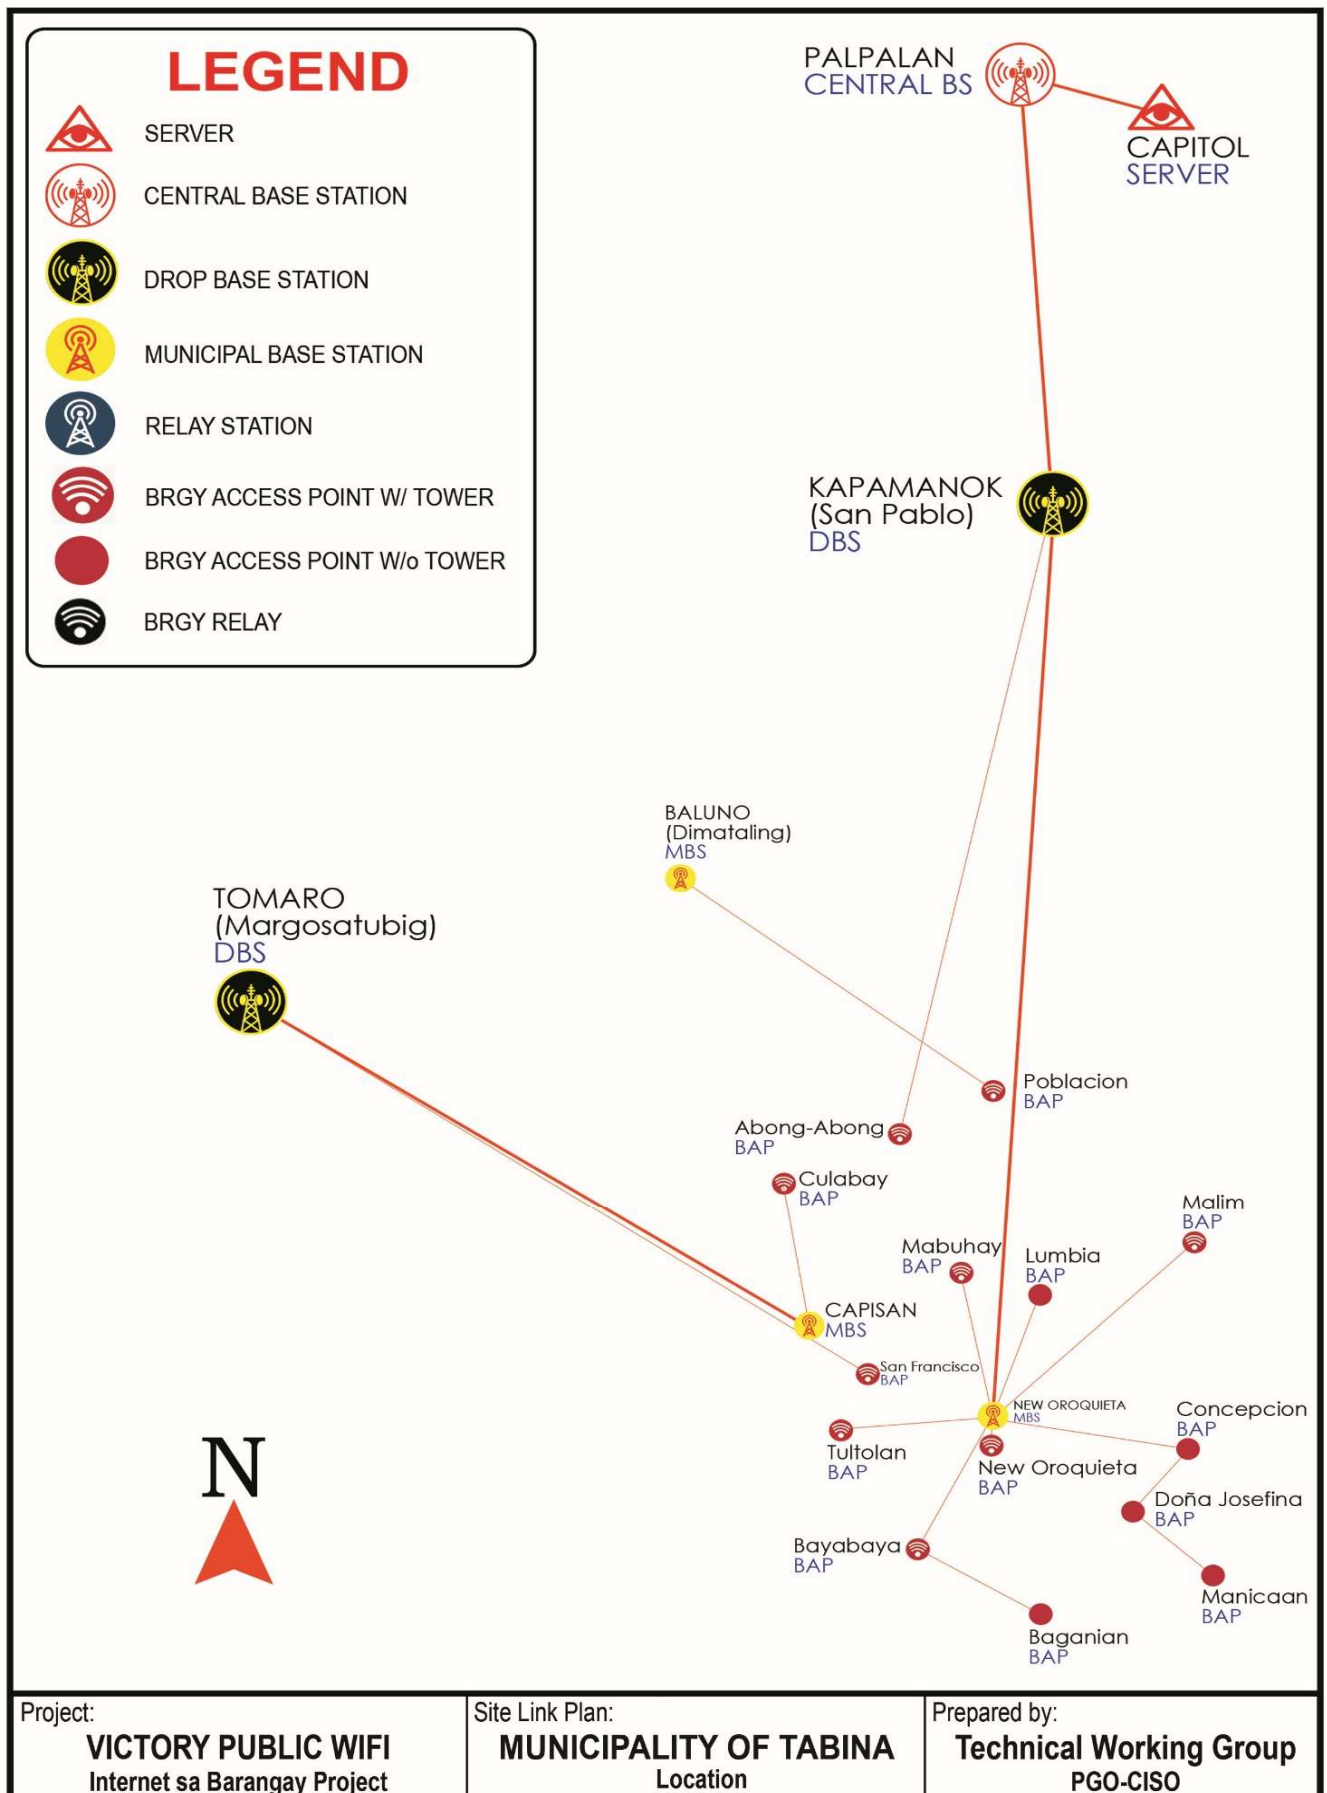


Attachment 19 - Site Link Plan - Pitogo

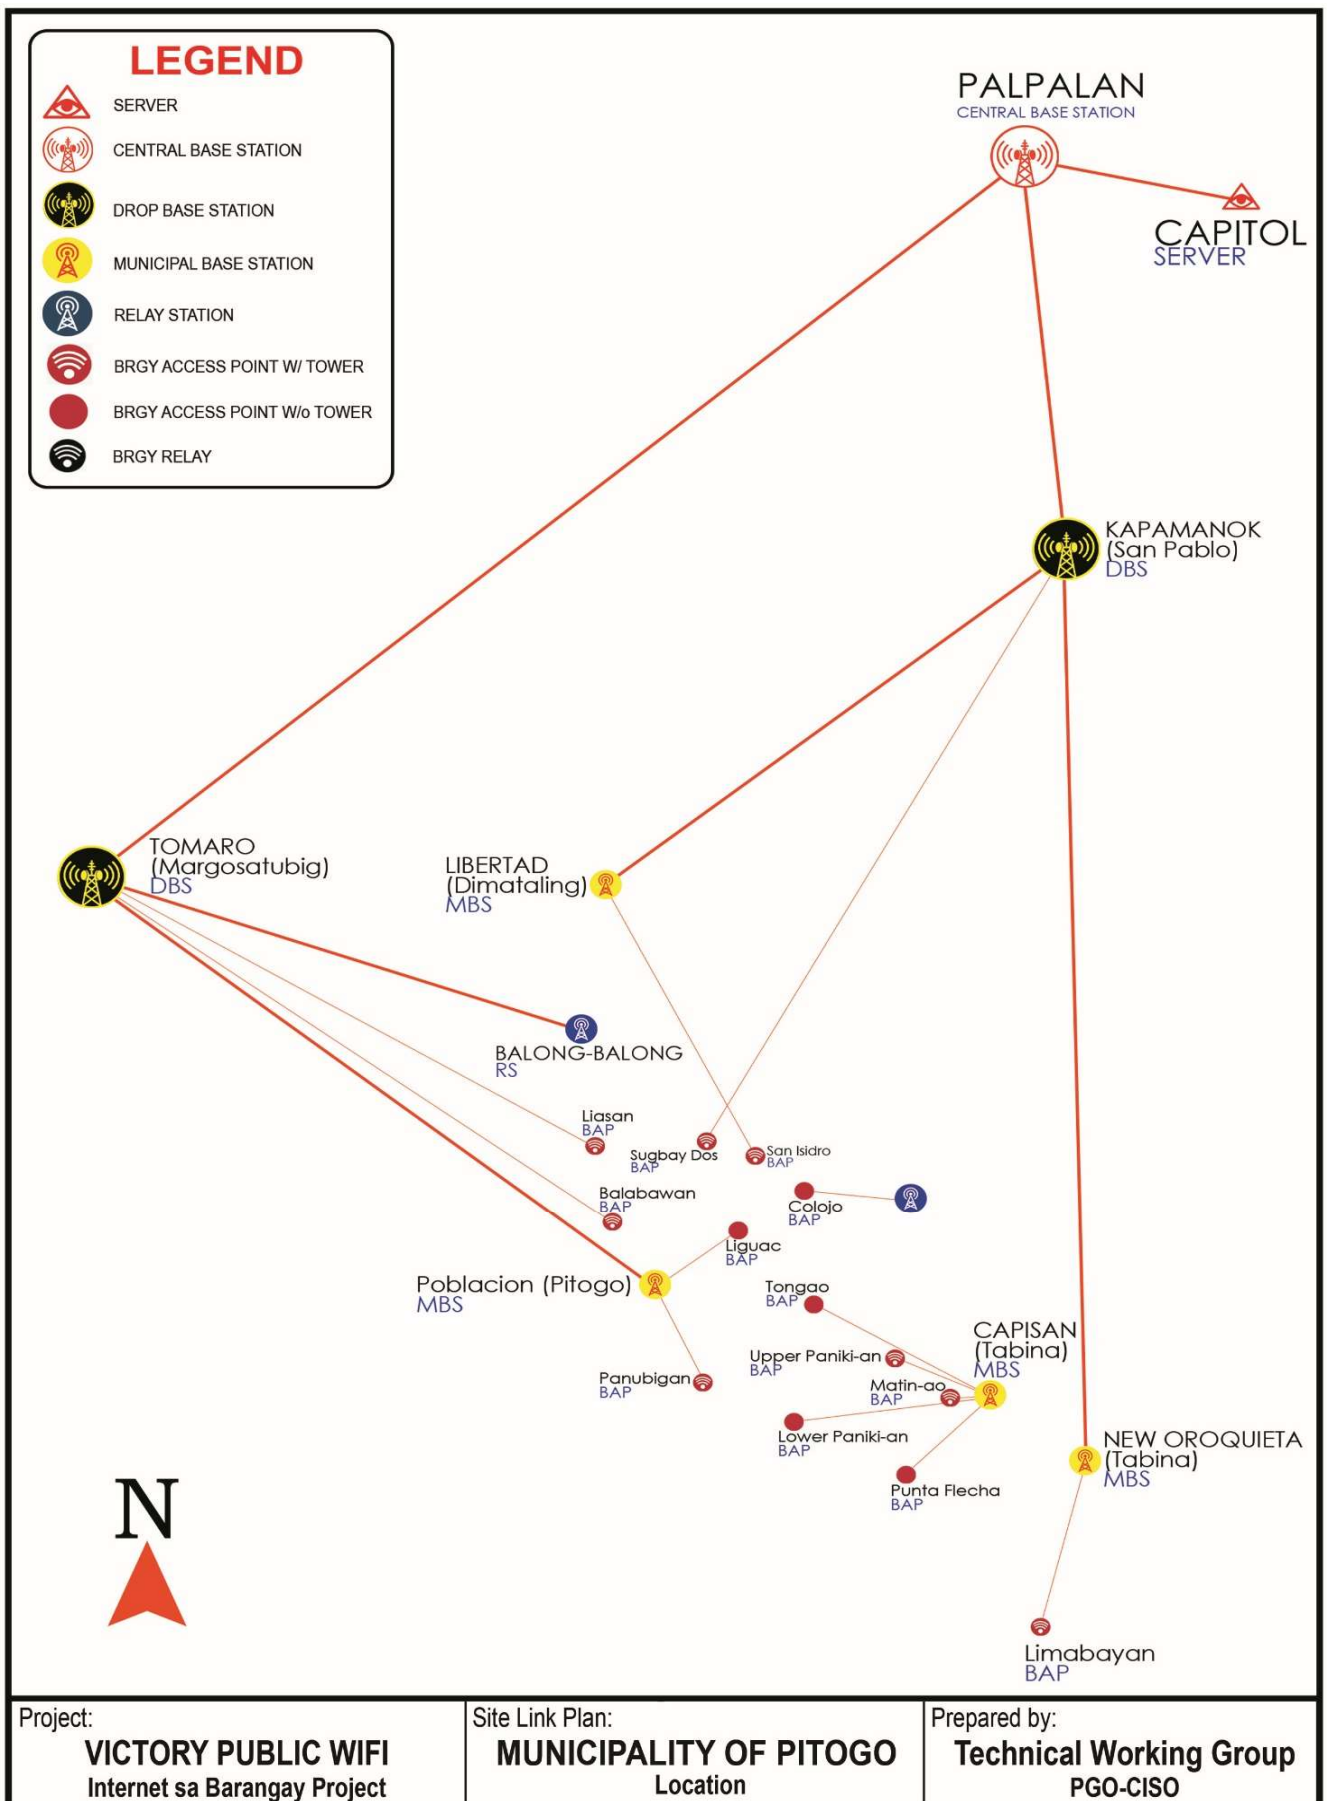


Attachment 20 - Site Link Plan - Vincenzo Sagun

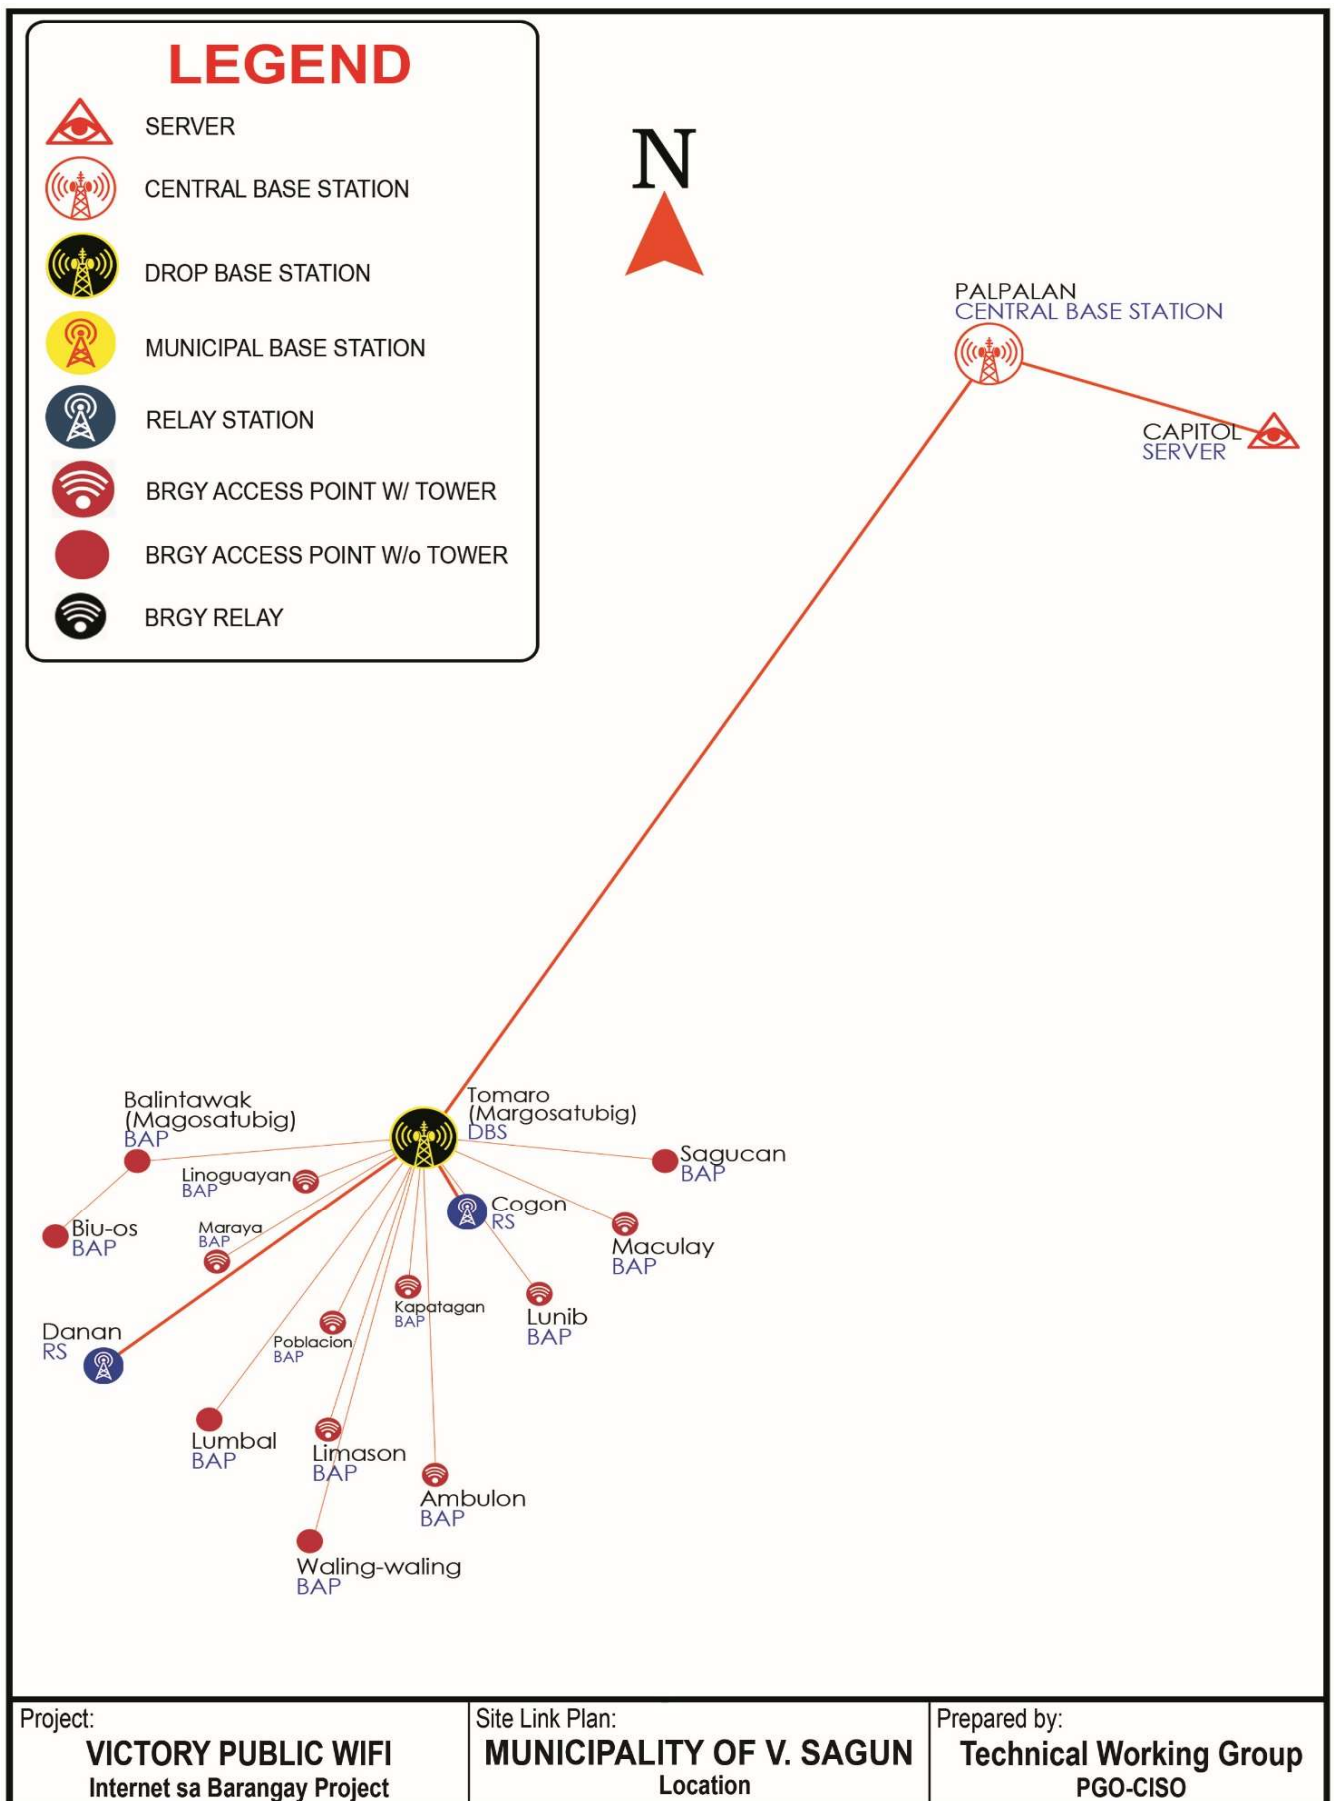


Attachment 21 - Site Link Plan - Margosatubig

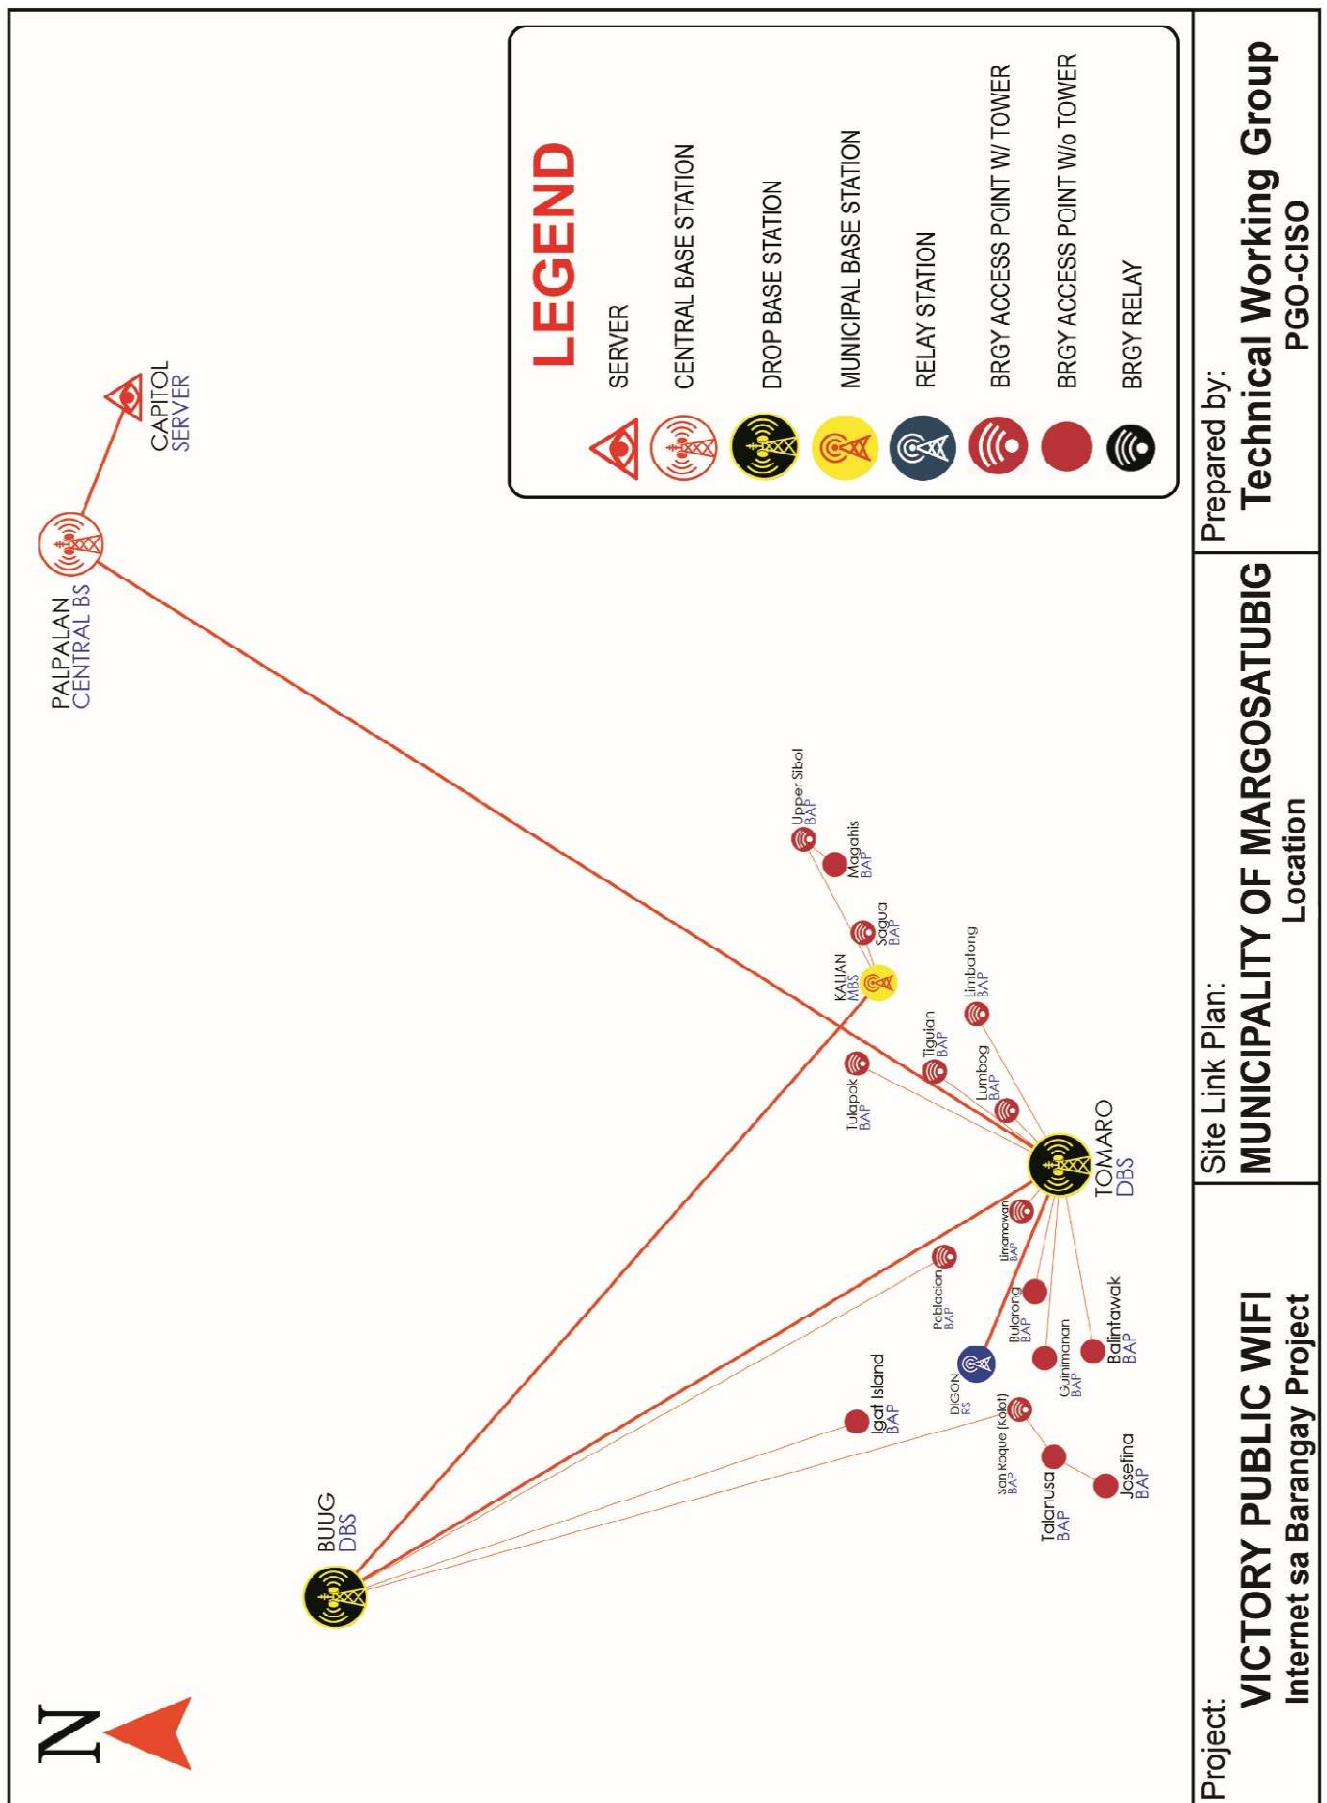


Attachment 23 - Site Link Plan - San Miguel

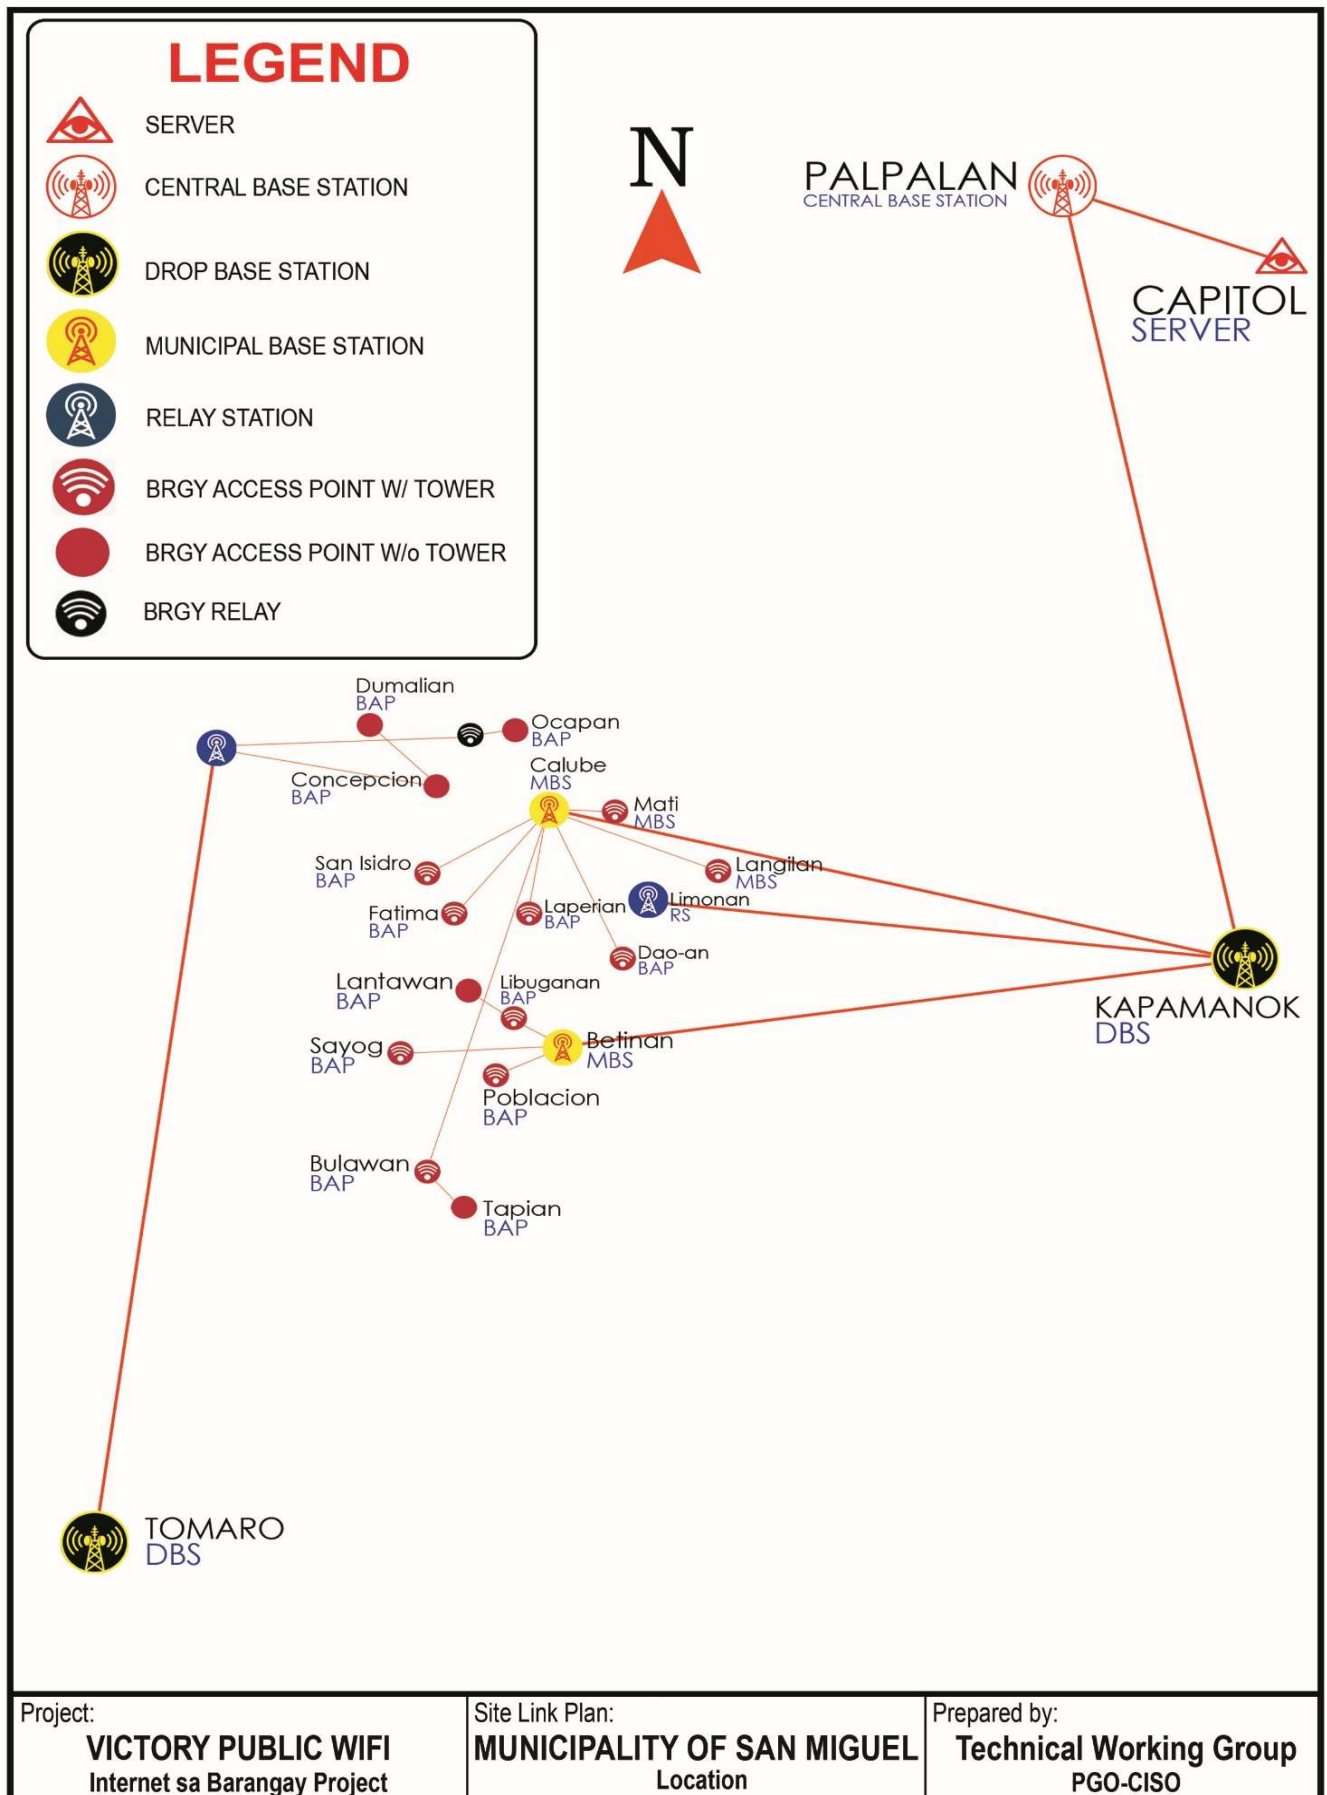


Attachment 24 - Site Link Plan - Kumalarang

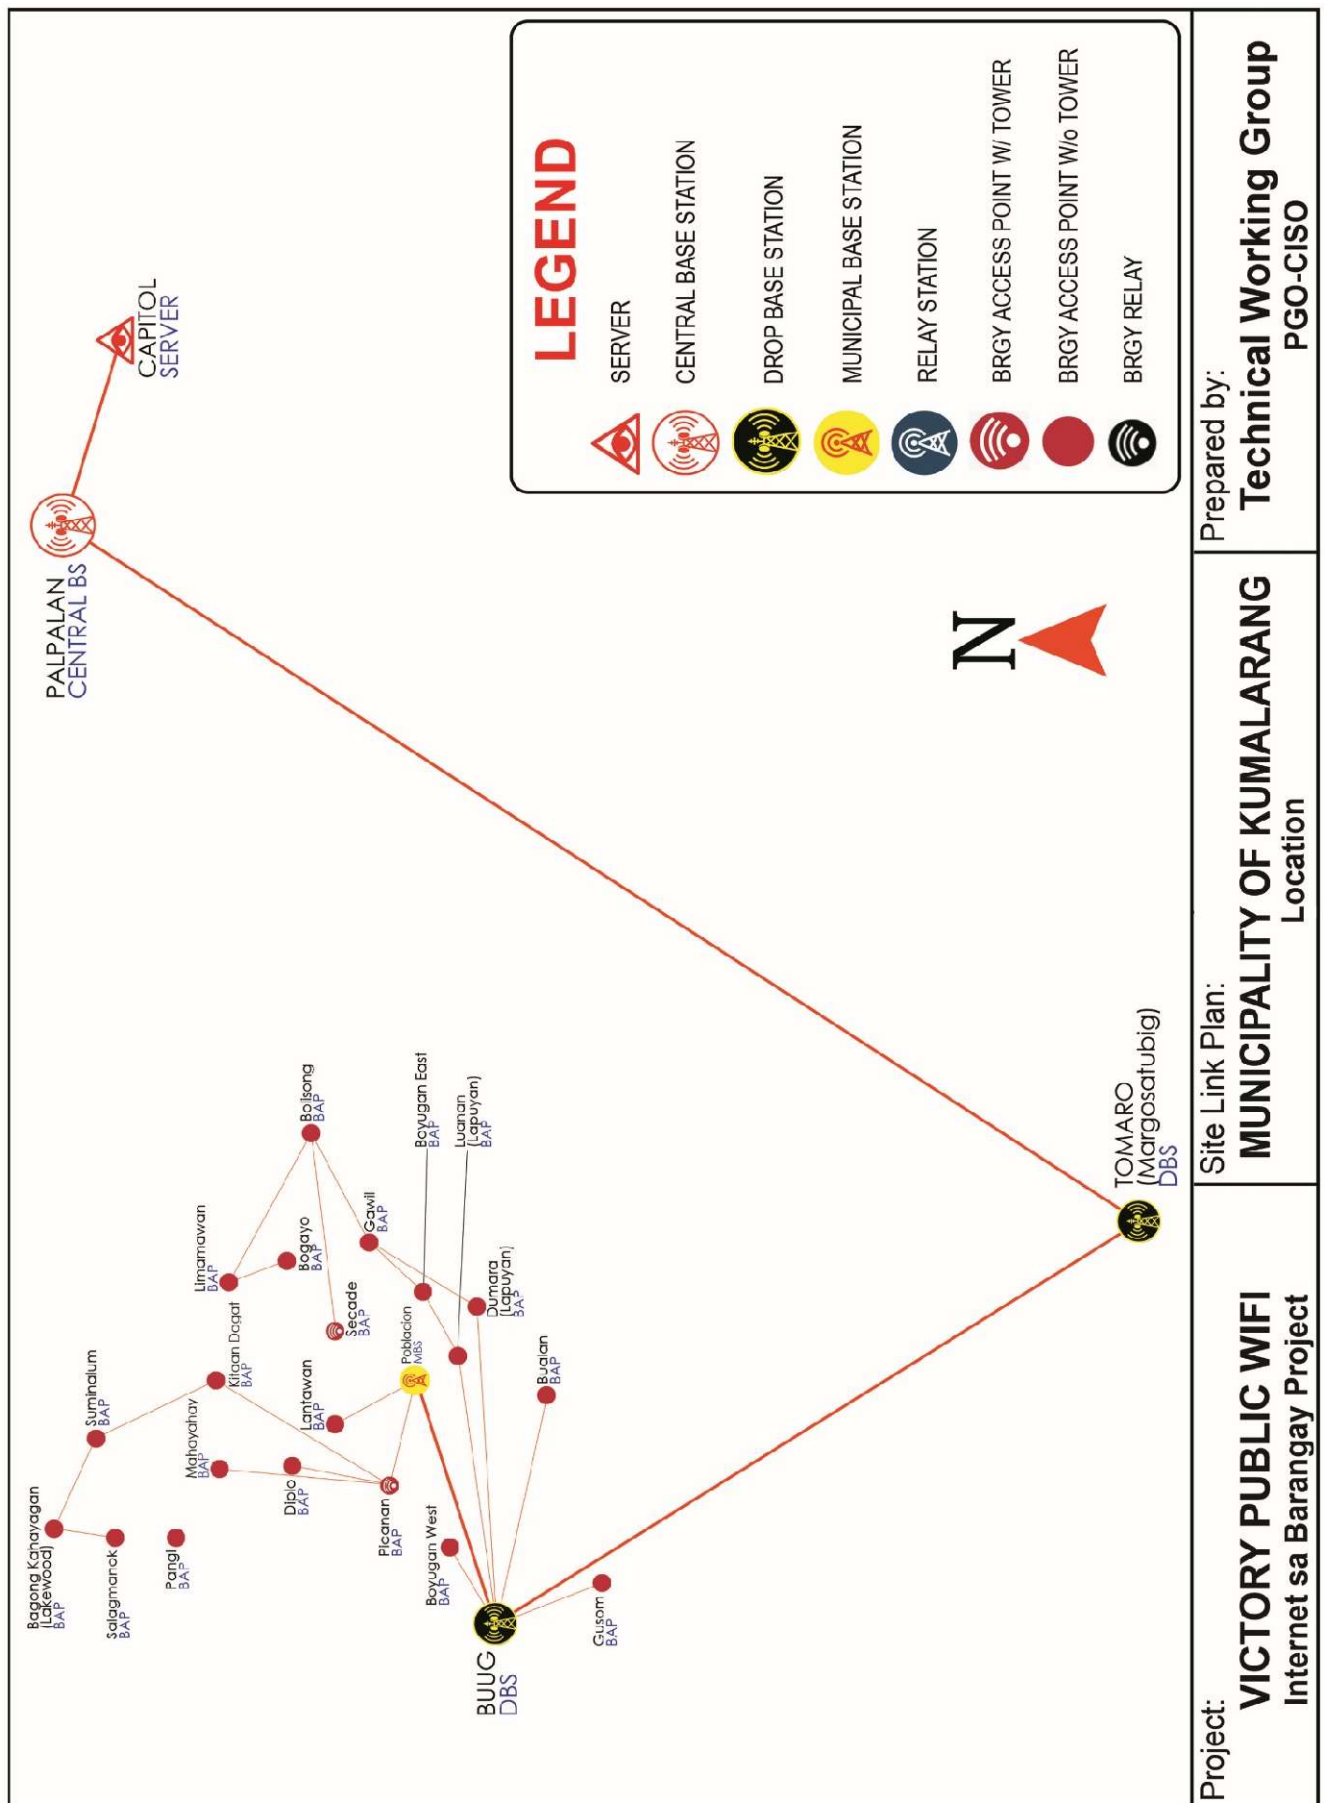


Attachment 25 - Site Link Plan - Bayog

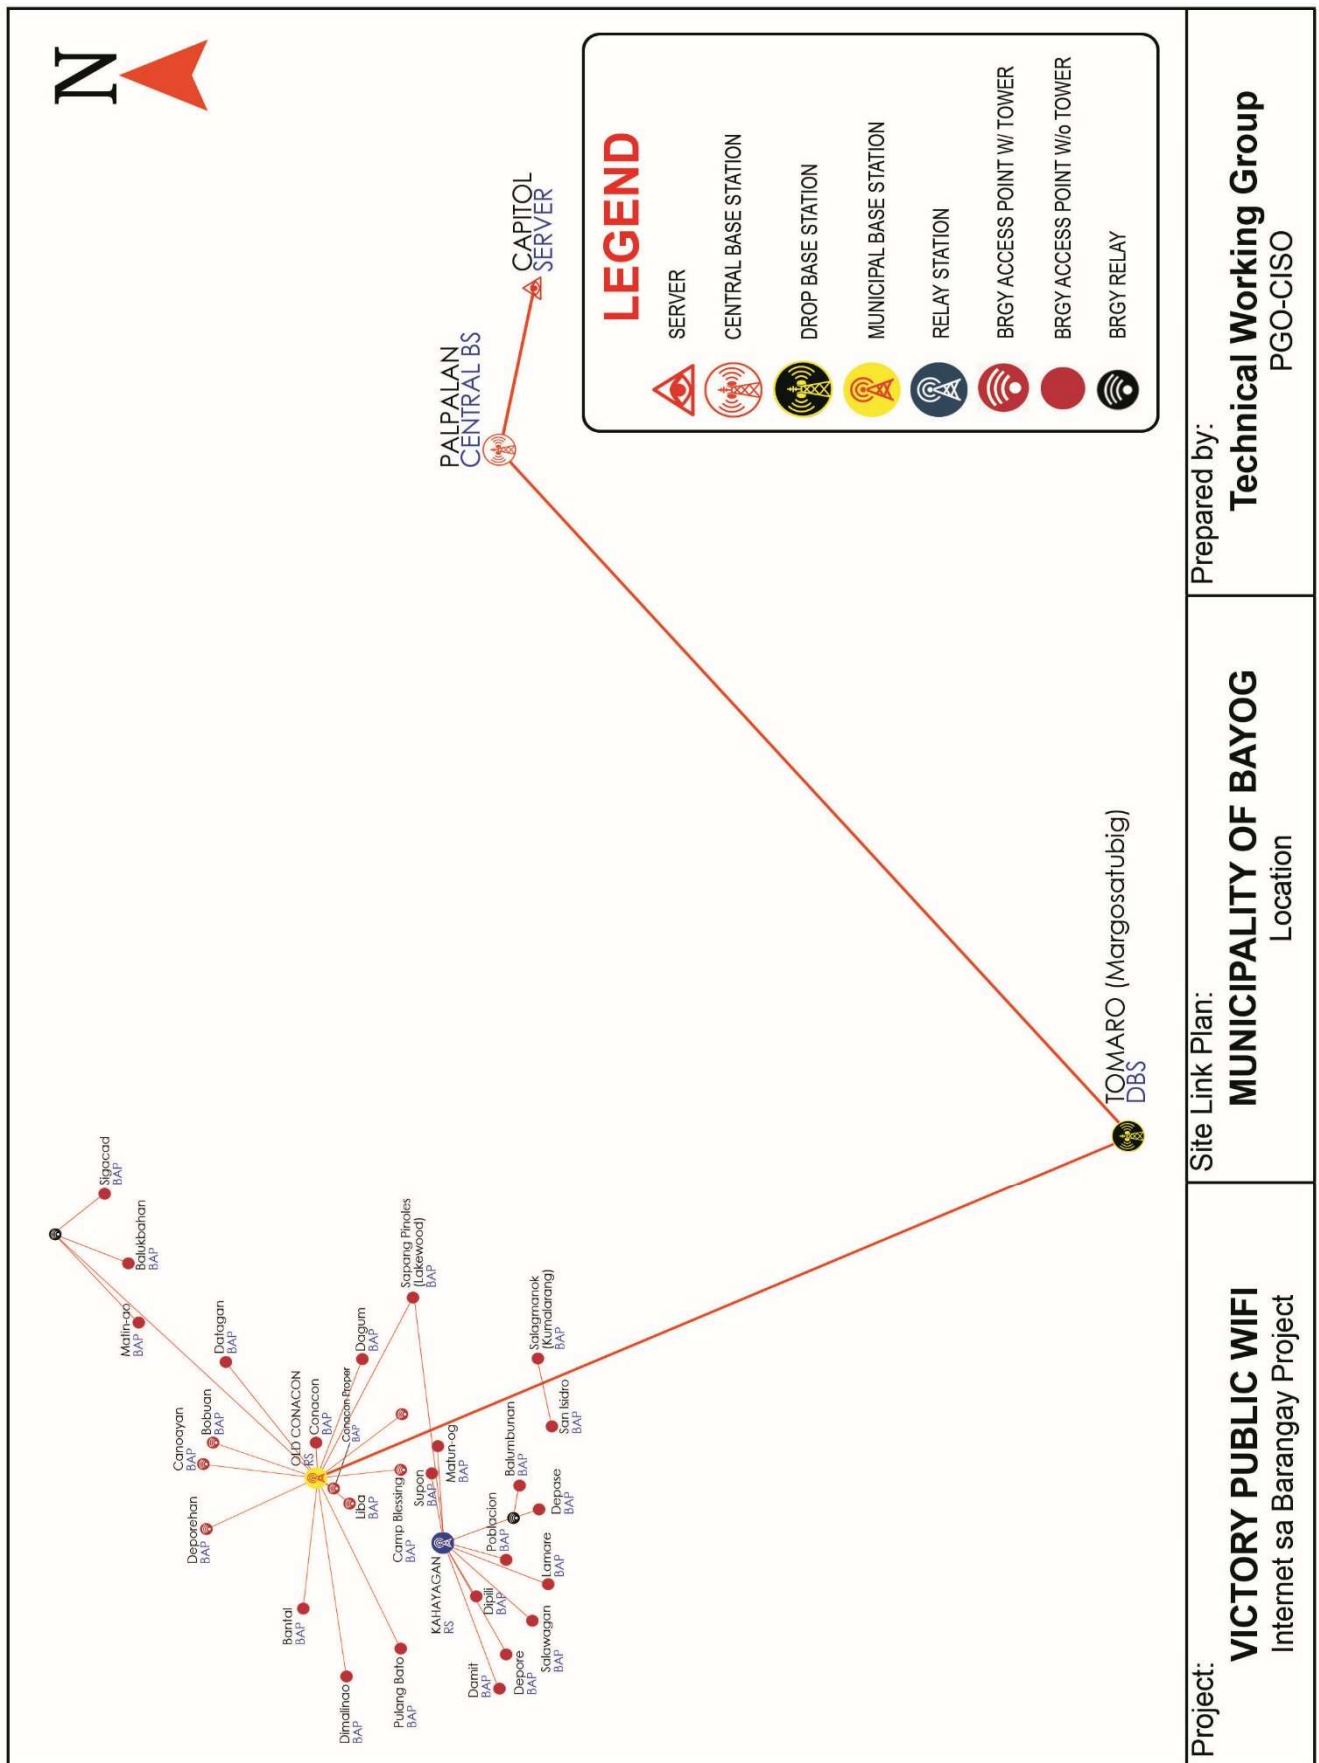


Attachment 26 - Site Link Plan - Lakewood

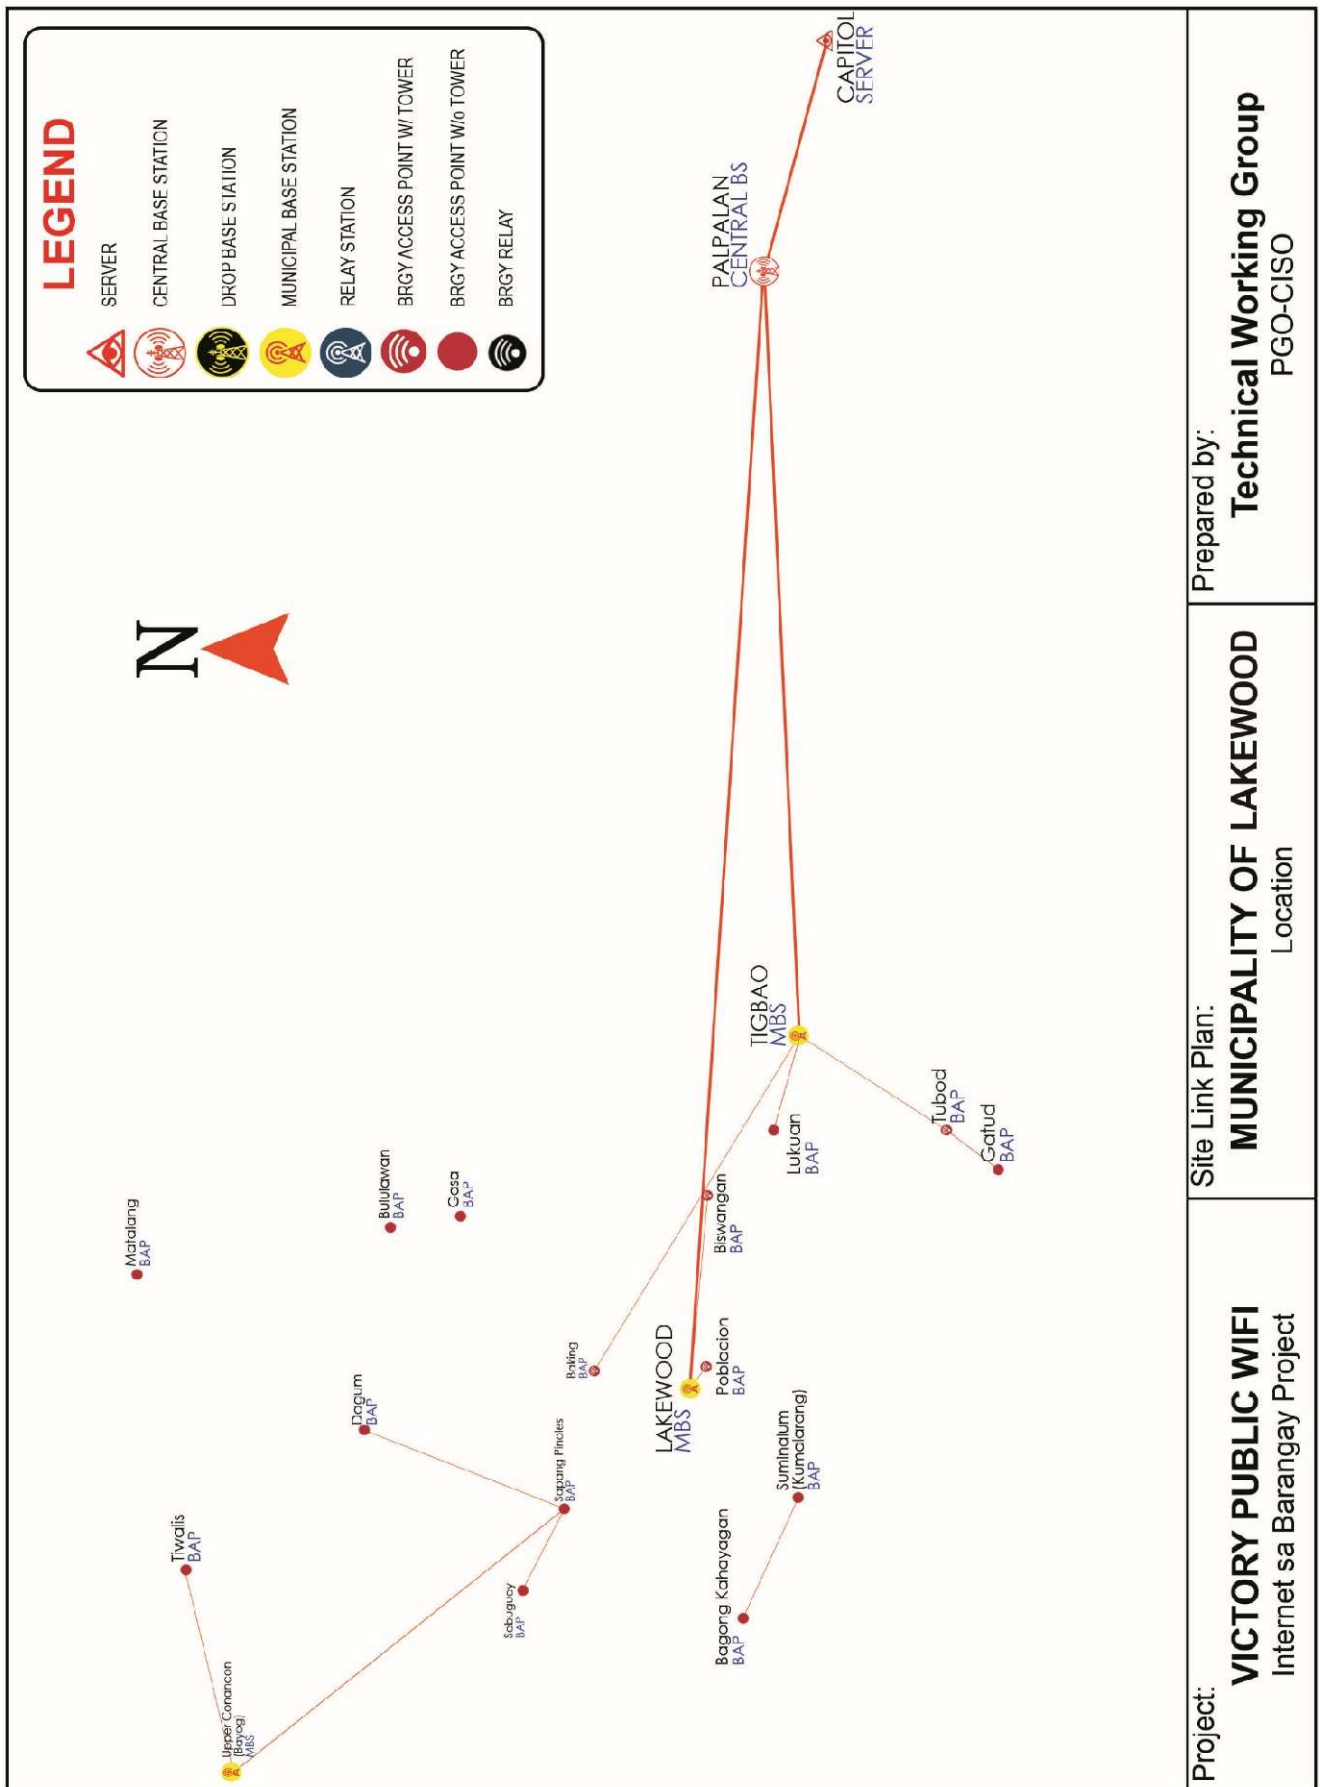

Attachment 27 - Site Link Plan - Tigbao

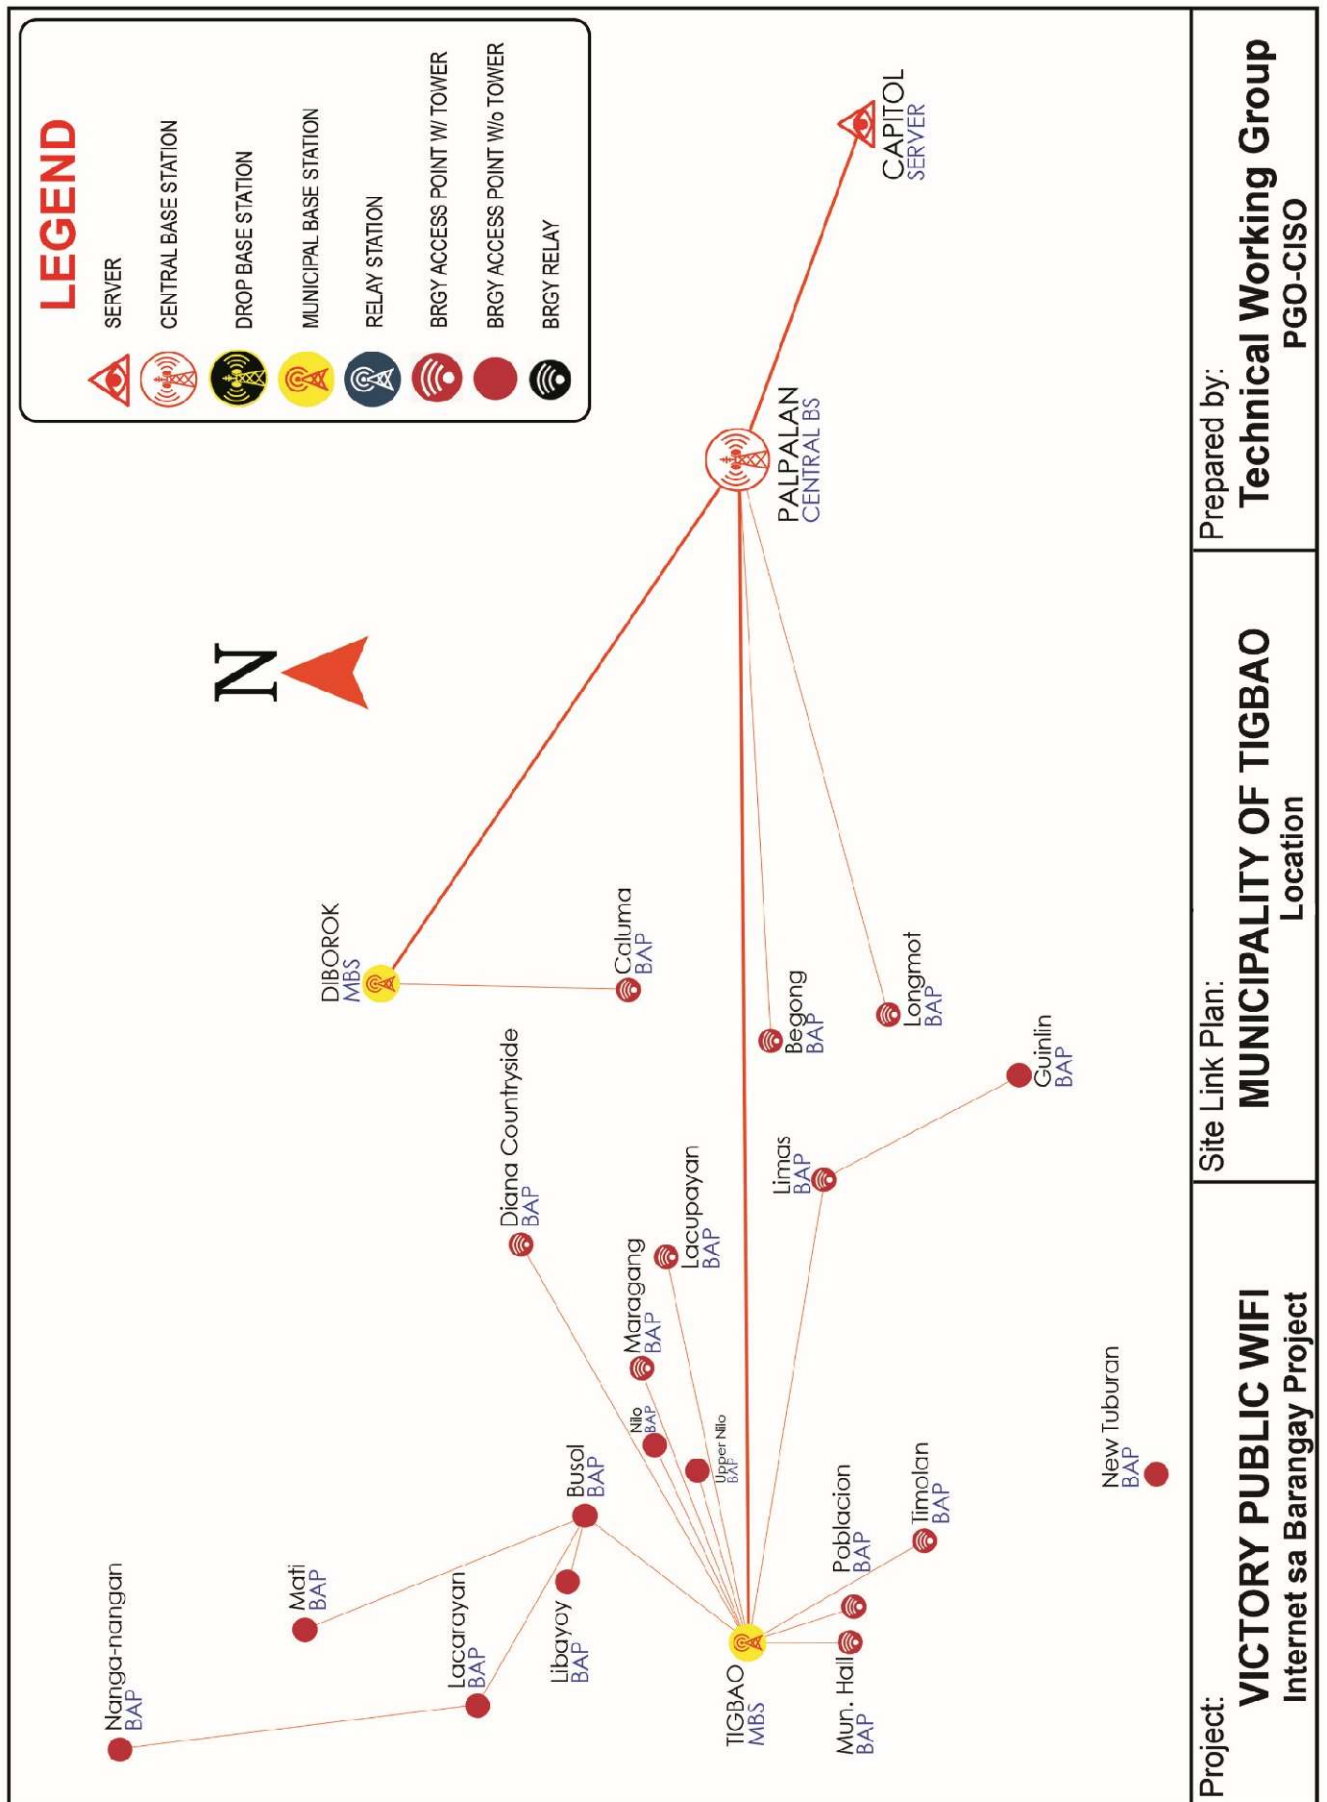

Attachment 28 - Site Link Plan - Backbone Link

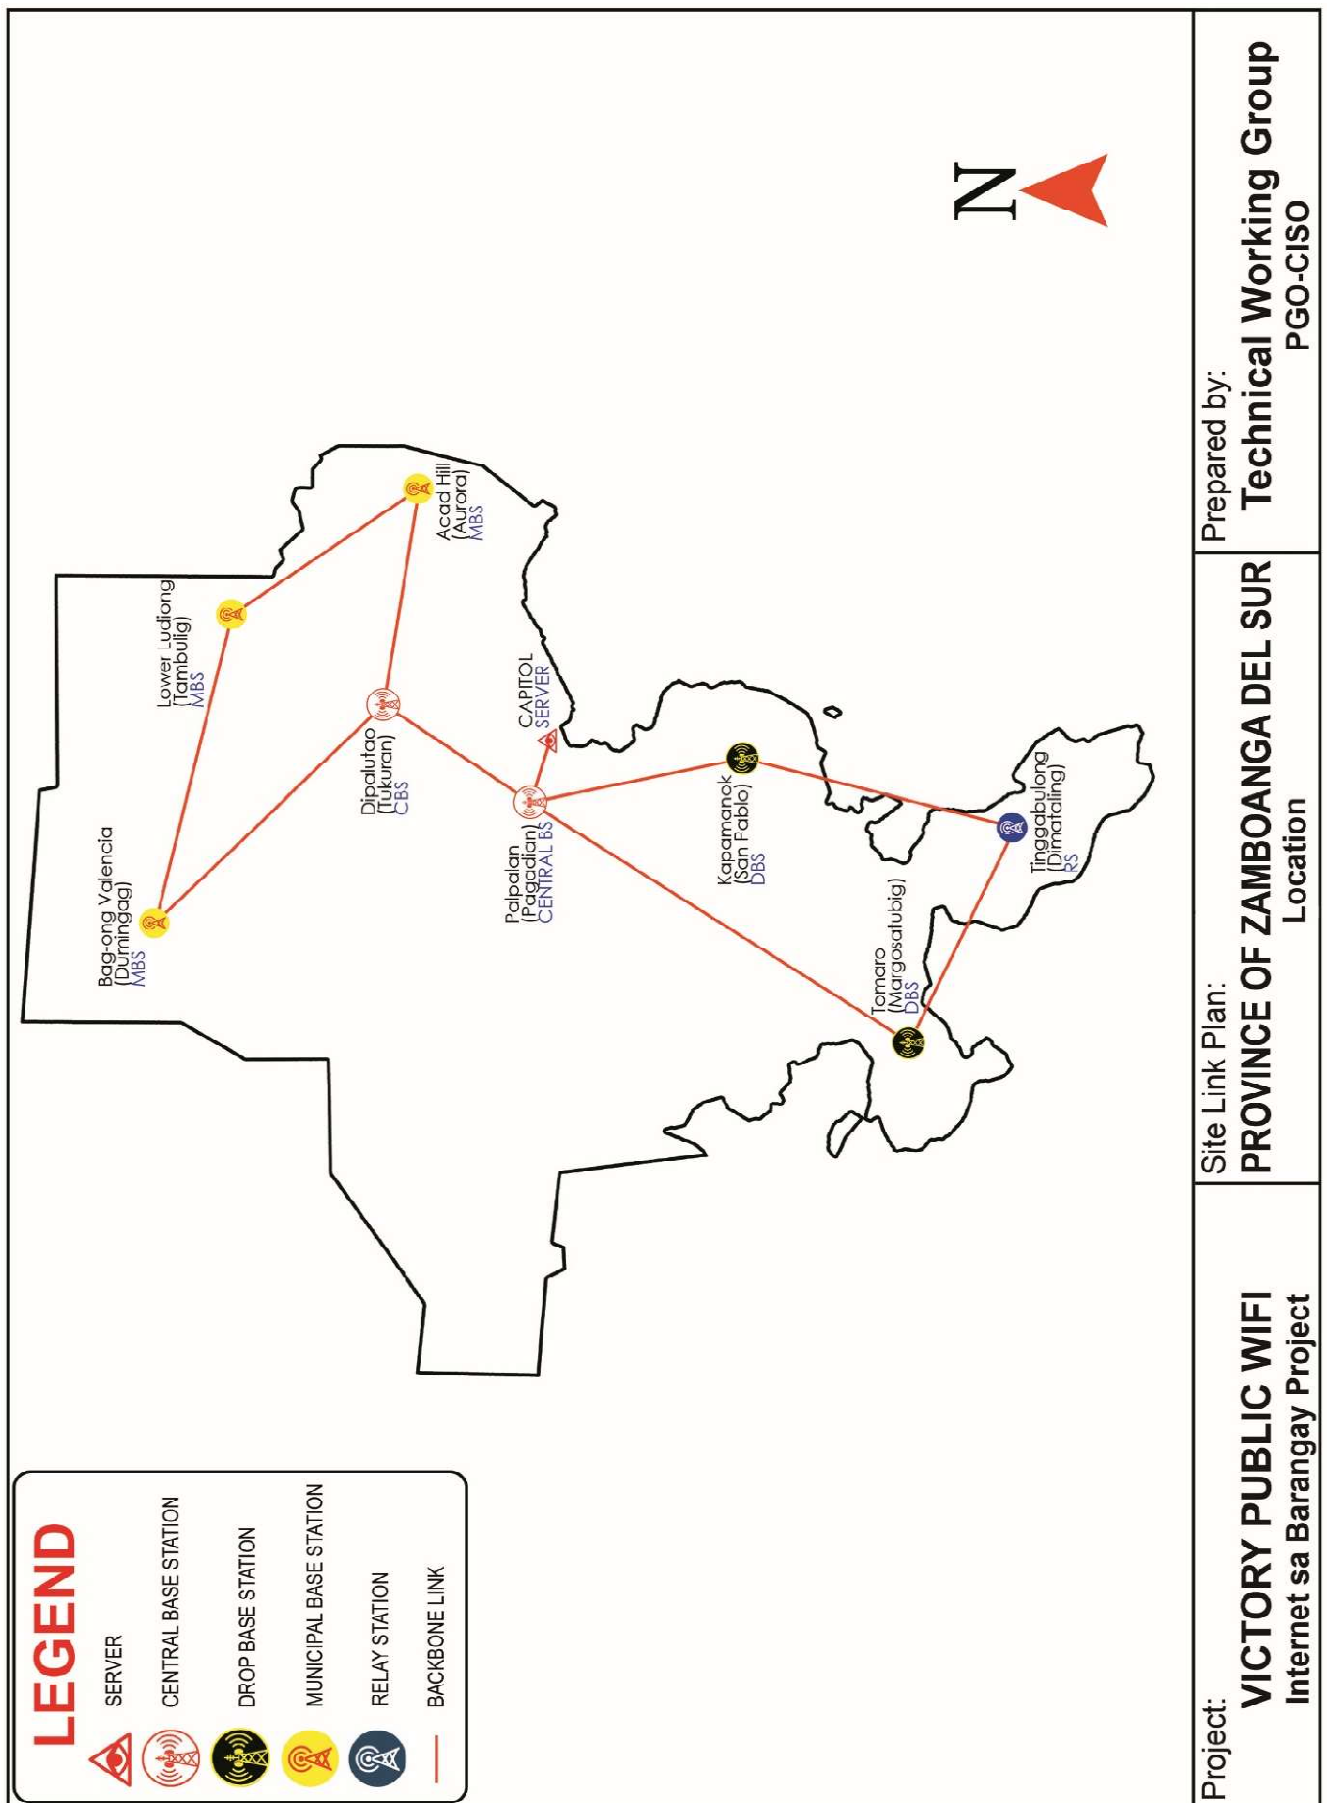

Attachment 29 - **SAMPLE CAPTIVE PORTAL**

VICTORY FREEWiFi
ACCESS SERVICE

PUBLIC WIFI

Please enter your details below

Email Address

First Name

Last Name

Please select your age group ▼

CONTINUE

☐ Please confirm you agree to the Terms and Conditions.

☐ Yes, I would like to receive news, offers and promotions

[View our Terms & Conditions](#)

VICTORY FREEWiFi **victoryfreewifi.net**



Republic of the Philippines
Region IX, Zamboanga Peninsula
PROVINCE OF ZAMBOANGA DEL SUR
Communication and Information Service Office



INSTALLATION CERTIFICATE

SITE INFORMATION (Check Type of Site)

Site Type* : ☐ DCS ☐ CBS ☐ BAP ☐ REL ☐ SCH ☐ OTH

Address :

Location : Tower Height: Power:

EQUIPMENT INSTALLED (Use separate sheets if necessary)

NO. (Item#)	DESCRIPTION (Device Name and Model)	MAC ADDRESS (Device MAC / SN)	IP ADDRESS (Assigned IP)	MODE (AP/STA)	LINKED SITE (AP Connected)

* SITE TYPE: DCS = Data Center Server CBS = Central Base Station BAP = Barangay Access Point REL = Site Relay Station SCH = Public Schools OTH = Other Public Places

CONTACT INFORMATION

Installer: _____ Contact: _____
(Signature Over Printed Name) (Phone Number / Email Address)

Client: _____ Contact: _____
(Signature Over Printed Name) (Phone Number / Email Address)

Remarks: _____
(On-Site Issues and Concerns)

Checked/Recorded by:

JAIME CASTILLON MAATA
Network Administrator

Conformed by:

JUSTIN PAOLO C. HERRERA
Chief, CISO-VFW

APPROVED BY:

HON. VICTOR J. YU
Provincial Governor



VICTORY FREE WIFI - CERTIFICATE OF INSTALLATION

Provincial Government of Zamboanga del Sur - CISO - <https://victoryfreewifi.ml>
